

Rehearsal room build guide

Field binder · drawing set · scope schedule · trade coordination



36 SCOPE ITEMS	7 WORK PHASES	43 FIELD CHECKS	15 SURVEY BUNDLES
-------------------	------------------	--------------------	----------------------

ISSUE STATUS	Coordination + quotation / field release required. Proposed dimensions, products and assemblies remain held where the stated gate calls for survey, sample, shop drawing, engineering, official review or Greg's decision.
--------------	---

Digital checkmarks record task progress. They never release engineering, permit, order, fabrication or installation holds automatically.

Authority + certainty

WORKING AUTHORITY	The dated guide JSON is the coordination schedule. The approved concept governs visual direction. Manufacturer research supports candidate selection. Field records, reviewed shop drawings, engineered assemblies and official decisions govern release where the schedule says they do.
-------------------	---

LOCKED INTENT	Approved room direction or count; dimensional fit may still require field confirmation.
VERIFIED PRODUCT	Manufacturer data checked on the listed date; installed fit and project-specific assembly remain gated.
FIELD VERIFY	Trace, measure, photograph and record the existing condition before downstream work.
HOLD	Do not order, fabricate, demolish or install until the named release evidence exists.

Current shell basis

SOURCE POLYGON	8-point main-room trace · calculated 298.86 sq ft · dimensions unverified on site
CEILING PLANE	102 in working height · field verification required
BOOTH	Plan-traced polygon · glass, curved wall, vestibule, ceiling and services require field survey
ORIGIN	Northwest corner at finished floor; X east, Z south. Dimensions in inches.

CHANGE CONTROL	Any as-built departure updates every affected plan, elevation, quantity, product fit, service route and trade review before release. A 2% survey discrepancy is an escalation trigger, not permission to fabricate within a 2% tolerance.
----------------	---

Authority sources

Approved room concept, September 13	assets/approved-concept.png
Claude brief, copied September 26	evidence/current-brief.md
Initial corrected schedule snapshot, 70 records	evidence/claude-elements-snapshot.json
Reviewed schedule at source commit 1a1d56d	evidence/claude-elements-reviewed.json
Source refresh and adopted corrections	evidence/source-refresh.md
2024 labeled floor-plan crop	assets/plan-source.png
Tape polygon source	evidence/room-polygon-source.json
Owned equipment inventory	evidence/gear-inventory.csv
Existing room photograph	assets/current-room.jpeg
Existing booth walkthrough frame	assets/booth-existing.jpg
Santa Monica permit application types	https://www.santamonica.gov/building-permit-application-types
Walker mirror installation guidance	https://www.walkerglass.com/blog/seven-deadly-sins-of-mirror-installation/

Open coordination conflicts

RESOLVE BEFORE RELEASE

Each conflict names the evidence, downstream consequence and resolution path. Keep the associated order, demolition, fabrication or installation hold in place until the stated status is closed in the dated coordination set.

C-01 · Door and booth geometry has superseded versions		Open for field proof; Pass 7 is the current source geometry and the initial 70-element snapshot is provenance only.
EVIDENCE	Early prose invents D-1; the brief addendum places D-3 on the west wall but gives an earlier booth position; the initial 70-element snapshot misplaces D-3 on the south wall. Frozen Pass 7 commit 1a1d56d restores D-3 to the west wall at z 223..259, hinged south and swinging in, while retaining the traced booth behind the 29-inch vestibule at z 288.5..384.	
CONSEQUENCE	Wrong walls, openings, circulation and booth dimensions could be issued or fabricated.	
RESOLVE	Field-survey D-2, D-3, vestibule and booth; revise every plan and delete D-1.	
C-02 · Locked 5+5 guitar layout is absent from the current model		Open; do not preselect a different row count.
EVIDENCE	The brief fixes two rows of five; the reviewed 69-element Pass 7 source uses ten vertical instruments in one row after a horizontal option collided.	
CONSEQUENCE	Backing and hangers could be installed for an unapproved arrangement.	
RESOLVE	Build a full-size 5+5 template with the actual ten instruments before elevation or backing release.	
C-03 · PMC model and cabinet envelope conflict		Open.
EVIDENCE	Brief and inventory say PMC IB1 at 15.8 by 19.7 inches; current elements say PMC IB1S at 11 by 17.7 inches.	
CONSEQUENCE	Speaker stands, toe-in, desk spacing and service access can be wrong.	
RESOLVE	Read model plates and measure the installed pair and stands before fixing the bay elevation.	
C-04 · NU1X identity and source dimensions are wrong		Open; NU1X remains the approved design intent.
EVIDENCE	Yamaha lists the NU1X at 59.125 W by 18.25 D by 40.3125 H inches; the brief and Pass 7 source use 57.5 inches wide, and inventory lists a Clavinova rather than an NU1X.	
CONSEQUENCE	Holding the Pass 7 north edge at z 3 moves the corrected center to z 32.5625 and the south edge to z 62.125, changing the bar start, bench/sofa conflict, delivery and circulation checks.	
RESOLVE	Confirm the physical instrument, then field-test the corrected proposal: north edge z 3, center z 32.5625, source-derived proposed 8-inch gap and bar start z 70.125 before bar or floor-layout release.	
C-05 · Booth drum identity is unresolved		Open; 72 by 66 inches is a planning envelope only.
EVIDENCE	Photos are described as Yamaha; inventory records a Gretsch Catalina; current elements combine Yamaha naming with Gretsch inventory details.	
CONSEQUENCE	Kit footprint, setup, mic positions and asset handling may be assigned to the wrong kit.	
RESOLVE	Photograph badges and shells, inventory the complete setup and measure its deployed envelope.	
C-06 · Main-room fabric and plaster directions conflict		Open; existing fabric is retained until the finish decision is released.
EVIDENCE	Old v0.1 retains the existing grey acoustic fabric; current elements remove it and apply charcoal plaster; performance is unmeasured.	
CONSEQUENCE	Finish work could remove paid acoustic treatment without a replacement plan.	
RESOLVE	Inspect the wall build-up, measure the room, mock up both controlled finish options and record Greg's decision.	

C-07 · Lighting intent exceeds verified ceiling and controls		Open.
EVIDENCE	The brief calls for cove, recessed cans and track; requirements call for DMX-addressable control; current elements name Caseta Pro; plenum and circuits are unknown.	
CONSEQUENCE	Fixture type, control protocol, cutouts, drivers and permit scope can change.	
RESOLVE	Survey ceiling and circuits, then issue a coordinated fixture/control schedule and reflected ceiling plan.	
C-08 · Overhead mirror has no issued attachment design		Hold fabrication and overhead installation.
EVIDENCE	Current elements show a 96 by 96 inch mirror on plywood under a 102-inch ceiling; weight, glass makeup and structure are unverified.	
CONSEQUENCE	Fabrication or installation could proceed without a safe supported assembly.	
RESOLVE	Glazier and qualified design professional issue glass, backing, load and attachment details after ceiling inspection.	
C-09 · Published model, notes and old build sheet are stale		Open until the field-verified set is issued.
EVIDENCE	An older 59-element published artifact observed during the initial review, old notes and the v0.1 sheet describe obsolete scope; it is not a claim about the source project's current deployment. The initial 70-element snapshot preserves the first guide input, while frozen Pass 7 commit 1a1d56d is the reviewed 69-element source: it removes the unsupported booth floor lamp, records the booth rug as a provisional 66 by 88 inches, restores west-wall D-3 and corrects the west-wall order.	
CONSEQUENCE	Crews can quote, order or build obsolete scope.	
RESOLVE	Issue one dated coordination set and mark stale files reference-only; do not reuse old totals or durations as current facts.	
C-10 · Grandstage X body is larger than the working model		Open; keep the instrument at sitting height and always in audio.
EVIDENCE	Korg lists 53.98 W by 18.15 D inches excluding the stand; current elements use 53 W by 14.6 D inches for the staged rig.	
CONSEQUENCE	Bench, D-2 swing, HVAC and playing clearances can fail after the stand, pedals and rear cable bend are added.	
RESOLVE	Measure the selected stand and full playing envelope, then re-run the southeast full-size fit check.	
C-11 · The candidate refrigerator does not fit the source bar depth		Hold bar and refrigerator orders.
EVIDENCE	Zephyr lists a 23.375-inch body plus 1 inch rear plug clearance. The Pass 7 source bar is 24 inches deep, still 0.375 inch short before finish tolerance.	
CONSEQUENCE	The unit, outlet, vent or door can project into the stool and sofa zone or make service impossible.	
RESOLVE	Test a proposed 26-inch bar allowance full size and require a coordinated shop drawing; Greg approves the final depth and adjacent layout.	
C-12 · Candidate dark flooring cannot overlay a floating floor		Hold dark-floor order and demolition.
EVIDENCE	Karndean's SCB89 installation guide requires floating flooring to be removed; the existing oak LVP installation is unknown.	
CONSEQUENCE	The recoverable overlay concept may void the floor warranty or force removal of existing oak.	
RESOLVE	Identify the existing assembly. Keep oak plus rugs as an explicit option; any oak removal and dark-floor scope requires Greg's written approval and a preservation plan where feasible.	
C-13 · Candidate slat panels do not cover the 102-inch wall		Hold panel quantity and cut plan.
EVIDENCE	WoodUpp item 1029 is 94.49 inches high; the room plane is 102 inches before field verification.	
CONSEQUENCE	A 7.51-inch joint, trim or custom extension affects the guitar elevation, cove and backing.	
RESOLVE	Show the exact termination in the elevation and shop drawing; coordinate it with the locked 5+5 instrument layout.	


C-14 · Corrected west-wall seating still has unproven conflicts		Open; do not reduce the stool count or alter the sofa by default.
EVIDENCE	The corrected piano bench overlaps the source sofa envelope. The proposed 26-inch bar corner still overlaps the unchanged sofa box by 2.86 by 7.875 inches, the north stool overlaps the sofa, and the south stool conflicts with the west swivel once their nominal and occupied envelopes are considered.	
CONSEQUENCE	The piano bench, 26-inch bar, sectional, occupied stools, west swivel, refrigerator door and circulation route cannot all be treated as independently fitting.	
RESOLVE	Run the corrected full-size combined mockup with the piano bench and sofa together, 26-inch bar corner marked, all three stools occupied, west swivel rotated and occupied, and refrigerator door open; record all four conflict zones and route any change through Greg.	

A01 · Room plan + fit envelopes

Coordination drawing · dimensions and release notes shown on sheet · field verification controls

A01 / ROOM + DOOR PLAN

Latest source geometry, corrected equipment envelopes, unresolved occupied clearances.

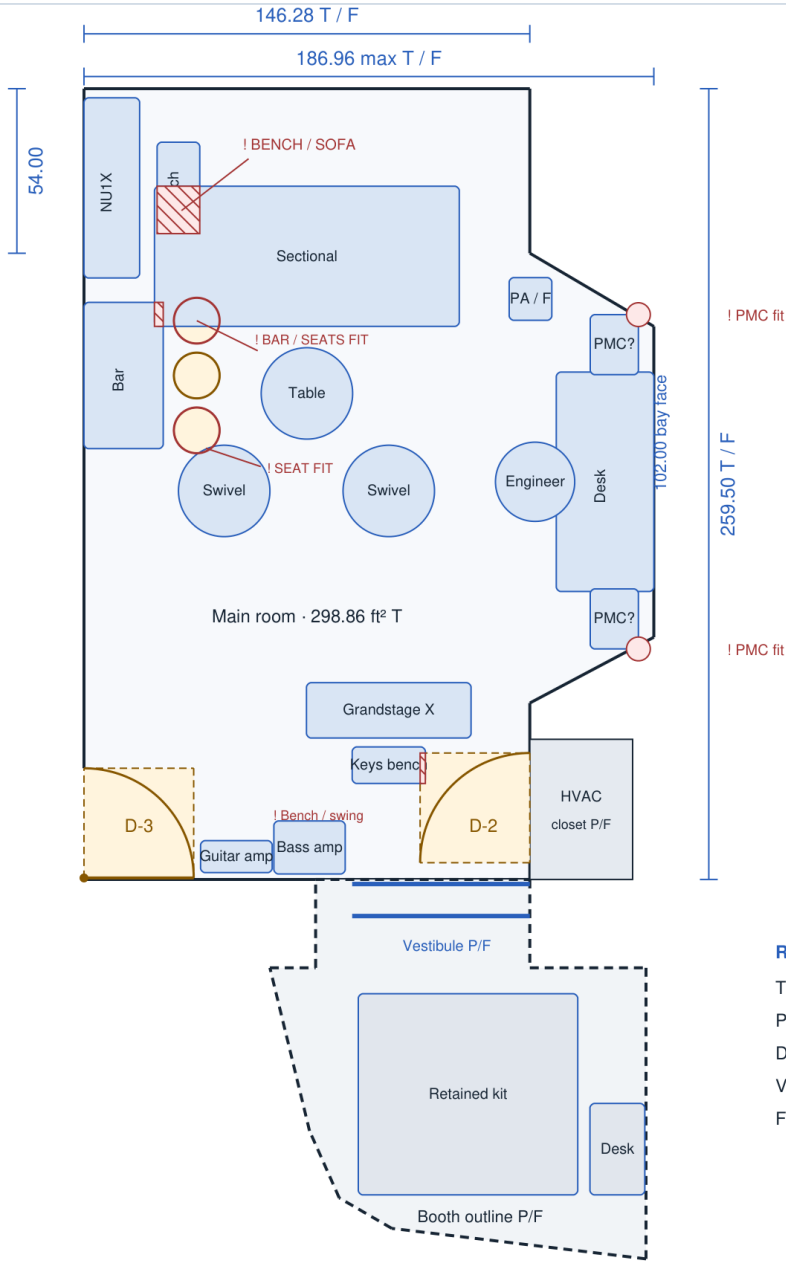

READ THIS PLAN

- T · typed tape
- P · plan trace
- D · proposed
- V · maker size
- F · field check


D-3: west wall, hinged south; door swings need field confirmation.
PA/pole: nominal 14 × 14 in source box; verify actual base, aim and cable route.
Red marks: furniture/seat, speaker/return and bench/door conflicts.

A02 · Mirror wall elevation

Coordination drawing · dimensions and release notes shown on sheet · field verification controls

A02 / NORTH MIRROR ELEVATION

Design envelopes for quotation. No glass cut sizes or support capacities are released.

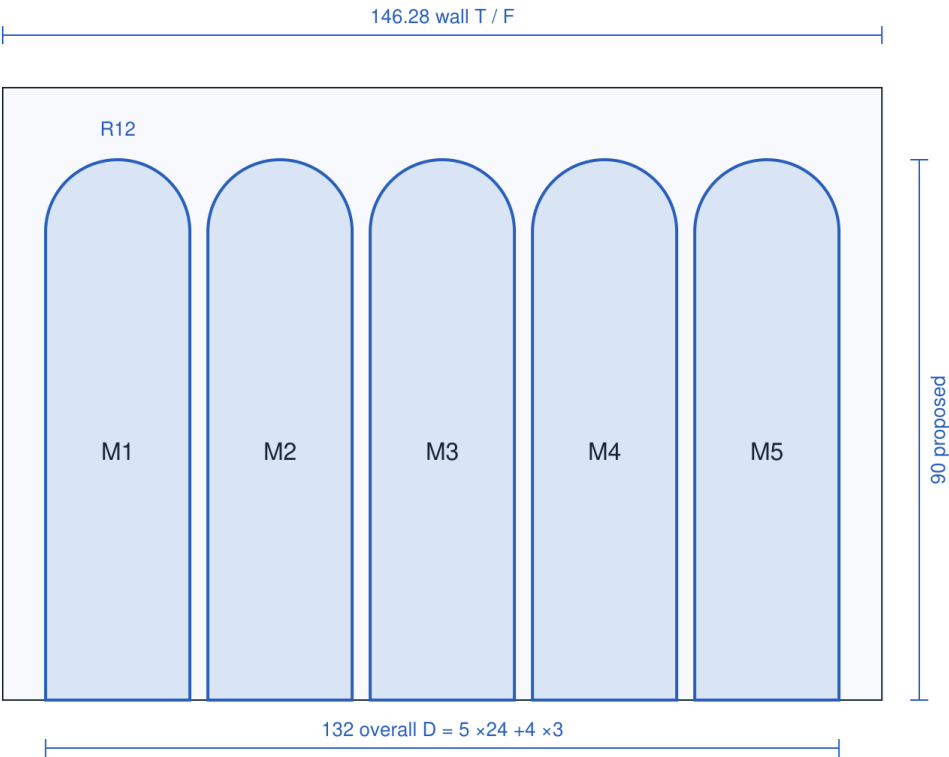

MIR-01 · FIVE ARCHES

24 W × 90 H in nominal envelopes; 3 in gaps; 7.14 in end margins.

Arches start at the proposed floor line. Protect bottom edges and coordinate trim.

Template after finished-wall datum and floor buildup are known.

LGT-02 · LIGHT THE SIDES + ARCH HEAD

80.71 ft net = $5 \times [2 \times (90 - 12) + \pi \times 12] / 12$.

Do not order curved channel from this elevation; supplier details the bend.

Backing, glass assembly, mechanical retention and access by the glazier.

A03 · Bar + piano elevation


Coordination drawing · dimensions and release notes shown on sheet · field verification controls

A03 / WEST BAR + PIANO ELEVATION

Facing west: piano is north / viewer-right; bar is south / viewer-left. Source correction adopted.

SOUTH / VIEWER LEFT

NORTH / VIEWER RIGHT

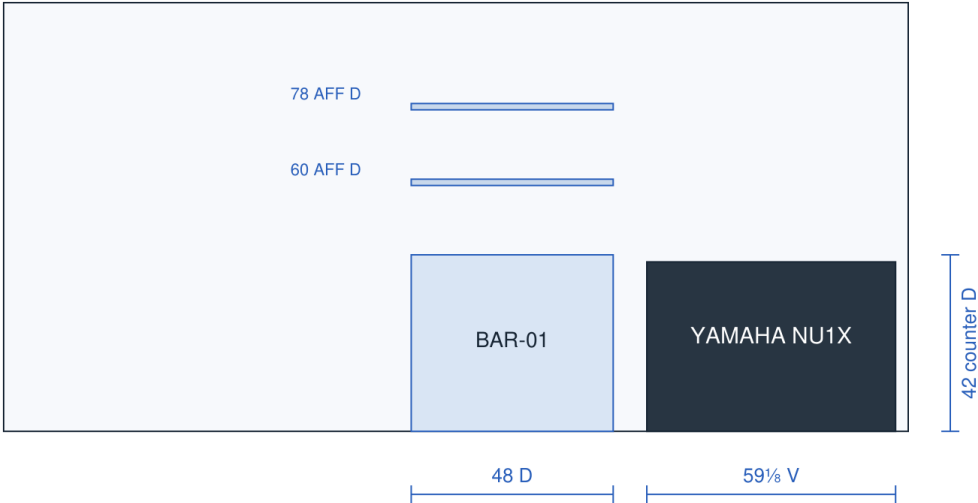

FRIDGE COORDINATION · BAR-05

Zephyr PRB15C01CG: 15 W × 23 3/8 D × 33 3/8–34 7/8 H in.

Minimum opening 15 1/8 W × 34 H in; allow 1 in behind for plug.

Proposed 26 in cabinet depth still needs a shop drawing and occupied fit test.

North datum: 3 in setback + 59 1/2 in piano + 8 in gap + 48 in bar (proposed).

THREE STOOLS REMAIN A DESIGN HOLD

48 in / 3 = 16 in of bar run per seat. Source stools sit 18 in apart.

Mock up three occupied stools, fridge open, and piano bench in use.

COUNTER + FLOOR SEQUENCE

Set the finished-floor datum → install carcass → template stone → fit appliances.


No sink or water service is included. Front vent and pull-out access stay clear.

A04 · Guitar wall elevation

Coordination drawing · dimensions and release notes shown on sheet · field verification controls

A04 / GUITAR WALL FIT STUDY

Five instruments per row shown as nominal 39.5 in envelopes; instrument size is not uniform.

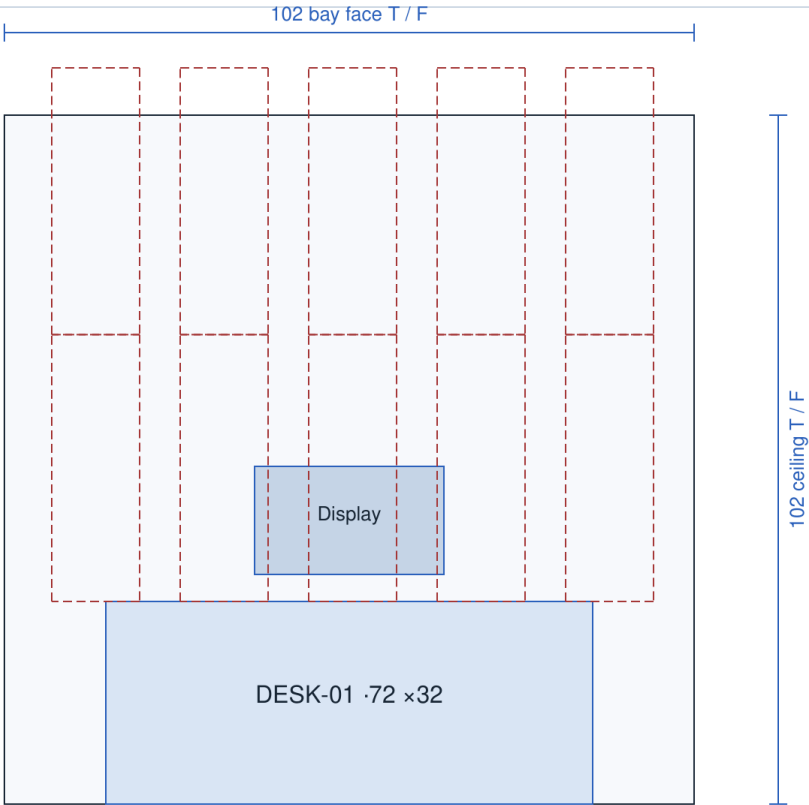

5 +5 IS STILL THE REQUESTED ARRANGEMENT
30 in desk +2 x39.5 in guitars =109 in before any gaps.
Basses are longer; the display already occupies the lower area.
This stacked example fails. It is a fit test, not an installation elevation.


NEXT · GTR-01 + GTR-02
Template all ten actual instruments, headstock and removal paths on the bay/returns.
Test stagger/angle options full size. Any change to 5+5 goes to Greg for approval.
Only then locate structural backing and price the final hanger set.

E01 · Lighting + power coordination

Coordination drawing · dimensions and release notes shown on sheet · field verification controls

E01 / REFLECTED CEILING COORDINATION

12 proposed main-room fixtures; separate booth control; exact recess/driver clearance unverified.

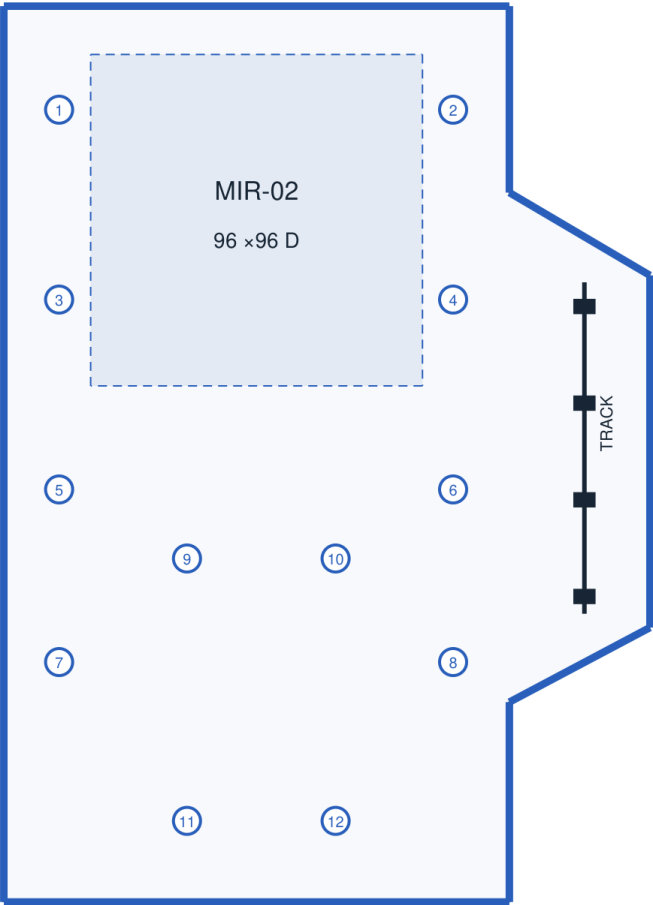

PROPOSED POINTS (X,Z) · ALL INCHES
1(16,30) 2(130,30) 3(16,85) 4(130,85) 5(16,140) 6(130,140)
7(16,190) 8(130,190) 9(53,160) 10(96,160) 11(53,236) 12(96,236)


12 x 15 W Nora candidate = 180 W connected main-room downlight load.
This is not a circuit design or a photometric prediction. Keep access to every driver.
Coordinate ceiling mirror, structure, HVAC and existing safety devices before drilling.

A05 · Booth plan

Coordination drawing · dimensions and release notes shown on sheet · field verification controls

A05 / BOOTH + VESTIBULE PLAN

The corrected current trace includes the 29 in vestibule. No field survey confirms it yet.

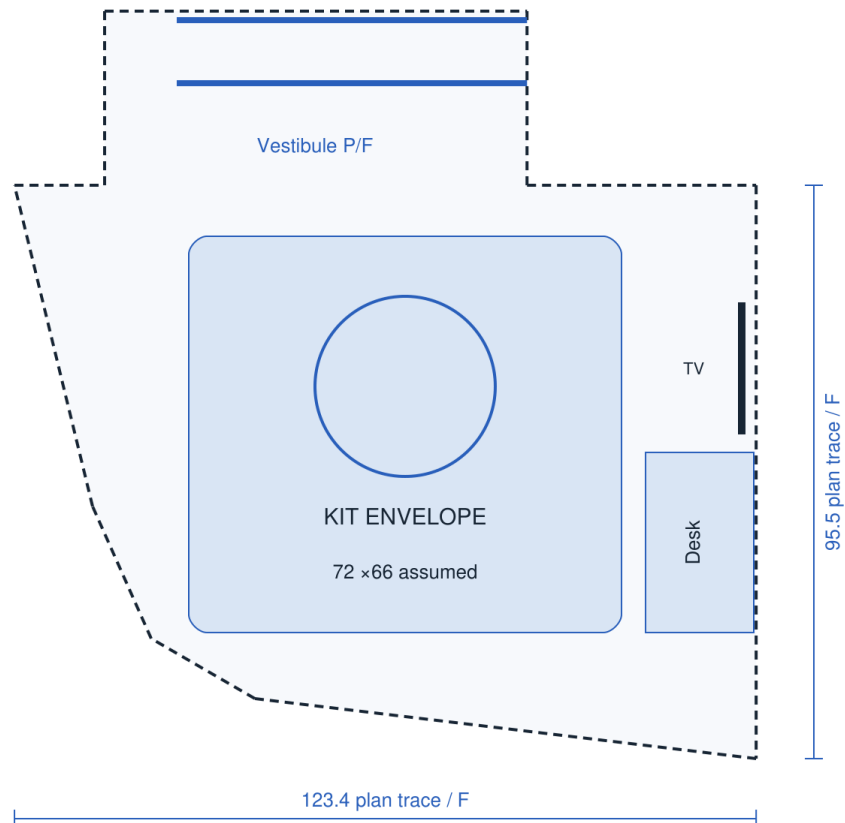

BOO-01 / BOO-02 / BOO-03

Retain the drum/vocal booth; verify Yamaha vs Gretsch identity in person.

Survey both slider layers and the curved/sloping wall before surface takeoffs.

Test kit access, mic boom sweep, desk use and cable routes together.

Absorber/cloud quantities are provisional; ceiling supports require a trade detail.

Do not cover door tracks, supply/return paths, access panels or the camera view.


D01 · Assembly details + release holds

Coordination drawing · dimensions and release notes shown on sheet · field verification controls

D01 / COORDINATION DETAILS


Show what adjacent trades need from one another before they close the wall or ceiling.

D1 · SERVICEABLE MIRROR LIGHT EDGE

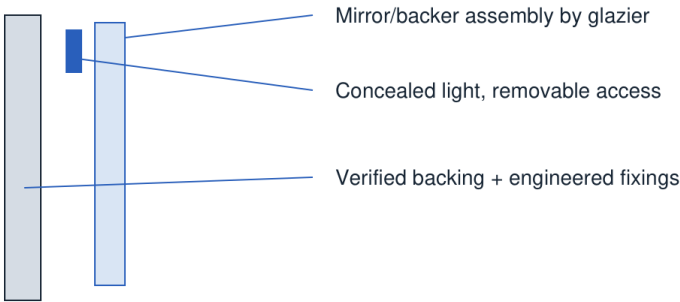

Coordination section; no anchor sizes or load capacity implied.

D2 · FRIDGE + COUNTER SECTION

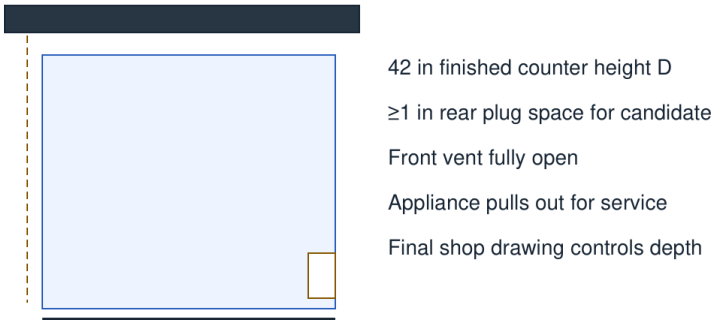

No sink/plumbing scope; stone templated after base installation.

D3 · CEILING MIRROR HOLD POINT

Approve panel modules, weight, support structure, retention and accessible lighting as one overhead assembly. Site verification + support designer + glazier release it. The render and this guide supply appearance and coordination, not engineering.

Build scope + release gates

USE	Quote each line with its stated quantity basis. A quote, digital completion mark or approved sample does not override a field, shop-drawing, engineering, official-review or Greg-decision hold.
-----	--

Prepare

PRE-01 · Field survey + full-size room mockup		1 visit Lead builder	Arrange now
SPEC	Laser + tape survey; photograph all eight corners, door swings, booth vestibule, ceiling, services, and existing gear. Tape full furniture and occupied-seat envelopes on the floor.		
RELEASE GATE	Record M-01 through M-15; Greg approves the occupied mockup before custom work.		
SOURCE	Basis · Current brief + new coordination scope Sheet · A01		
PRE-02 · Trade drawings + approval review		1 package Lead builder	Quote now
SPEC	Coordinated millwork, glazing/support, lighting/power, floor-transition and acoustic details. Confirm landlord and city review required for the selected scope.		
RELEASE GATE	Lead builder confirms review route and inspection points before strip-out.		
SOURCE	Basis · New coordination scope Sheet · A01		
PRE-03 · Protection, removals + disposal		1 scope Lead builder	Quote now
SPEC	Document and label retained gear; move to protected storage; protect corridor and sliders; isolate power for two main-room troffers and booth troffer. Retain doors, HVAC access and absorption pending review.		
RELEASE GATE	Safe isolation and staged room closure; no blind demolition of fabric or ceiling.		
SOURCE	Basis · Current brief + booth photos Sheet · A01		

Mirrors

MIR-01 · Five antique-mirror arches		5 panels Glazier	Hold custom order
SPEC	Proposed 24 W × 90 H in overall envelope; semicircular 12 in head radius. Black smoked antique appearance with gold veining; approve an illuminated sample. Field-template all shapes, clearances and support.		
RELEASE GATE	M-03 + M-12 + M-07; glazier confirms glass build-up, weight, retention, edge protection and compatible materials.		
SOURCE	Basis · Approved concept; dimensions are proposed Sheet · A02		
CANDIDATE	Candidate · Omega Antique Mirror Dark Cloud, Smoky Quartz, and Gold Vein Overlay Samples		
MIR-02 · Lit ceiling mirror inset		1 assembly Glazier + support designer	Hold custom order
SPEC	Proposed 96 × 96 in visual zone, surface-applied beneath the flat ceiling. Finish to match arches; removable service access. Panel modules, thickness, backing, anchors and total weight are by the support designer.		
RELEASE GATE	M-03 + M-07 + M-09 / M-10; approved overhead assembly and structural load path. Adhesive alone is not a released detail.		
SOURCE	Basis · Approved concept; structural assembly unknown Sheet · E01		
CANDIDATE	Candidate · Omega Antique Mirror Dark Cloud, Smoky Quartz, and Gold Vein Overlay Samples		

Bar + piano

BAR-01 · Compact bar carcass		1 assembly Millworker	Hold custom order
SPEC	48 in long × 26 in deep × 42 in finished counter height proposed, south of the NU1X with an 8 in nominal gap; black finish, serviceable fridge bay, clear front vent and accessible outlet. Zephyr candidate needs 23-3/8 in body depth + 1 in rear clearance; final cabinet/shop drawing controls.		
RELEASE GATE	M-12 / M-11; appliance cutout, open door, ventilation, cable/plug space and occupied furniture mockup approved. Proposed bar and north stool still overlap the sectional envelope. Increase depth if chosen fridge requires it.		
SOURCE	Basis · Reviewed source 1a1d56d; depth increased from its 24 in to proposed 26 in Sheet · A03		

BAR-02 · Black stone counter + support		1 top Stone fabricator	Hold custom order
SPEC	48 × 26 in nominal top, honed black stone or approved quartz sample; eased edge. Finished counter top 42 in AFF. Template after carcass installation; fabricator details thickness, joints and supported overhangs.		
RELEASE GATE	Installed carcass surveyed; refrigerator and three-stool fit resolved.		
SOURCE	Basis · Current brief; nominal dimensions Sheet · A03		

BAR-03 · Smoked-glass bar front		1 set Glazier	Hold custom order
SPEC	Field-sized smoked-glass infill with brushed brass trim and warm diffused backlight. Keep refrigerator ventilation and service panel clear. Specify appropriate safety glazing and retention for this location.		
RELEASE GATE	Millwork shop drawing and lit glass sample approved.		
SOURCE	Basis · Approved concept Sheet · A03		

BAR-04 · Backlit bottle shelves		2 shelves Millworker	Hold custom order
SPEC	48 L × 10 D in nominal; proposed shelf tops 60 and 78 in AFF. Black finish; recessed diffused LED; hidden cable route and removable channel cover. Brackets/backing designed for bottles and glassware.		
RELEASE GATE	M-12 / M-11 + M-07; backing, shelf load and bottle-height mockup approved.		
SOURCE	Basis · Current element schedule; dimensions proposed Sheet · A03		

BAR-05 · Front-venting glass-door beverage fridge		1 unit Millworker + electrician	Select + verify fit
SPEC	Built-in-rated narrow glass-door model, black finish; blue interior light is visual intent. Size the cabinet from the selected installation manual, including door swing and ventilation.		
RELEASE GATE	Verify product cutout and depth before BAR-01 shop drawings; do not enclose a freestanding appliance.		
SOURCE	Basis · Current brief Sheet · A03		
CANDIDATE	Candidate · Zephyr Presrv PRB15C01CG 15-inch Beverage Cooler		

BAR-06 · Dark leather bar stools		3 stools Furniture	Hold fit decision
SPEC	Approx. 30 in seat height with foot rings for 42 in counter. Source placeholders are 15 in diameter at 18 in centers; allow actual occupied envelopes in the mockup.		
RELEASE GATE	M-12 / M-11. A 48 in bar provides only 16 in of run per person for three seats. Confirm a workable arrangement or obtain Greg's layout decision.		
SOURCE	Basis · Three stools fixed in brief; spacing unresolved Sheet · A03		

KEY-01 · Yamaha NU1X hybrid upright + bench		1 set Piano supplier	Verify ownership
SPEC	Yamaha NU1X polished ebony: manufacturer lists 59-1/8 W × 18-1/4 D × 40-5/16 H in. Place at the north end of the west wall, north/right of the bar when facing west. Proposed north setback 3 in, then actual piano body and 8 in gap before bar. Confirm exact model and ownership; the brief understated width by 1-5/8 in. NU1XA is a separate substitution.		
RELEASE GATE	M-11 + M-12 + M-15; confirm model, bench/playing clearance and delivery route. The bench overlaps the sectional envelope. Inventory does not establish NU1X ownership.		
SOURCE	Basis · Reviewed source 1a1d56d corrects brief direction; inventory conflict remains Sheet · A03		
CANDIDATE	Candidate · Yamaha AvantGrand NU1X		

Lounge

SEAT-01 · Curved charcoal sectional		1 sofa Upholsterer	Hold fit decision
SPEC	Approx. 100 W × 46 D × 30 H in source envelope. Charcoal patterned performance fabric and low dark plinth; back toward mirrors. Obtain actual curved footprint and upholstery sample.		
RELEASE GATE	M-12; current envelope overlaps the piano bench, bar corner and north stool. Full-size occupied mockup must pass before order; also test south stool against west swivel.		
SOURCE	Basis · Approved concept; source envelope is not a proven fit Sheet · A01		

SEAT-02 · Black leather swivel chairs		2 chairs Furniture	Hold fit decision
SPEC	Approx. 30 × 30 in source envelope, low back, black base. Check rotated envelope and a seated person's knees rather than the catalogue box alone.		
RELEASE GATE	M-12; approve route to desk, bar, piano and booth with both chairs occupied.		
SOURCE	Basis · Approved concept; nominal envelope Sheet · A01		

SEAT-03 · Smoked-glass cocktail table		1 table Furniture	Hold fit decision
SPEC	30 in diameter × 16 in high proposed. Black pedestal and smoked-glass top. Recheck actual sofa-to-table access in mockup.		
RELEASE GATE	M-12; the source's sofa-to-table gap is only 7 in.		
SOURCE	Basis · Current model envelope Sheet · A01		

SEAT-04 · Dark patterned lounge rug + pad		1 set Flooring + furniture	Sample now
SPEC	120 × 108 in nominal custom size from source model; charcoal medallion/pattern and low pile. Select edge treatment and pad compatible with the chosen floor.		
RELEASE GATE	Final furniture footprint and clear circulation confirmed; do not cover thresholds or ventilation.		
SOURCE	Basis · Approved concept; custom size proposed Sheet · A01		

Finishes

FIN-01 · Dark main-room floor		328.75 sq ft allowance Flooring	Sample + quote
SPEC	298.86 sq ft source polygon × 1.10 waste = 328.75 sq ft before carton rounding. Karndean Ebony SCB89 candidate: 14 cartons × 23.64 = 330.96 sq ft. Remove existing floating LVP for this product; preserve boards where feasible. Keep-oak + rug alternative requires Greg's finish decision.		
RELEASE GATE	M-08; moisture/flatness, underlayment, thresholds, door clearances and final installed buildup approved.		
SOURCE	Basis · Derived from unverified shell + proposed 10% waste Sheet · A01		
CANDIDATE	Candidate · Karndean Van Gogh Rigid Core Ebony SCB89		

FIN-02 · Charcoal wall finish + acoustic retention		1 measured scope Finish contractor + acoustician	Sample + quote
SPEC	Remove the visual chair-rail division through a coordinated trim/fabric detail. Keep existing absorptive construction until assessed; re-cover in charcoal acoustically suitable fabric where retained. Plaster only approved solid surfaces.		
RELEASE GATE	M-07 + M-14; finish sample and acoustic scope approved. Gross wall area is only an estimating upper bound.		
SOURCE	Basis · Visual intent with proposed acoustic-preserving approach Sheet · A02		
CANDIDATE	Candidate · FabriTRAK GeoTRAK Black Fabric-Retention Profiles / Guilford of Maine FR701, style 2100, color 408 Black		

FIN-03 · Black slat panels at bay returns		66.08 sq ft net Finish carpenter	Sample + quote
SPEC	Two nominal returns: 47.23 and 46.06 in long × 102 in high. Black wood slats and black backing. Obtain tested assembly data; coordinate joints, hanger backing and service access. The 94.49 in WoodUpp candidate is 7.51 in short of 102 in; agree a joint or taller product before ordering.		
RELEASE GATE	M-01 / M-02 + M-03 + M-13 / M-11; panel size, fire-performance documentation and return angles approved.		
SOURCE	Basis · Derived return lengths; ceiling unverified Sheet · A04		
CANDIDATE	Candidate · WoodUpp Akupanel Colored Black Wrapped on Black Felt, item 1029		

FIN-04 · Ceiling, trim + exposed solid-surface paint		1 scope Painter	Quote now
SPEC	Matte black ceiling and cove fascia; compatible dark finish on approved solid walls and trim. Sample sheen under actual 2700K light. Keep paint off acoustic fabric, equipment and labels.		
RELEASE GATE	Patch/rough-in inspection complete; substrate prep and finish samples approved.		
SOURCE	Basis · Current visual brief Sheet · E01		

Studio + guitars

DESK-01 · Fixed production desk + 12U rack		1 set Millworker + AV	Survey + quote
SPEC	72 L × 32 D × 30 H in nominal desk along bay face; console secured, rack under north end, removable cable trays, clear knees and accessible service. Reuse suitable owned desk/rack if verified.		
RELEASE GATE	M-02 + M-11 + M-13; confirm bay dimensions, PMC identity, rack depth/heat, exact console, display and engineer-chair clearance.		
SOURCE	Basis · Current brief; product fit unverified Sheet · A04		

GTR-01 · Guitar/bass hangers + structural backing		10 positions Carpenter + AV	Hold fit decision
SPEC	Ten securely supported hangers. Two rows of five remain the requested concept. Template actual headstocks, bodies and removal arcs above desk; bracket and finish compatibility per maker.		
RELEASE GATE	M-02 + M-07 + M-11 + M-13. Two full-height rows do not yet fit the stated ceiling/desk zone; Greg approves a tested elevation before holes or backing heights are fixed.		
SOURCE	Basis · Current brief; current model differs Sheet · A04		
CANDIDATE	Candidate · String Swing CC01K Hardwood Home & Studio Guitar Keeper		

GTR-02 · Additional instruments, buy or borrow		4 provisional instruments Greg + AV	Inventory first
SPEC	Reconcile the six listed owned guitars/basses against ten display positions. Borrow or reassign suitable instruments first; record model, size, weight and finish for each hanger.		
RELEASE GATE	M-11 inventory reconciled and GTR-01 elevation approved. Four is an inventory difference, not a purchase authorization.		
SOURCE	Basis · Current brief: 1 guitar + 5 basses Sheet · A04		

Light + power

LGT-01 · Perimeter cove tape + channel		71.6 linear ft net Lighting supplier + electrician	Sample + quote
SPEC	2700K, CRI 90+ minimum; continuous diffused warm line. 71.60 ft derived perimeter. Separate feed runs and accessible matched drivers; no unsupported continuous-run assumption.		
RELEASE GATE	M-03 + M-09 / M-10; sample dimming, voltage-drop/run-length design and feed locations approved.		
SOURCE	Basis · Derived shell perimeter Sheet · E01		
CANDIDATE	Candidate · Diode LED BLAZE 100 2700K Tape + S1 Black Channel + OMNIDRIVE Basics 96W Driver		

LGT-02 · Arch backlight tape + channel		80.71 linear ft net Lighting supplier + glazier	Sample + quote
SPEC	Five 24 × 90 in arches, lit along two sides and semicircular head; excludes bottom edge. Conceal individual feeds and leave removable access.		
RELEASE GATE	Final arch template and supplier-approved bend/cut/channel detail; continuous curved light may require a different product from straight cove tape.		
SOURCE	Basis · Calculated from proposed arches Sheet · A02		

LGT-03 · Ceiling inset perimeter backlight		32 linear ft net Lighting supplier + glazier	Sample + quote
SPEC	Four sides of nominal 96 × 96 in ceiling inset; diffused 2700K line with source concealed from the seated view.		
RELEASE GATE	Mirror support, service access and lighting detail coordinated before fabrication.		
SOURCE	Basis · Calculated from proposed inset Sheet · E01		

LGT-04 · Shelf + counter accent tape		12 linear ft net Lighting supplier + millworker	Sample + quote
SPEC	Two 48 in shelves plus one 48 in counter accent = 12 ft net; diffused 2700K lighting. Keep tape heat and driver access away from stored bottles and fridge intake.		
RELEASE GATE	BAR-01 + BAR-04 shop drawings and compatible driver/channel selected.		
SOURCE	Basis · Calculated from proposed bar Sheet · A03		

LGT-05 · Main-room 4 in downlights		12 fixtures Electrician	Select + mock up
SPEC	2700K, CRI 90+ minimum, black trim or verified black-trim option. Proposed coordination points avoid the ceiling mirror; confirm fixture depth, driver space, ceiling ratings and actual light distribution.		
RELEASE GATE	M-03 + M-09 / M-10; ceiling investigation, fixture/dimmer test and lighting plan approved. Surface alternative requires visual approval if recessing cannot work.		
SOURCE	Basis · Current brief 10–12; proposed count12 Sheet · E01		
CANDIDATE	Candidate · Nora Lighting NM4-RDC27BB 4-inch Round Deep Cone Reflector		

LGT-06 · Guitar-wall track + four heads		1 set Electrician	Select + mock up
SPEC	Black track, four adjustable 2700K CRI90+ heads proposed; compatible track/feed family. Aim to avoid screen, mirror and seated-eye glare.		
RELEASE GATE	Guitar elevation + ceiling support + electrical control choice approved.		
SOURCE	Basis · Current model proposed count4 Sheet · E01		

LGT-07 · Lighting control + matched drivers		1 engineered package Electrician + AV	Quote after samples
SPEC	Independently controllable cove, downlights, mirror glow, bar/shelves, guitar track and booth. One user scene interface. Reconcile earlier DMX requirement with current dimmer-system brief before selecting protocol.		
RELEASE GATE	M-09 / M-10; signed load/run schedule, fixture/dimmer compatibility, service access and camera/low-level dim tests.		
SOURCE	Basis · Control conflict remains open Sheet · E01		
CANDIDATE	Candidate · Diode LED BLAZE 100 2700K Tape + S1 Black Channel + OMNIDRIVE Basics 96W Driver		

PWR-01 · Surveyed electrical + low-voltage work		1 scope Electrician + AV	Survey + quote
SPEC	Map panel/circuits and actual loads; plan AV, lights, fridge and general receptacles from survey. Label circuits. Separate Apollo/TV power arrangement per verified AV plan; diagnose hum before selecting remedies.		
RELEASE GATE	M-09 / M-10; licensed design and inspections as applicable. Never remove safety earth or treat a power strip as an isolation design.		
SOURCE	Basis · Current operational rules; no circuit schedule exists Sheet · E01		

Studio + guitars

AV-01 · Retained AV + plug-and-play commissioning		1 scope AV engineer	Quote now
SPEC	Retain verified PMC mains, HS8s, Turbosound PA/pole, interfaces, Trinnov, sub and member laptop station. PA stays north of the desk: verify actual base footprint, pole stability, aim and cable route; A01 uses the provisional 14 × 14 in source box. Korg always connected at seated height. Label R-01... at cable heads; print patch map; front Furman outlet free; Mac sleep disabled. Confirm both PMC envelopes inside the canted shell and the Korg bench clear of D-2; current plan flags these fit checks.		
RELEASE GATE	M-11 + M-14; cold-start, channel, hum, latency, monitor, PA coverage, booth and laptop tests pass; Trinnov/sub operating rule documented.		
SOURCE	Basis · Current brief + retained inventory Sheet · A01		
CANDIDATE	Candidate · Korg Grandstage X		

Booth

BOO-01 · Booth fabric/absorber work + cloud review		1 measured scope Acoustician + carpenter	Survey + quote
SPEC	Retain existing drum/vocal function and glass separation. Evaluate six nominal 24 × 48 × 2 in wall panels plus one 48 × 48 in cloud as a provisional treatment study; preserve existing absorption until measured.		
RELEASE GATE	M-05 + M-07 + M-14; approve actual coverage, response, fire-performance documentation, clearances and ceiling suspension.		
SOURCE	Basis · Current booth intent; quantities proposed Sheet · A05		
BOO-02 · Booth floor finish + retained rug		1 measured scope Flooring	Sample + quote
SPEC	Charcoal low-pile carpet tile or approved acoustic finish; keep existing Persian rug if serviceable. Trace curved wall and vestibule for takeoff; check slider tracks, thresholds and instrument access.		
RELEASE GATE	M-05 + M-08; selected flooring assembly approved for existing floor/substrate.		
SOURCE	Basis · Current booth element schedule Sheet · A05		
BOO-03 · Booth warm lights + service checks		2 downlights Electrician + HVAC + AV	Survey + quote
SPEC	Two proposed 4 in 2700K lights, separate control from lounge; retain working/task light in all scenes. Recheck HVAC airflow, noise, camera, TV, mic boom, rack and drum clearances.		
RELEASE GATE	M-03 + M-05 + M-09 / M-10 + M-06 / M-14; coordinate cloud, access and microphone positions.		
SOURCE	Basis · Current booth element schedule Sheet · A05		

Complete

CLOSE-01 · Styling, spare materials + handover		1 scope Lead builder + Greg	After commissioning
SPEC	Plant, restrained brass/black accessories and flameless candles. Keep labeled finish samples, spare flooring, LED product records, paint codes, as-built dimensions, patch/circuit maps and driver access photos.		
RELEASE GATE	Full punch list, operation test, cleaning and Greg's room walk-through complete.		
SOURCE	Basis · Approved visual intent + new handover scope Sheet · A01		

Sequence · 7 phases / 43 checks

PROGRESS CONTROL

Check boxes capture progress and evidence. They never release affected purchase, fabrication, permit, engineering or installation holds. Revisions caused by field findings flow through every affected layout and review.

P0 · Freeze the field record

Owner · Owner representative + field survey lead

Sequence allowance · Low-confidence allowance: 1-2 site days after access

Depends on · None

Ready when

- ✓ Current brief, approved concept, frozen Pass 7 source commit 1a1d56d, initial 70-element snapshot, labeled plan and inventory are in the field packet.
- ✓ Main room, closet, vestibule and booth are accessible with ceiling and electrical access arranged.

- ☐ **P0-T1** · Laser-check every main-room wall, both diagonals, ceiling height at four points and both bay returns.

Evidence · Dimension log, marked plan and scale photos agree.

- ☐ **P0-T2** · Survey D-2, the west-wall D-3 at z 223..259, closet, vestibule, both slider layers and the booth curve from named control points.

Evidence · Openings, jambs, swings, thresholds and glass overlap are recorded; D-3 is photographed from both sides with its south hinge and inward swing identified.

- ☐ **P0-T3** · Open one approved ceiling and wall inspection point; record plenum, structure, studs, backing and acoustic-fabric build-up.

Evidence · Photos include a ruler and the exact inspection location.

- ☐ **P0-T4** · Photograph the panel schedule, breakers, receptacles, data plates, tie lines, lighting controls and HVAC supply/return path.

Evidence · Each device is keyed to the marked plan.

- ☐ **P0-T5** · Audit every retained instrument, speaker, rack item and booth object against the inventory by model and current location.

Evidence · Discrepancies are listed without relabeling assumed items as owned.

- ☐ **P0-T6** · Lay out the corrected west-wall sequence and the rest of the room full size: NU1X at the north end, source-proposed 8-inch gap, 48-inch bar, three stools, west-wall D-3, lounge, desk, Korg and door swings. Test the source 24-inch bar depth and the proposed 26-inch depth allowance required by the verified refrigerator candidate.

Evidence · Dimensioned photos show the north-to-south west-wall order, piano-bench/sofa, 26-inch-bar-corner/sofa, north-stool/sofa and south-stool/west-swivel conflicts, access route and both door swings; neither bar depth, gap nor any seating fit is released by the mockup alone.

Stop if

- ! Any shell discrepancy changes fit, access or a fabrication dimension; discrepancies over 2 percent escalate immediately to Greg and the design professional.
- ! The labeled-plan door or booth geometry does not match the room.
- ! Ceiling, wall, floor or panel access cannot be inspected safely.

P1 · Issue the coordination set

Owner · Design professional + general contractor

Sequence allowance · Low-confidence allowance: 1-3 weeks after the field record

Depends on · P0

Ready when

- ✓ Field record is signed and dated.
- ✓ Every conflict has an owner and a written resolution path.

- ☐ **P1-T1** · Redraw the main room, closet, vestibule and booth from the field record; remove the nonexistent Live Room door.

Evidence · Plan dimensions close and match the field log.

- ☐ **P1-T2** · Prepare furniture, equipment, door-swing and access plans around the approved three-stool and 5+5 guitar concepts.

Evidence · No locked element is traded away; the plan shows NU1X north of the bar, D-3 on the west wall, and every unresolved seating conflict.

- ☐ **P1-T3** · Prepare north, west, bay and booth elevations with AFF heights, mounting zones and field-verified backing.

Evidence · Mirror, shelf, piano, desk, display, guitar, absorber and 94.49-inch slat-panel termination heights are dimensioned.

- ☐ **P1-T4** · Prepare a reflected ceiling plan for the ceiling mirror, cove, downlights, track, booth lights, detectors and retained devices.

Evidence · Every fixture has a coordinate, circuit/control zone and access note.

- ☐ **P1-T5** · Have the electrician and building official or design professional confirm permit/review scope, egress criteria and the 36-inch planning target.

Evidence · Written direction states the governing review and required path width.

- [] P1-T6** · Issue structural attachment details for wall mirrors, overhead mirror, guitar blocking, track, panels and ceiling-mounted work.
Evidence · Details name substrates, fasteners, loads and inspection hold points.

- [] P1-T7** · Set change control: every field or as-built departure updates each affected plan, elevation, reflected ceiling plan, fit check, quote and order before work resumes.
Evidence · Revision log names the changed dimension, downstream documents, reviewer and release decision.

Stop if

- ! Permit or review responsibility is still unnamed.
- ! Door swings, access path or equipment service zones remain unresolved.
- ! Any attachment detail relies on unverified backing or ceiling structure.

P2 · Quote, sample and release purchases

Owner · Owner representative + general contractor
Sequence allowance · Vendor lead times; release only after field and design holds clear
Depends on · P1

Ready when

- ✓ Issued coordination drawings carry a revision and date.
- ✓ Quote requests use field-verified quantities and written alternates.

- [] P2-T1** · Quote five wall arches and the overhead mirror as separate packages with safety, edge, backing, weight and attachment data.
Evidence · Glazier quote follows issued dimensions and attachment details.

- [] P2-T2** · Quote the 48-inch bar, shelves and three stools with the Pass 7 source's 24-inch depth and the proposed 26-inch depth allowance; coordinate the Zephyr body, 1-inch rear plug clearance, front vent, service pullout and west-wall D-3.
Evidence · Shop drawing proves appliance, outlet, vent and pull-out service while the full-size layout records piano-bench/sofa, 26-inch-bar-corner/sofa, north-stool/sofa and south-stool/west-swivel conflicts; depth, gap and seating remain held for Greg's approval.

- [] P2-T3** · Obtain samples for wall finishes, 94.49-inch slat panels, booth finishes, a compatible dark-floor assembly and the explicit keep-oak-plus-rugs alternative.
Evidence · Approved sample board records product, color, sheen, assembly, fire data and room location.

- [] P2-T4** · Quote the complete lighting and control package from the reflected ceiling plan, including drivers, dimming, emergency compatibility and commissioning.
Evidence · Fixture and control schedule has approved SKUs and substitutions.

- [] P2-T5** · Confirm the 59.125 by 18.25 by 40.3125 inch NU1X, the 53.98 by 18.15 inch Grandstage X body and stand, PMC model, booth kit and four additional guitars.
Evidence · Purchase list separates owned, relocate, buy and pending-verification items and uses verified product envelopes.

- [] P2-T6** · Release long-lead orders only after field dimensions, finish samples, access path and written owner approval match the order.
Evidence · Order log records approver, revision, deposit, lead time and cancellation terms.

Stop if

- ! A quote uses the old 96-inch bar, four stools, reversed bar/piano order, south-wall D-3, old booth position or an uncoordinated refrigerator depth.
- ! A vendor substitutes a product without a reviewed sample or technical submittal.
- ! A long-lead item lacks verified delivery access or field dimensions.
- ! A field or as-built change has not been reviewed against every affected quote and order.

P3 · Protect, isolate and open the work

Owner · General contractor
Sequence allowance · Low-confidence allowance: 2-4 site days
Depends on · P1

Ready when

- ✓ Permit/review path and selective-demolition scope are documented.
- ✓ Retained equipment, glass, flooring and acoustic fabric are tagged and protected.

- [] P3-T1** · Photograph, label, disconnect and relocate retained AV, instruments and booth contents to a protected inventory zone.
Evidence · Move log identifies each item and destination.

- [] P3-T2** · Protect the oak LVP, sliders, closet door, camera, grille and acoustic fabric while flooring and finish decisions remain open.
Evidence · Protection is continuous at traffic and dust paths.

- [] P3-T3** · Remove the main-room and booth troffers, abandoned fixtures and only the finishes marked for removal on issued drawings.
Evidence · Circuits are made safe and removed items are logged.

- [] P3-T4** · Open only the wall and ceiling areas needed for approved backing, wiring, lighting and inspection.

Evidence · Hidden conditions are photographed before concealment.

- [] P3-T5** · Confirm whether the oak LVP is floating or adhered, then record flatness, moisture, threshold build-up and dark-floor assembly options.

Evidence · Installer states whether the proposed product is warrantable; oak removal remains a Greg approval hold.

Stop if

- ! Demolition exposes moisture, damaged framing, unsafe wiring or undocumented isolation construction.
- ! The acoustic fabric cannot be removed and reinstated as assumed.
- ! Protected equipment or glass remains in the active work zone.
- ! A hidden condition changes an issued layout and the affected documents have not been reissued.

P4 · Complete rough-in and backing

Owner · General contractor + licensed electrician + AV integrator

Sequence allowance · Low-confidence allowance: 1-2 weeks, subject to inspection

Depends on · P2, P3

Ready when

- ✓ Approved submittals and attachment details are on site.
- ✓ Wall and ceiling cavities are open for coordinated work.

- [] P4-T1** · Install inspected backing for arches, shelves, guitar hangers, slat panels, displays, absorbers and ceiling mirror supports.

Evidence · Backing photos include dimensions before closure.

- [] P4-T2** · Install permitted branch circuits, receptacles, drivers and controls from the electrician's field-verified design.

Evidence · Rough inspection and circuit directory are complete.

- [] P4-T3** · Route separate labeled pathways for power, analog audio, digital audio, network, display and member-laptop connections.

Evidence · Pathway plan and pull labels match the rack schedule.

- [] P4-T4** · Rough in the cove, downlights, guitar track, mirror halos, bar LEDs and booth lighting from the approved ceiling and control plans.

Evidence · Driver access and fixture cutouts are verified before closure.

- [] P4-T5** · Service the documented HVAC scope without covering the closet grille, return path, controls or camera view.

Evidence · Air path and maintenance access remain open.

- [] P4-T6** · Run an inspection hold before walls and ceiling close; compare every rough-in to the issued revision.

Evidence · Signed punch list is closed or carried visibly.

Stop if

- ! Electrical capacity, grounding topology or control compatibility is unresolved.
- ! A ceiling fixture or mirror support lacks verified structure.
- ! Door, slider, HVAC or equipment-service access is obstructed.
- ! Installed rough-in departs from the issued revision without downstream layout review.

P5 · Install shell, finishes and fixed elements

Owner · General contractor + finish trades

Sequence allowance · Low-confidence allowance: 1-3 weeks plus vendor lead time

Depends on · P4

Ready when

- ✓ Rough inspections and concealment photos are complete.
- ✓ Approved samples and field templates are on site.

- [] P5-T1** · Close and finish wall and ceiling openings; apply the controlled main-room wall-finish decision and matte-black ceiling finish.

Evidence · Mockup, sheen and acoustic-treatment disposition match the approval record.

- [] P5-T2** · Execute Greg's approved floor decision: keep oak with rugs, or remove/preserve it as feasible and install a warrantable dark-floor assembly; complete the booth floor finish.

Evidence · Written approval, installer warranty, transitions and door/slider operation are recorded.

- [] P5-T3** · Install the approved bar, shelves, fridge, slat-panel termination and desk; preserve appliance, rack and cable service access.

Evidence · Millwork dimensions, refrigerator clearances, 102-inch-wall panel joint/trim and service openings match submittals.

- [] P5-T4** · Install wall arches and overhead mirror under the approved glazing and attachment details.

Evidence · Glazier documents safety backing, edge condition, fasteners and final inspection.

- P5-T5 · Install booth absorbers, ceiling cloud and lighting while retaining sliders, kit sightline, TV, desk and mic-boom use.

Evidence · Booth plan and elevations match the installed work.
- P5-T6 · Mount the approved 5+5 guitar layout from a full-size field template only after the actual ten instruments are assigned.

Evidence · Each yoke, body envelope, headstock and removal path clears lights, display and speakers.

Stop if
! A field template or as-built condition differs from an issued layout and the affected documents have not been reviewed and reissued.
! Mirror, millwork or flooring dimensions require site cutting outside approved tolerances.
! A finish change would remove acoustic treatment without written disposition.

P6 · Set equipment, commission and hand over	Owner · AV integrator + general contractor + owner representative Sequence allowance · Low-confidence allowance: 2-4 commissioning days Depends on · P5
---	--

Ready when
✓ Fixed work is complete, clean and powered.
✓ Open inspection and safety items are closed.

- P6-T1 · Set the approved three stools, NU1X, lounge, Korg, desk, monitors, rack, amps and booth kit from the verified plan, preserving the north-to-south west-wall order of NU1X, bar and D-3.

Evidence · Full-size layout, recorded seating clearances and both door swings match the approved field record.
- P6-T2 · Patch and label every cable R-01 onward at the cable head; issue rack, tie-line and signal-flow records.

Evidence · A second person traces each labeled path successfully.
- P6-T3 · Have the electrician and AV integrator test circuits, investigate hum/static and document the accepted power arrangement.

Evidence · Test record names the observed fault, corrective work and retest result.
- P6-T4 · Commission lounge, session and meditation lighting scenes at 2700K; verify all controls, drivers and service access.

Evidence · Scene levels and control labels are recorded.
- P6-T5 · Measure room response, noise floor and HVAC-on/HVAC-off conditions; tune monitoring from the recorded baseline.

Evidence · Before/after files, mic position and settings are archived.
- P6-T6 · Verify member laptop audio, always-on Korg audio, Turbosound PA coverage and stability, no-sleep computer, separate Apollo/TV power, empty front Furman plug and always-powered Trinnov/sub rules.

Evidence · A cold-start member workflow completes without troubleshooting; PA aiming and cable routes preserve occupied access.
- P6-T7 · Deliver as-builts, change-impact log, approved submittals, warranties, spare finishes, cleaning instructions and open-item log.

Evidence · As-builts include every approved field change and the owner representative signs the handover record.

Stop if
! Door, slider, access or required egress path is blocked.
! Electrical noise, overheating, control failure or unstable mounting remains.
! The member workflow or retained power rules fail the witnessed test.

Trade scope + acceptance

Use these boundaries in bid invitations and coordination reviews. Exclusions are named so work is not assumed by silence.

TR-01 · General contractor / site coordinator

SCOPE	• Site logistics, protection, selective demolition, sequencing and daily coordination. • Coordinate main room, closet, vestibule and booth as one work area.
DELIVER	• Baseline schedule with low-confidence allowances identified. • Submittal, RFI, inspection, photo and punch logs.
ACCEPT	✓ Issued revision is present at each installation. ✓ Retained items and access routes remain protected and usable.
EXCLUDES	– Structural, electrical, HVAC, acoustic or code design outside the contractor's license.

TR-02 · Design professional / permit coordinator

SCOPE	• Field-verified plans, elevations, reflected ceiling plan and attachment coordination. • Confirm permit/review and egress criteria with the building official.
DELIVER	• Issued coordination set with revision history. • Written permit, review and inspection matrix.
ACCEPT	✓ Drawings reconcile the corrected doors, vestibule, booth and closet. ✓ Locked owner decisions are visible and unresolved choices are marked.
EXCLUDES	– Treating the concept render or old v0.1 draft as permit documents.

TR-03 · Licensed electrician / lighting controls

SCOPE	• Survey panel, circuits, grounding topology, fixtures, controls and available capacity. • Design and install permitted power and lighting work.
DELIVER	• Circuit and control schedules, fixture submittals and test results. • Updated panel directory and as-built device plan.
ACCEPT	✓ Rough and final inspections pass. ✓ Lighting scenes, drivers, dimming and service access work under load.
EXCLUDES	– Assuming a ground-loop cause or copying the unverified old circuit scheme.

TR-04 · Carpenter / millworker / flooring installer

SCOPE	• Backing, bar, shelves, desk interfaces, wall preparation, slat panels and floor finishes. • Build from field templates at bay, closet, door and slider edges.
DELIVER	• Shop drawings, finish samples, hardware schedule and field templates. • Substrate, floor-flatness, floor-assembly and transition report.
ACCEPT	✓ Fixed work matches verified dimensions and approved samples. ✓ Appliance, rack, cable, door and slider service access remains open.
EXCLUDES	– Changing the 48-inch bar, three stools or 5+5 guitar concept, removing oak flooring or hiding a slat-panel joint without written approval.

TR-05 · Glazier / mirror installer

SCOPE	• Five wall arches, overhead mirror, edge treatment, safety backing and attachment system. • Coordinate halos, brass trim, access panels and adjacent finishes.
DELIVER	• Shop drawings, glass makeup, weights, samples and attachment calculations. • Installation and final inspection record.
ACCEPT	✓ Glass, backing, edges and supports match approved details. ✓ No exposed sharp edge, unstable panel or blocked service access remains.
EXCLUDES	– Fabricating from concept-image proportions or unverified ceiling structure.

TR-06 · HVAC / acoustic consultant

SCOPE	• Document supply, return, airflow, noise and main-room/booth acoustic baseline. • Review wall-fabric disposition, booth absorbers and ceiling cloud.
DELIVER	• HVAC access and performance note. • Before/after acoustic measurements and treatment placement plan.
ACCEPT	✓ Air path, maintenance access and camera/grille clearances remain open. ✓ Treatment decisions cite measured conditions rather than assumed NRC.
EXCLUDES	– Claiming the existing grey fabric's performance without testing or construction data.

TR-07 · AV / studio integrator

SCOPE	• Verify equipment, rack, monitoring, Turbosound PA/pole north of desk, patching, laptop workflow, labels and signal paths. • Coordinate AV power and low-voltage routes with the electrician.
DELIVER	• Equipment and cable schedule, rack elevation, patch map and signal-flow drawing. • Commissioning record for monitoring and member workflow.
ACCEPT	✓ All R-number labels trace correctly. ✓ Cold-start laptop, Korg, DAW, PA coverage and monitoring tests pass.
EXCLUDES	– Substituting IB1S for IB1 or moving unidentified inventory without approval.

Retained conditions + gear

DEFAULT ACTION	Protect, identify and verify retained work before removals. An unknown existing assembly stays in place until the named decision is made.
R-01	Existing light-oak LVP; dark-floor change remains controlled
VERIFY	Floating versus adhered assembly, substrate, moisture, flatness, transitions and door clearances.
ACTION	Protect and keep oak-plus-rugs explicit; if the selected dark floor requires removal, obtain Greg's written approval and preserve the oak where feasible.
R-02	Grandfathered existing grey acoustic fabric and hidden wall assembly
VERIFY	Construction, attachment, condition and measured acoustic contribution.
ACTION	Keep in place until the controlled finish/acoustic decision is issued.
R-03	HVAC closet, D-2, supply grille and dome camera
VERIFY	Field dimensions, airflow, access, swing and camera view.
ACTION	Protect and keep serviceable; finish only exposed approved faces.
R-04	D-3 entry and required access path
VERIFY	West-wall opening at z 223..259, south hinge, inward swing, hardware, threshold and official egress criteria.
ACTION	Keep the full swing and reviewed path clear through every phase.
R-05	Two-layer sliding glass booth doors
VERIFY	Track condition, pane makeup, overlap, seals, head height and service access.
ACTION	Protect, clean and retain unless a reviewed repair is required.
R-06	Booth kit, Persian rug, desk, TV and mic boom
VERIFY	Actual identity, dimensions, condition and deployed positions; Pass 7 records the Persian rug as a provisional 66 by 88 inches from photos, still requiring field measurement, and includes no booth floor lamp.
ACTION	Inventory before moving; reset from the verified booth plan.
R-07	Korg Grandstage X and sitting-height stand
VERIFY	53.98 by 18.15 inch body, stand footprint, bench, music rest, pedals, cable bend, power, audio and MIDI paths.
ACTION	Keep in the main room and always available in audio.
R-08	HS8 pair, PMC pair, Turbosound PA/pole, rack and production electronics
VERIFY	Models, stand/base footprints, pole stability, PA aiming, service clearances, signal paths and power behavior.
ACTION	Protect, label, reinstall and commission; do not infer the PMC model.
R-09	Front Furman outlet, Trinnov and sub power rules
VERIFY	Witness current behavior and accepted electrician/AV power arrangement.
ACTION	Keep the front plug free; preserve required always-powered devices in the commissioned workflow.

Site-survey register · 15 bundles

RECORD ONCE		Photograph the mark, keep the raw reading, identify the measuring face and enter the result in the dated revision record. Findings update all affected plans, quantities and release reviews.
M-01	Main-room polygon and diagonals Greg tape measurement from May 2026; measured-as-typed, unverified current. A 2 percent discrepancy triggers escalation and redesign review, not fabrication tolerance.	
METHOD	Laser each wall at floor and 60 inches AFF; tape-check both diagonals.	
RECORD	Marked plan, raw readings, closure calculation and scale photos.	
UNLOCKS	P1-T1 · P1-T2 · P2-T2	
M-02	Bay face and canted returns Typed polygon gives 30.54 and 28 degrees; least reliable shell dimensions.	
METHOD	Measure both return lengths, offsets from the east wall line, face length and corner angles.	
RECORD	Four control points, diagonals and a rigid full-size desk-wall template.	
UNLOCKS	P1-T2 · P1-T3 · P5-T3 · P5-T6	
M-03	Ceiling plane, plenum and structure 102-inch plane is measured-as-typed; slab/drop construction and load capacity are unknown.	
METHOD	Laser floor-to-ceiling at four points; inspect one approved opening to structure.	
RECORD	Heights, plenum depth, framing direction, member spacing and photos.	
UNLOCKS	P1-T4 · P1-T6 · P2-T1 · P4-T4	
M-04	D-2 and D-3 door schedule Frozen Pass 7 source commit 1a1d56d places D-3 on the west wall at z 223..259, hinged south and swinging in; field opening, leaf, hinge, swing and 80-inch modeled height remain unverified.	
METHOD	Measure rough and finished openings, leaves, jambs, hinges, swings, thresholds and hardware.	
RECORD	Door schedule with photos from both sides and swing arcs on plan.	
UNLOCKS	P1-T1 · P1-T2 · P1-T5 · P6-T1	
M-05	Booth, vestibule and sliders Nominal room size comes from the labeled plan; current outline is a pixel trace, not a field survey.	
METHOD	Survey control points for vestibule depth, booth boundaries, curve, glass tracks, overlap and head height.	
RECORD	Point list, curve offsets, slider section and booth interior dimensions.	
UNLOCKS	P1-T1 · P1-T3 · P5-T5	
M-06	HVAC closet, grille and camera Closet is nominally 34 by 46 inches from the labeled plan; field size and HVAC performance are unknown.	
METHOD	Measure closet faces, door, grille, camera view, access panels and visible duct path.	
RECORD	Plan/elevation dimensions plus access and maintenance envelopes.	
UNLOCKS	P1-T1 · P4-T5	

M-07	Wall build-up and backing Existing grey stretched fabric is confirmed; its construction and acoustic performance are unknown.
METHOD	Open one approved fabric panel; locate studs and measure layers, spacing and existing blocking.
RECORD	Annotated section, stud map, photos and attachment assessment.
UNLOCKS	P1-T3 · P1-T6 · P4-T1

M-08	Floor, substrate and thresholds Light-oak LVP is existing. Karndean SCB89 forbids installation over a floating floor; existing installation and substrate are unknown.
METHOD	Inspect one threshold, determine floating versus adhered installation, map flatness, measure existing plank and test moisture for each proposed assembly.
RECORD	Substrate report, warranty statement, transition heights, door clearances and keep-oak/dark-floor options.
UNLOCKS	P2-T3 · P3-T5 · P5-T2

M-09	Panel, circuits and device map No verified panel or circuit schedule exists for this room.
METHOD	Licensed electrician traces breakers and records receptacles, loads, grounding topology and controls.
RECORD	Panel photo, circuit schedule, device plan and test notes.
UNLOCKS	P1-T4 · P2-T4 · P4-T2 · P6-T3

M-10	Existing lighting and control Prior rig was partly moved; current fixtures and control are unverified.
METHOD	Count, locate and energize each troffer, can, track head, entertainment fixture, switch and controller.
RECORD	Fixture map, circuit/control response and retained/remove disposition.
UNLOCKS	P1-T4 · P2-T4 · P4-T4

M-11	Gear identity and dimensions Manufacturer data gives NU1X 59.125 W by 18.25 D by 40.3125 H inches and Grandstage X 53.98 W by 18.15 D inches excluding stand; field identity and installed envelopes remain open.
METHOD	Read model plates and measure actual PMC cabinets/stands, piano, Grandstage body/stand, drum kit, PA, display, desk and rack.
RECORD	Photo inventory with model, quantity, location and measured envelope; compare against manufacturer dimensions.
UNLOCKS	P2-T5 · P6-T1 · P6-T2

M-12	Full-room floor fit Pass 7 corrected the sequence but used a 57.5-inch piano and 24-inch bar; this guide corrects the NU1X to 59.125 inches and proposes a 26-inch bar for the verified refrigerator. Physical fit has not been field-proven.
METHOD	Tape the corrected north-to-south west-wall sequence with the NU1X north edge at z 3, corrected 59.125-inch body centered at z 32.5625, source-proposed 8-inch gap, 48-inch bar from z 70.125 to 118.125, source 24-inch and proposed 26-inch depths, stools at z 76.125, 94.125 and 112.125, and D-3 at z 223..259; then operate doors, sliders, fridge, stools, chairs and service panels.
RECORD	Dimensioned overhead and corner photos; piano-bench/sofa, 26-inch-bar-corner/sofa, north-stool/sofa and south-stool/west-swivel conflict dimensions; west-wall D-3 swing; and signed layout sketch.
UNLOCKS	P1-T2 · P2-T2 · P6-T1

M-13	Full-size 5+5 guitar wall template 5+5 is locked design intent; the current one-row model does not prove it fits.
METHOD	Trace the actual ten instrument envelopes and yokes on paper or removable wall film at issued elevations.

RECORD	Instrument-to-position map, yoke centers, removal arcs and interference photos.
UNLOCKS	P1-T3 · P4-T1 · P5-T6

M-14	Acoustic and HVAC baseline No measured RT60, noise-floor, bleed or airflow baseline is on record.
METHOD	Record calibrated room response, noise floor and HVAC-on/off readings in the empty main room and booth.
RECORD	Audio files, mic position, settings, temperature and operating conditions.
UNLOCKS	P2-T3 · P5-T1 · P5-T5 · P6-T5

M-15	Delivery and service access No verified delivery route exists for piano, glass, millwork or sectional.
METHOD	Measure the route from loading point to room, including doors, turns, stairs, elevator, thresholds and staging area.
RECORD	Route plan with minimum dimensions and item-specific handling notes.
UNLOCKS	P2-T1 · P2-T5 · P2-T6

Candidate products + manufacturer sources

SELECTION STATUS

These are research-backed candidates or owned-equipment checks. A manufacturer link is evidence for the listed facts; it is not purchase authorization or a released project-specific assembly.

YAMAHA-NU1X	Yamaha AvantGrand NU1X owned-check · checked 2026-09-26
SOURCE	https://usa.yamaha.com/products/musical_instruments/pianos/avantgrand/nu1x/specs.html
DIMENSIONS	W 59.125 in · D 18.25 in · H 40.3125 in
VERIFIED	✓ Yamaha lists the NU1X at 59-1/8 inches wide, 18-1/4 inches deep, and 40-5/16 inches high. ✓ Yamaha lists the weight as 240 pounds 11 ounces. ✓ Yamaha's regional NU1X specification page marks this exact model discontinued; the U.S. site retains its legacy specification and support page.
RELEASE	Measure the owned NU1X at its widest, tallest, and deepest points and confirm bench, power, service, and circulation clearances before bar millwork or final floor marking.

KORG-GRAND STAGE-X	Korg Grandstage X owned-check · checked 2026-09-26
SOURCE	https://www.korg.com/us/products/synthesizers/grandstage_x/
DIMENSIONS	W 53.98 in · D 18.15 in · H 6.61 in
VERIFIED	✓ Korg's owner manual lists the instrument at 53.98 inches wide, 18.15 inches deep, and 6.61 inches high, excluding the music stand. ✓ The listed weight is 55.12 pounds. ✓ The listed power consumption is 20 watts.
RELEASE	Measure the selected stand, bench, music rest, pedals, and rear cable bend in the room; then confirm door, HVAC, and playing clearances at the southeast position.

STRING-SWING -CC01K	String Swing CC01K Hardwood Home & Studio Guitar Keeper candidate · checked 2026-09-26
SOURCE	https://www.stringswing.com/guitar-hanger-hardwood-wall-mount-for-acoustic-and-electric-guitars/
VERIFIED	✓ The pivoting yoke is padded and is rated by String Swing for instruments up to 15 pounds. ✓ The hardwood block is offered in Cherry, Oak, Ash, and Black Walnut. ✓ String Swing directs wider classical-guitar and bass necks to its original CC01 yoke rather than assuming CC01K fits every instrument.
RELEASE	Inventory every instrument's weight, neck width, headstock geometry, and finish; assign CC01K or CC01 per instrument; mock up both rows; and have the installer fasten into verified structural backing.

ZEPHYR-PRES RV-PRB15C01CG	Zephyr Presrv PRB15C01CG 15-inch Beverage Cooler candidate · checked 2026-09-26
SOURCE	https://docs.zephyronline.com/docs/specs/Presrv_PRB15C01CG_spec.pdf
DIMENSIONS	W 15 in · D 23.375 in · H min 33.875 in · H max 34.875 in · cutout W min 15.125 in · cutout H min 34 in · rear min 1 in · wall-side min 2.25 in
VERIFIED	✓ The unit is front-venting and may be built in when its front air vent remains unobstructed. ✓ Zephyr lists overall dimensions of 15 inches wide, 23-3/8 inches deep, and 33-7/8 to 34-7/8 inches high. ✓ The installation manual requires a cabinet opening at least 15-1/8 inches wide and 34 inches high.
RELEASE	Cabinet shop must issue a coordinated shop drawing that preserves the front vent, 15-1/8-inch minimum opening, 34-inch minimum height, 1-inch rear plug clearance, door swing, outlet location, and pull-out service access.

DIODE-LED-BL AZE-100-SYST EM	Diode LED BLAZE 100 2700K Tape + S1 Black Channel + OMNIDRIVE Basics 96W Driver candidate · checked 2026-09-26
SOURCE	https://www.dioeled.com/blaze.html
DIMENSIONS	tape W 0.31 in · channel L 96 in · channel W 0.67 in · channel H 0.31 in
VERIFIED	✓ BLAZE 100 part DI-24V-BLBSC1-27-016 is 24-volt, 2700K, 90+ CRI tape rated at 113 lumens and 1.46 watts per foot. ✓ The manufacturer specifies a 55-foot maximum run and 1.96-inch cut points for this tape. ✓ The recommended S1 black channel is DI-CHB-S1-96B, supplied in 96-inch lengths with a classic frosted lens.
RELEASE	Lighting designer and electrician must produce a zone, feed, channel-joint, driver-load, driver-access, and dimmer schedule. Keep every feed at or below 55 feet and every driver at or below 96 watts, confirm a neutral at each PD-5NE, and bench-test the exact tape-driver-dimmer load for low-end stability and flicker before release.

NORA-NM4-RD C27BB	Nora Lighting NM4-RDC27BB 4-inch Round Deep Cone Reflector candidate · checked 2026-09-26
SOURCE	https://noralighting.com/product/nm4-rdc/
DIMENSIONS	cutout Ø 3.5 in · trim Ø 4.5 in · H 4.875 in
VERIFIED	✓ Part NM4-RDC27BB is the 2700K matte-black configuration. ✓ Nora lists 90+ CRI, 1027 delivered lumens, 15 watts, a 37-degree narrow-flood beam, and Triac or ELV dimming to 10 percent. ✓ The listed ceiling cutout is 3.5 inches; the trim is 4.5 inches wide and the module is 4.875 inches high.
RELEASE	Approve a reflected-ceiling and photometric plan, verify the actual ceiling cavity and insulation condition, obtain the exact dimmer/load compatibility result, and mock up 2700K output against the black ceiling before ordering.

WOODUPP-AK UPANEL-1029	WoodUpp Akupanel Colored Black Wrapped on Black Felt, item 1029 candidate · checked 2026-09-26
SOURCE	https://woodupp.com/products/akupanel
DIMENSIONS	W 23.62 in · H 94.49 in · thk 0.866 in · slat width 1.063 in · slat depth 0.512 in · gap 0.512 in
VERIFIED	✓ Item 1029 is a black-wrapped slat on black felt panel measuring 94.49 by 23.62 inches and 0.866 inch thick. ✓ The construction uses 0.354-inch felt, 0.512-inch-deep by 1.063-inch-wide slats, and 0.512-inch gaps. ✓ WoodUpp claims acoustic absorption Class A only when installed with 45 mm battens and insulation between them.
RELEASE	Order a finish sample and have the architect, acoustician, and installer approve the exact wall build-up, cavity insulation, substrate, fastener pattern, fire-test documentation, and interfaces with instrument backing and fabric-track areas.

FABRITRAK-G EOTRAK-BLAC K	FabriTRAK GeoTRAK Black Fabric-Retention Profiles candidate · checked 2026-09-26
SOURCE	https://www.fabritrak.com/products/geotrak
DIMENSIONS	profile depth options 0.5/1/1.375 in
VERIFIED	✓ GeoTRAK is a PVC-free black fabric-retention framework with fabric-receiving jaws. ✓ FabriTRAK lists 1/2-inch, 1-inch, and 1-3/8-inch profile depths. ✓ The system is site-installed by FabriTRAK dealers and professional installers and may be paired with acoustic core and finish fabric.
RELEASE	A qualified dealer must submit the exact track, core, fabric, substrate, perimeter, outlet, door, HVAC, slat-junction, and service-removal details and the test documentation for the complete proposed assembly.

KARNDGAN-VA N-GOGH-EBON Y-SCB89	Karndean Van Gogh Rigid Core Ebony SCB89 candidate · checked 2026-09-26
SOURCE	https://www.karndean.com/en-us/floors/products/ebony-scb89
DIMENSIONS	plank L 48 in · plank W 7 in · thk 0.177 in
VERIFIED	✓ Ebony SCB89 is a black and charcoal-gray rigid-core plank measuring 48 by 7 inches. ✓ Karndean lists a 20 mil wear layer, 4.5 mm total thickness, and 23.64 square feet per carton. ✓ Karndean's U.S. rigid-core installation guide says laminate and any floating floor must be removed before installation.
RELEASE	Identify whether the existing oak LVP is floating or adhered, inspect the underlying substrate, verify flatness and moisture conditions, order a room sample, and obtain the installer's written warranty for the exact floor assembly before release.

OMEGA-ANTIQU UE-MIRROR-SAM PLES	Omega Antique Mirror Dark Cloud, Smoky Quartz, and Gold Vein Overlay Samples candidate · checked 2026-09-26
SOURCE	https://omegamirrorproducts.com/products/antique-mirrors/
VERIFIED	✓ Omega presents Dark Cloud Antique, Smoky Quartz Mirror, and Gold Vein Overlay Mirror as distinct decorative patterns. ✓ The products are handcrafted and pattern variation is expected. ✓ Omega offers physical samples for evaluation before fabrication.
RELEASE	Order physical samples and build a full-size visual mockup. A local mirror fabricator and structural engineer must design the final panel sizes, edge treatment, safety backing or lamination, substrate, mechanical retention, access, and every overhead attachment before any wall-arch or ceiling release.

GUILFORD-FR7 01-2100-408	Guilford of Maine FR701, style 2100, color 408 Black candidate · checked 2026-09-26
SOURCE	https://www.guilfordofmaine.com/swatches/2100-408
DIMENSIONS	usable W 66 in
VERIFIED	✓ Color 408 is the black option in style 2100 FR701. ✓ The fabric is 100 percent post-consumer recycled polyester with a 66-inch usable width and no backing or added finish. ✓ Duvaltex reports 95 percent acoustic transparency for the fabric before anechoic termination.
RELEASE	Order a current fabric card and production sample, approve the dye lot and visual texture under the room lighting, verify stretch and retention with the selected track, and test or document the exact track-core-fabric assembly required for the project.

LOCAL SOURCE FILES	Canonical schedule · guide.json Execution sequence · research/build-content.json Product evidence · research/products.json
--------------------	--
