

Rehearsal room build guide

Materials · installation instructions · drawings · trade coordination



37 SCOPE ITEMS	7 WORK PHASES	44 FIELD CHECKS	16 SURVEY BUNDLES
-------------------	------------------	--------------------	----------------------

ISSUE STATUS

Coordination + quotation / field release required. Proposed dimensions, products and assemblies remain held where the stated gate calls for survey, sample, shop drawing, engineering, official review or Greg's decision.

Digital checkmarks record task progress. They never release engineering, permit, order, fabrication or installation holds automatically.

Authority + certainty

WORKING AUTHORITY	The dated guide JSON is the coordination schedule. The approved concept governs visual direction. Manufacturer research supports candidate selection. Field records, reviewed shop drawings, engineered assemblies and official decisions govern release where the schedule says they do.
-------------------	---

LOCKED INTENT	Approved room direction or count; dimensional fit may still require field confirmation.
VERIFIED PRODUCT	Manufacturer data checked on the listed date; installed fit and project-specific assembly remain gated.
FIELD VERIFY	Trace, measure, photograph and record the existing condition before downstream work.
HOLD	Do not order, fabricate, demolish or install until the named release evidence exists.

Current record basis

PRINTED CONTROLS	High confidence in the records: north 146.25 in · west 259.50 in · maximum width 188.00 in · published area 298.75 sq ft
WORKING POLYGON	8-point planner trace · calculated 299.738 sq ft · east-bay segment positions remain estimated and require a site laser
ENTRY DR-3	South boundary at x 0.99..37.31 in · west-jamb hinge · swings north into the main room · moderate-confidence plan registration; current condition and head unverified
BOOTH + CLOSET	Printed nominal booth 123 × 95 in and closet 34 × 46 in are high-confidence record dimensions; traced curve, sliders and openings still require field survey
CEILING PLANE	102 in working height · low confidence · no original room record states this dimension · field laser required
ORIGIN	Northwest finished-floor corner; X east, Z south. Dimensions in inches.

CHANGE CONTROL	Any as-built departure updates every affected plan, elevation, quantity, product fit, service route and trade review before release. A 2% survey discrepancy is an escalation trigger, not permission to fabricate within a 2% tolerance.
----------------	---

Authority sources

Approved room concept, September 13	assets/approved-concept.png
Original-record dimension audit v1.2	research/room-dimensions-records-v1.2.md
Canonical room record v1.0.0	room-records.json
Magicplan floor-plan record	assets/records/magicplan-floor-plan.pdf
2024 labeled floor-plan record	assets/records/labeled-floor-plan-2024.pdf
Claude brief, copied September 26	evidence/current-brief.md
Initial corrected schedule snapshot, 70 records	evidence/claude-elements-snapshot.json
Reviewed schedule at source commit 1a1d56d	evidence/claude-elements-reviewed.json
Source refresh and adopted corrections	evidence/source-refresh.md
2024 rehearsal plan detail	assets/records/rehearsal-plan-detail.png
Tape polygon source	evidence/room-polygon-source.json
Build-guide PDF packet v1.0	exports/rehearsal-room-build-guide-v1.0.pdf
Owned equipment inventory	evidence/gear-inventory.csv
Existing room photograph	assets/current-room.jpeg
Existing booth walkthrough frame	assets/booth-existing.jpg
Santa Monica permit application types	https://www.santamonica.gov/building-permit-application-types
Walker mirror installation guidance	https://www.walkerglass.com/blog/seven-deadly-sins-of-mirror-installation/

Open coordination conflicts

RESOLVE BEFORE RELEASE

Each conflict names the evidence, downstream consequence and resolution path. Keep the associated order, demolition, fabrication or installation hold in place until the stated status is closed in the dated coordination set.

C-01 · Door and booth geometry has superseded versions		Corrected in the active guide; field proof remains open. Derived west-wall-door files are superseded geometry and provenance only.
EVIDENCE	Derived brief and Pass 7 files place D-3 on the west wall, but the primary 2024 plan vectors place the entry on the south boundary at its west end. After registration to the Magicplan controls, its jambs are x 0.99..37.31 at z 259.50, with a west-jamb hinge and northward swing. The same original record supports a 29.04 inch vestibule, two parallel 70.6 inch slider layers and a nominal 123 by 95 inch booth body.	
CONSEQUENCE	Wrong walls, openings, circulation and booth dimensions could be issued or fabricated.	
RESOLVE	Use the original-record registration for current planning, field-survey D-2, D-3, vestibule, sliders and booth, then revise every affected plan before fabrication.	
C-02 · TV and instrument fit is not field-proven		Open; do not promise ten instruments or preselect hanger centers.
EVIDENCE	The v1.5 direction places the selected TV between the right-wall guitars/basses. Ten instrument positions are shown only as an illustrative modeled arrangement, while the source list identifies six owned instruments without recording their actual bodies, yokes or removal arcs.	
CONSEQUENCE	Backing, hangers, TV mount and device locations could be installed for a layout that cannot be serviced safely.	
RESOLVE	Build the M-13 full-size template from the selected TV and physically present instruments, then release only the instrument count that fits.	
C-03 · PMC model and cabinet envelope conflict		Open.
EVIDENCE	Brief and inventory say PMC IB1 at 15.8 by 19.7 inches; current elements say PMC IB1S at 11 by 17.7 inches.	
CONSEQUENCE	Speaker stands, toe-in, desk spacing and service access can be wrong.	
RESOLVE	Read model plates and measure the installed pair and stands before fixing the bay elevation.	
C-04 · NU1X identity and source dimensions are wrong		Open; NU1X remains the approved design intent.
EVIDENCE	Yamaha lists the NU1X at 59.125 W by 18.25 D by 40.3125 H inches; the brief and Pass 7 source use 57.5 inches wide, and inventory lists a Clavinova rather than an NU1X.	
CONSEQUENCE	Using the wrong piano body or the obsolete z32.5625 pose changes the current x9.5/z90 piano proposal, the x13/z160 bar proposal, their modeled 16.4375-inch body gap, bench envelope, delivery and circulation checks.	
RESOLVE	Confirm the physical instrument, then field-test the current proposal: 59.125 by 18.25 inch body centered x9.5/z90 at 270 degrees, bar centered x13/z160 at 270 degrees, and 16.4375 inches between modeled bodies before bar or floor-layout release.	
C-05 · Booth drum identity is unresolved		Open; 72 by 66 inches is a planning envelope only.
EVIDENCE	Photos are described as Yamaha; inventory records a Gretsch Catalina; current elements combine Yamaha naming with Gretsch inventory details.	
CONSEQUENCE	Kit footprint, setup, mic positions and asset handling may be assigned to the wrong kit.	
RESOLVE	Photograph badges and shells, inventory the complete setup and measure its deployed envelope.	

C-06 · Main-room fabric and plaster directions conflict		Open; existing fabric is retained until the finish decision is released.
EVIDENCE	Old v0.1 retains the existing grey acoustic fabric; current elements remove it and apply charcoal plaster; performance is unmeasured.	
CONSEQUENCE	Finish work could remove paid acoustic treatment without a replacement plan.	
RESOLVE	Inspect the wall build-up, measure the room, mock up both controlled finish options and record Greg's decision.	
C-07 · Lighting intent exceeds verified ceiling and controls		Open.
EVIDENCE	The brief calls for cove, recessed cans and track; requirements call for DMX-addressable control; current elements name Caseta Pro; plenum and circuits are unknown.	
CONSEQUENCE	Fixture type, control protocol, cutouts, drivers and permit scope can change.	
RESOLVE	Survey ceiling and circuits, then issue a coordinated fixture/control schedule and reflected ceiling plan.	
C-08 · Overhead mirror has no issued attachment design		Hold fabrication and overhead installation.
EVIDENCE	Current elements show a 96 by 96 inch mirror on plywood under a 102-inch ceiling; weight, glass makeup and structure are unverified.	
CONSEQUENCE	Fabrication or installation could proceed without a safe supported assembly.	
RESOLVE	Glazier and qualified design professional issue glass, backing, load and attachment details after ceiling inspection.	
C-09 · Published model, notes and old build sheet are stale		Open until the field-verified set is issued.
EVIDENCE	An older 59-element published artifact, old notes and the v0.1 sheet describe obsolete scope. The initial 70-element snapshot and frozen Pass 7 commit 1a1d56d remain historical proposal evidence: Pass 7 removes the unsupported booth floor lamp, records the booth rug as a provisional 66 by 88 inches and corrects the piano/bar order, but its west-wall D-3 claim is superseded by the primary 2024 plan vectors.	
CONSEQUENCE	Crews can quote, order or build obsolete scope.	
RESOLVE	Issue one dated coordination set and mark stale files reference-only; do not reuse old totals or durations as current facts.	
C-10 · Grandstage X body is larger than the working model		Open; keep the instrument at sitting height and always in audio.
EVIDENCE	Korg lists 53.98 W by 18.15 D inches excluding the stand; current elements use 53 W by 14.6 D inches for the staged rig.	
CONSEQUENCE	Bench, D-2 swing, HVAC and playing clearances can fail after the stand, pedals and rear cable bend are added.	
RESOLVE	Measure the selected stand and full playing envelope, then re-run the southeast full-size fit check.	
C-11 · The candidate refrigerator does not fit the source bar depth		Hold bar and refrigerator orders.
EVIDENCE	Zephyr lists a 23.375-inch body plus 1 inch rear plug clearance. The Pass 7 source bar is 24 inches deep, still 0.375 inch short before finish tolerance.	
CONSEQUENCE	The unit, outlet, vent or door can project into the stool and sofa zone or make service impossible.	
RESOLVE	Test a proposed 26-inch bar allowance full size and require a coordinated shop drawing; Greg approves the final depth and adjacent layout.	


C-12 · Candidate dark flooring cannot overlay a floating floor		Hold dark-floor order and demolition.
EVIDENCE	Karndean's SCB89 installation guide requires floating flooring to be removed; the existing oak LVP installation is unknown.	
CONSEQUENCE	The recoverable overlay concept may void the floor warranty or force removal of existing oak.	
RESOLVE	Identify the existing assembly. Keep oak plus rugs as an explicit option; any oak removal and dark-floor scope requires Greg's written approval and a preservation plan where feasible.	
C-13 · Candidate slat panels do not cover the 102-inch wall		Hold panel quantity and cut plan.
EVIDENCE	WoodUpp item 1029 is 94.49 inches high; the room plane is 102 inches before field verification.	
CONSEQUENCE	A 7.51-inch joint, trim or custom extension affects the guitar elevation, cove and backing.	
RESOLVE	Show the exact termination in the elevation and shop drawing; coordinate it with the M-13 TV-and-instrument field-fit layout.	
C-14 · Current furniture layout still needs occupied field proof		Open; current geometry is a coordinated proposal pending occupied field proof.
EVIDENCE	The v1.5 plan uses a conservative 90.5 by 36 inch Alpine envelope and two smaller DYVLINGE chairs at the current issued poses. The sofa's official graphic says 90.5 inches while its text specification says 90 inches. Body footprints are coordinated, but occupied swivel, recline, approach, door, platform and service clearances are not field measurements.	
CONSEQUENCE	Furniture may fit as drawn yet obstruct a door, raised platform, appliance service path, instrument removal path or comfortable occupied circulation.	
RESOLVE	Run M-12 and M-16 together at full size with every seat occupied and swiveled, refrigerator and doors operated, service zones marked and access walked; route any changed pose through the current layout record before order or installation.	

A01 · Room plan + fit envelopes

Coordination drawing · dimensions and release notes shown on sheet · field verification controls

A01 / CURRENT ROOM + DOOR PLAN

Current rotated furniture footprints; field boundaries, occupied envelopes and raised platforms remain holds.

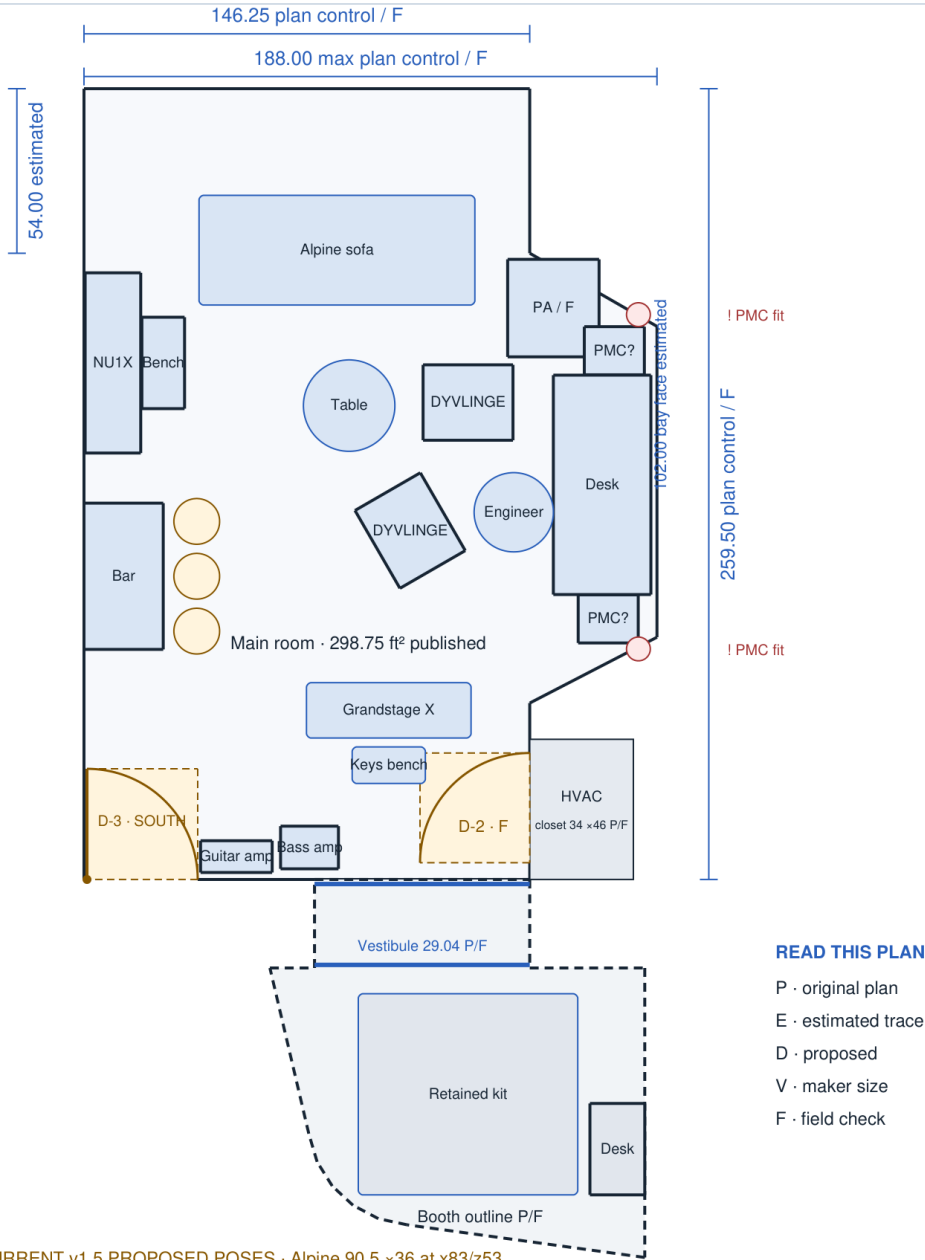


CURRENT v1.5 PROPOSED POSES · Alpine 90.5 × 36 at x83/z53.
NU1X x9.5/z90/270°; bar x13/z160/270°; modeled body gap 16.4375 in.
DYVLINGE chairs x126/z103/90° and x107/z145/150°.
All locations remain proposed until M-12; M-16 surveys both raised platforms.

A02 · Mirror wall elevation

Coordination drawing · dimensions and release notes shown on sheet · field verification controls

A02 / NORTH MIRROR ELEVATION

Current illustrative custom geometry; north-wall record is exact, arch dimensions remain proposed.

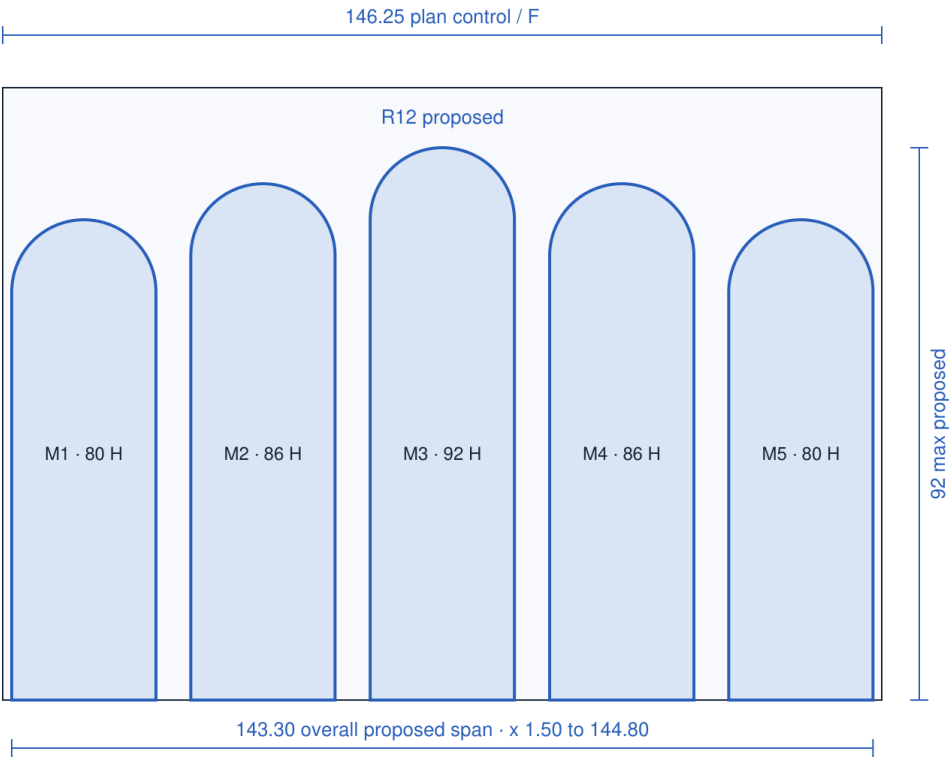

MIR-01 · FIVE GRADUATED PROPOSED ARCHES

Centers x 13.5 / 43.3 / 73.14 / 103.0 / 132.8; each 24 W.

Heights 80 / 86 / 92 / 86 / 80; clear gaps 5.80 / 5.84 / 5.86 / 5.80.

These illustrate design intent. Field templates and glazier cut sizes control fabrication.

LGT-02 · LIGHT THE SIDES + ARCH HEAD

76.3746 ft net = $\sum [2 \times (H - 12) + \pi \times 12] / 12$; no bottom edges.

Do not order curved channel from this elevation; supplier details each bend and cut.

Backing, glass assembly, mechanical retention and access remain trade-designed.

A03 · Bar + piano elevation


Coordination drawing · dimensions and release notes shown on sheet · field verification controls

A03 / WEST BAR + PIANO ELEVATION

Current proposed coordinates and maker bodies; field layout and millwork shop drawings control.

SOUTH / VIEWER LEFT

NORTH / VIEWER RIGHT

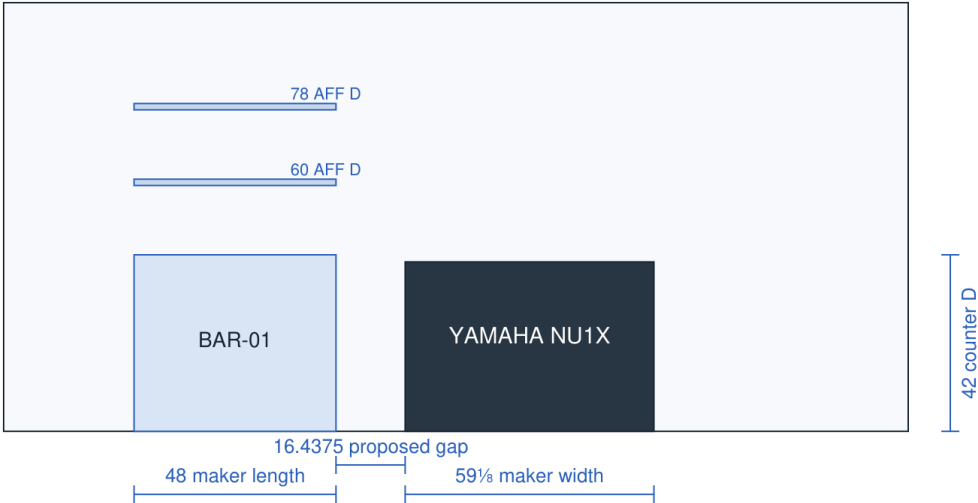

FRIDGE COORDINATION · BAR-05

Zephyr PRB15C01CG: 15 W × 23 3/8 D × 33 3/8–34 7/8 H in.

Minimum opening 15 1/8 W × 34 H in; allow 1 in behind for plug.

Proposed 26 in cabinet depth still needs a shop drawing and occupied fit test.

Model centers: NU1X x9.5/z90/270° · bar x13/z160/270° · 16.4375 in body gap.

THREE STOOLS REMAIN A DESIGN HOLD

48 in / 3 = 16 in of bar run per seat. Source stools sit 18 in apart.

Mock up three occupied stools, fridge open, and piano bench in use.

COUNTER + FLOOR SEQUENCE

Set the finished-floor datum → install carcass → template stone → fit appliances.


No sink or water service is included. Front vent and pull-out access stay clear.

A04 · Guitar wall elevation

Coordination drawing · dimensions and release notes shown on sheet · field verification controls

A04 / TV + INSTRUMENT ELEVATION

Actual TV body size with proposed bay pose; instrument and mount clearances remain a field-fit hold.

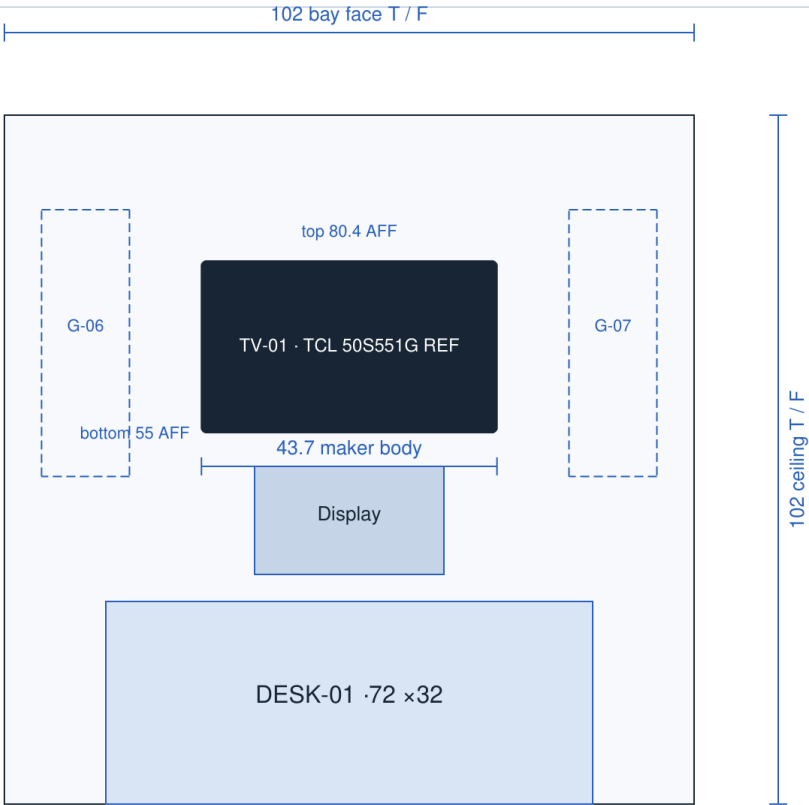

PROPOSED TV + INSTRUMENT ELEVATION

TCL reference body: 43.7 W x 25.4 H x 2.8 D; 19.6 lb; VESA 300 x 300.

Modeled TV center: x184.81 / z129 / 67.7 AFF; face x183.41.

G-06 and G-07 body envelopes each clear the TV laterally by 10.65 in.

FIELD-FIT HOLD · M-13

TCL availability, mount gap, connector/service path and backing remain unverified.

Template actual instrument bodies, headstocks, yokes and removal arcs across bay and returns.


Install only the field-approved count after Greg approves the full-size TV/instrument elevation.

E01 · Lighting + power coordination

Coordination drawing · dimensions and release notes shown on sheet · field verification controls

E01 / REFLECTED CEILING COORDINATION

Six proposed main-room fixtures plus two booth fixtures; exact recess and driver clearance unverified.

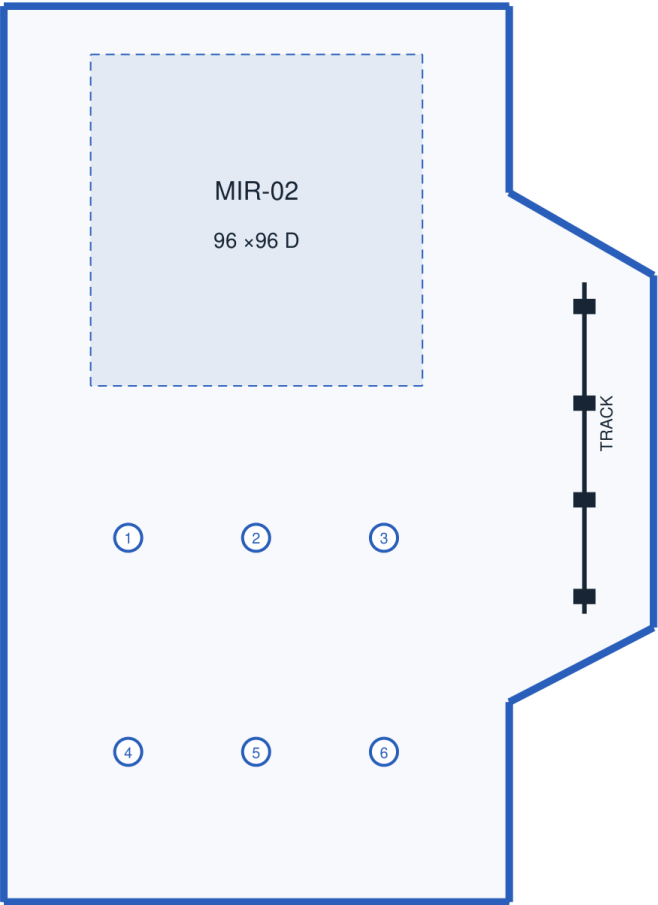

PROPOSED MAIN-ROOM POINTS (X,Z) · ALL INCHES

1(36,154) 2(73,154) 3(110,154)

4(36,216) 5(73,216) 6(110,216)

BOO-03 separately carries two proposed booth downlights.

6 × 15 W Nora candidate = 90 W connected main-room downlight load.

This is not a circuit design or a photometric prediction. Keep access to every driver.


Coordinate the proposed 96 x96 inset, structure, HVAC and safety devices before drilling.

A05 · Booth plan

Coordination drawing · dimensions and release notes shown on sheet · field verification controls

A05 / BOOTH + VESTIBULE PLAN

Original plan: 123 × 95 body, 29.04 vestibule, two 70.6 slider layers; field survey required.

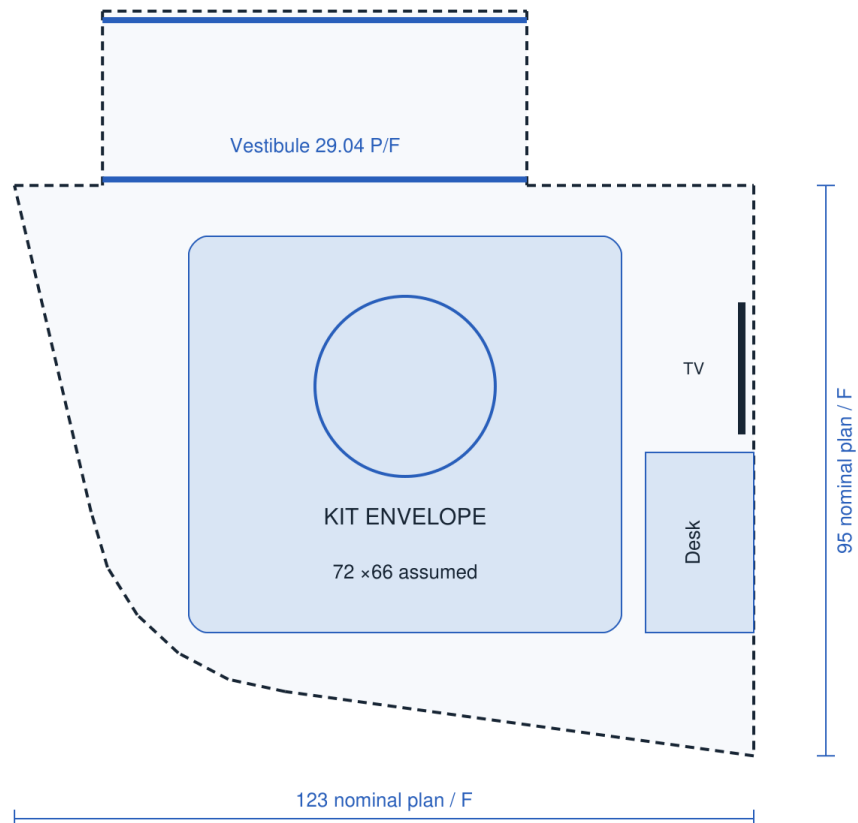

BOO-01 / BOO-02 / BOO-03

Retain the drum/vocal booth; verify Yamaha vs Gretsch identity in person.

Survey both slider layers and the curved/sloping wall before surface takeoffs.

Test kit access, mic boom sweep, desk use and cable routes together.

Absorber/cloud quantities are provisional; ceiling supports require a trade detail.

Do not cover door tracks, supply/return paths, access panels or the camera view.


D01 · Assembly details + release holds

Coordination drawing · dimensions and release notes shown on sheet · field verification controls

D01 / COORDINATION DETAILS


Show what adjacent trades need from one another before they close the wall or ceiling.

D1 · SERVICEABLE MIRROR LIGHT EDGE

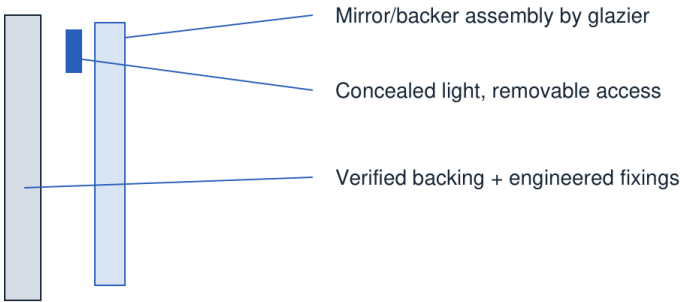

Coordination section; no anchor sizes or load capacity implied.

D2 · FRIDGE + COUNTER SECTION

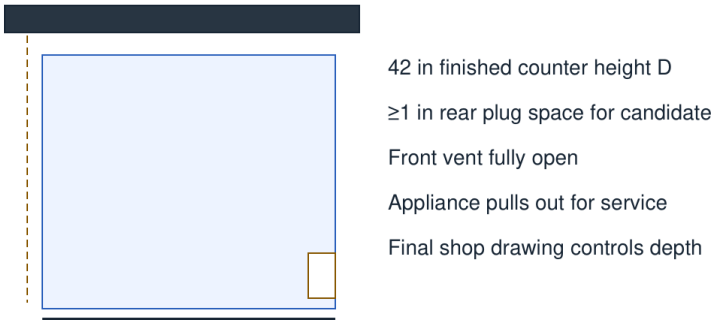

No sink/plumbing scope; stone templated after base installation.

D3 · CEILING MIRROR HOLD POINT

Approve panel modules, weight, support structure, retention and accessible lighting as one overhead assembly. Site verification + support designer + glazier release it. The render and this guide supply appearance and coordination, not engineering.

Build scope + release gates

USE	Quote each line with its stated quantity basis. A quote, digital completion mark or approved sample does not override a field, shop-drawing, engineering, official-review or Greg-decision hold.
-----	--

Prepare

PRE-01 · Field survey + full-size room mockup		1 visit Lead builder	Arrange now
SPEC	Laser + tape survey; photograph all eight corners, door swings, booth vestibule, both raised platforms, ceiling, services, and existing gear. Tape full furniture and occupied-seat envelopes on the floor.		
RELEASE GATE	Record M-01 through M-16; Greg approves the occupied mockup before custom work.		
SOURCE	Basis · Current brief + new coordination scope Sheet · A01		

PRE-02 · Trade drawings + approval review		1 package Lead builder	Quote now
SPEC	Coordinated millwork, glazing/support, lighting/power, floor-transition and acoustic details. Confirm landlord and city review required for the selected scope.		
RELEASE GATE	Lead builder confirms review route and inspection points before strip-out.		
SOURCE	Basis · New coordination scope Sheet · A01		

PRE-03 · Protection, removals + disposal		1 scope Lead builder	Quote now
SPEC	Document and label retained gear; move to protected storage; protect corridor and sliders; isolate power for two main-room troffers and booth troffer. Retain doors, HVAC access and absorption pending review.		
RELEASE GATE	Safe isolation and staged room closure; no blind demolition of fabric or ceiling.		
SOURCE	Basis · Current brief + booth photos Sheet · A01		

Mirrors

MIR-01 · Five graduated antique-mirror arches		5 panels Glazier	Hold custom order
SPEC	Current illustration proposes five 24 in wide arches at 80 / 86 / 92 / 86 / 80 in high, each with a semicircular 12 in head radius. Proposed centers are x 13.5, 43.3, 73.14, 103.0 and 132.8 in, spanning x 1.5 to 144.8 in overall. These are custom-design coordinates, not room measurements or glass cut sizes. Black smoked antique appearance with gold veining; approve an illuminated sample and field-template every shape, gap, edge and support.		
RELEASE GATE	M-03 + M-12 + M-07; glazier confirms field templates, glass build-up, weight, retention, edge protection and compatible materials before fabrication.		
SOURCE	Basis · Current full-room illustration; all custom dimensions proposed Sheet · A02		
CANDIDATE	Candidate · Omega Antique Mirror Dark Cloud, Smoky Quartz, and Gold Vein Overlay Samples		

MIR-02 · Lit ceiling mirror inset		1 assembly Glazier + support designer	Hold custom order
SPEC	Proposed 96 × 96 in visual zone, surface-applied beneath the flat ceiling. Finish to match arches; removable service access. Panel modules, thickness, backing, anchors and total weight are by the support designer.		
RELEASE GATE	M-03 + M-07 + M-09 / M-10; approved overhead assembly and structural load path. Adhesive alone is not a released detail.		
SOURCE	Basis · Approved concept; structural assembly unknown Sheet · E01		
CANDIDATE	Candidate · Omega Antique Mirror Dark Cloud, Smoky Quartz, and Gold Vein Overlay Samples		

Bar + piano

BAR-01 · Compact bar carcass		1 assembly Millworker	Hold custom order
SPEC	48 in long × 26 in deep × 42 in finished counter height proposed at planning center x 13, z 160, rotation 270 degrees. The current model leaves 16.4375 in between the 48 in bar body and the 59.125 in NU1X body; this is a proposed location, not a taped fact. Black finish, serviceable fridge bay, clear front vent and accessible outlet. Zephyr candidate needs 23-3/8 in body depth + 1 in rear clearance; final field layout and shop drawing control.		
RELEASE GATE	M-12 / M-11; field-test the 16.4375 in modeled piano-to-bar gap, appliance cutout, open door, ventilation, cable/plug space and current occupied furniture mockup. Increase depth if the chosen fridge requires it.		
SOURCE	Basis · Current ReferenceLayout.affordable proposal; physical envelope and fit require M-12 Sheet · A03		

BAR-02 · Black stone counter + support		1 top Stone fabricator	Hold custom order
SPEC	48 × 26 in nominal top, honed black stone or approved quartz sample; eased edge. Finished counter top 42 in AFF. Template after carcass installation; fabricator details thickness, joints and supported overhangs.		
RELEASE GATE	Installed carcass surveyed; refrigerator and three-stool fit resolved.		
SOURCE	Basis · Current brief; nominal dimensions Sheet · A03		

BAR-03 · Smoked-glass bar front		1 set Glazier	Hold custom order
SPEC	Field-sized smoked-glass infill with brushed brass trim and warm diffused backlight. Keep refrigerator ventilation and service panel clear. Specify appropriate safety glazing and retention for this location.		
RELEASE GATE	Millwork shop drawing and lit glass sample approved.		
SOURCE	Basis · Approved concept Sheet · A03		

BAR-04 · Backlit bottle shelves		2 shelves Millworker	Hold custom order
SPEC	48 L × 10 D in nominal; proposed shelf tops 60 and 78 in AFF. Black finish; recessed diffused LED; hidden cable route and removable channel cover. Brackets/backing designed for bottles and glassware.		
RELEASE GATE	M-12 / M-11 + M-07; backing, shelf load and bottle-height mockup approved.		
SOURCE	Basis · Current element schedule; dimensions proposed Sheet · A03		

BAR-05 · Front-venting glass-door beverage fridge		1 unit Millworker + electrician	Select + verify fit
SPEC	Built-in-rated narrow glass-door model, black finish; blue interior light is visual intent. Size the cabinet from the selected installation manual, including door swing and ventilation.		
RELEASE GATE	Verify product cutout and depth before BAR-01 shop drawings; do not enclose a freestanding appliance.		
SOURCE	Basis · Current brief Sheet · A03		
CANDIDATE	Candidate · Zephyr Presrv PRB15C01CG 15-inch Beverage Cooler		

BAR-06 · Three black bar stools · fit study		3 stools Furniture	Hold fit decision
SPEC	Approx. 30 in seat height with foot rings for 42 in counter. Source placeholders are 15 in diameter at 18 in centers; allow actual occupied envelopes in the mockup.		
RELEASE GATE	M-12 / M-11. A 48 in bar provides only 16 in of run per person for three seats. Confirm a workable arrangement or obtain Greg's layout decision. Sourced 17 in-body candidate needs 53 in at current centers, exceeding the 48 in bar.		
SOURCE	Basis · Three stools fixed in brief; spacing unresolved Sheet · A03		
CANDIDATE	Candidate · JONATHAN Y Trinity 30-inch backless stool		

KEY-01 · Yamaha NU1X hybrid upright + bench		1 set Piano supplier	Verify ownership
SPEC	Yamaha NU1X polished ebony: manufacturer lists 59-1/8 W × 18-1/4 D × 40-5/16 H in. Current proposed pose is center x 9.5, z 90, rotation 270 degrees, north of the bar; its body spans z 60.4375 to 119.5625 in the model. The modeled 16.4375 in gap to the bar is proposed, not a taped fact. Confirm exact model and ownership; the brief understated width by 1-5/8 in. NU1XA is a separate substitution.		
RELEASE GATE	M-11 + M-12 + M-15; field-test proposed pose and gap, confirm model, bench/playing clearance, current occupied furniture fit and delivery route. Inventory does not establish NU1X ownership.		
SOURCE	Basis · Current ReferenceLayout.affordable proposal + Yamaha body dimensions; field fit remains open Sheet · A03		
CANDIDATE	Candidate · Yamaha AvantGrand NU1X		

Lounge

SEAT-01 · Jennifer Taylor Home Alpine 90-inch sofa · Ebony Black Boucle		1 sofa Furniture	Selected reference; direct listing showed \$1,252.99 and ready to ship in 5 business days
SPEC	Selected SKU 64190-3-MBB: use 90.5 W × 36 D × 27.5 H in for planning; the official dimension graphic says 90.5 W while the text specification says 90 W, so confirm with the manufacturer. Seat 70.5 W × 24 D × 17.5 H in; arm 27.5 H in. Ebony black boucle over an oak frame with wedge legs; gently rounded profile, not a true half-moon.		
RELEASE GATE	M-12 + M-15; tape the conservative 90.5 × 36 in body plus occupied clearance, confirm the complete delivery route and room entry, resolve the half-inch published-width discrepancy, verify current \$1,252.99 price and stated ready-to-ship timing before ordering, and inspect the exact black boucle sample/return terms.		
SOURCE	Basis · Jennifer Taylor Home direct product listing checked 2026-09-28 Sheet · A01		
CANDIDATE	Candidate · Exact selected product / Jennifer Taylor Home Alpine 90-inch Sofa, Ebony Black Boucle		

SEAT-02 · IKEA DYVLINGE swivel armchairs · Keling black		2 chairs Furniture	Selected reference; IKEA listing showed \$199 each (\$398 pair)
SPEC	Selected article 805.708.31: each 24.75 W × 29.5 D × 26.75 H in with 16.875 in seat height. Black Keling corduroy upholstery with a chrome-color five-star swivel base; not leather. Selected sofa plus chair pair totals \$1,650.99 before tax, \$4,939.01 less than the prior HAY chair pair alone.		
RELEASE GATE	M-12 + M-15; tape both bodies and full occupied swivel envelopes, approve the low seat height and route, then verify local stock, current \$199 each price, delivery and return terms before ordering.		
SOURCE	Basis · IKEA direct product listing checked 2026-09-28 Sheet · A01		
CANDIDATE	Candidate · Exact selected product / IKEA DYVLINGE Swivel Chair, Keling Black		

SEAT-03 · Smoked-glass cocktail table		1 table Furniture	Hold fit decision
SPEC	30 in diameter × 16 in high proposed. Black pedestal and smoked-glass top. Recheck actual sofa-to-table access in mockup.		
RELEASE GATE	M-12; tape the current table, sofa and occupied chair envelopes before release.		
SOURCE	Basis · Current model envelope Sheet · A01		
CANDIDATE	Candidate · By-Boo Bunga · size and appearance reference		

SEAT-04 · Dark patterned lounge rug + pad		1 set Flooring + furniture	Sample now
SPEC	120 × 108 in nominal custom size from source model; charcoal medallion/pattern and low pile. Select edge treatment and pad compatible with the chosen floor. Ruggable Sloane Black 8 × 10 ft is a standard-size candidate, 12 in narrower; its system includes the pad. The room image remains unchanged.		
RELEASE GATE	Final furniture footprint and clear circulation confirmed; do not cover thresholds or ventilation.		
SOURCE	Basis · Approved concept; custom size proposed Sheet · A01		
CANDIDATE	Candidate · Ruggable Sloane Black flatwoven rug + Standard Pad		

Finishes

FIN-01 · Dark main-room floor		328.63 sq ft allowance Flooring	Sample + quote
SPEC	Published 298.75 sq ft room area × 1.10 waste = 328.63 sq ft before carton rounding. Karndean Ebony SCB89 candidate: 14 cartons × 23.64 = 330.96 sq ft. Remove existing floating LVP for this product; preserve boards where feasible. Keep-oak + rug alternative requires Greg's finish decision.		
RELEASE GATE	M-01 + M-08; reconcile published area to the field survey, then approve moisture/flatness, underlayment, thresholds, door clearances and final installed buildup.		
SOURCE	Basis · Original Magicplan record + proposed 10% waste; field reconciliation required Sheet · A01		
CANDIDATE	Candidate · Karndean Van Gogh Rigid Core Ebony SCB89		

FIN-02 · Charcoal wall finish + acoustic retention		1 measured scope Finish contractor + acoustician	Sample + quote
SPEC	Remove the visual chair-rail division through a coordinated trim/fabric detail. Keep existing absorptive construction until assessed; re-cover in charcoal acoustically suitable fabric where retained. Plaster only approved solid surfaces.		
RELEASE GATE	M-07 + M-14; finish sample and acoustic scope approved. Gross wall area is only an estimating upper bound.		
SOURCE	Basis · Visual intent with proposed acoustic-preserving approach Sheet · A02		
CANDIDATE	Candidate · FabriTRAK GeoTRAK Black Fabric-Retention Profiles / Guilford of Maine FR701, style 2100, color 408 Black		

FIN-03 · Black slat panels at bay returns		66.08 sq ft net Finish carpenter	Sample + quote
SPEC	Two nominal returns: 47.23 and 46.06 in long × 102 in high. Black wood slats and black backing. Obtain tested assembly data; coordinate joints, hanger backing and service access. The 94.49 in WoodUpp candidate is 7.51 in short of 102 in; agree a joint or taller product before ordering.		
RELEASE GATE	M-01 / M-02 + M-03 + M-13 / M-11; panel size, fire-performance documentation and return angles approved.		
SOURCE	Basis · Derived return lengths; ceiling unverified Sheet · A04		
CANDIDATE	Candidate · WoodUpp Akupanel Colored Black Wrapped on Black Felt, item 1029		

FIN-04 · Ceiling, trim + exposed solid-surface paint		1 scope Painter	Quote now
SPEC	Matte black ceiling and cove fascia; compatible dark finish on approved solid walls and trim. Sample sheen under actual 2700K light. Keep paint off acoustic fabric, equipment and labels.		
RELEASE GATE	Patch/rough-in inspection complete; substrate prep and finish samples approved.		
SOURCE	Basis · Current visual brief Sheet · E01		

Studio + guitars

DESK-01 · Fixed production desk + 12U rack		1 set Millworker + AV	Survey + quote
SPEC	72 L × 32 D × 30 H in nominal desk along bay face; console secured, rack under north end, removable cable trays, clear knees and accessible service. Reuse suitable owned desk/rack if verified.		
RELEASE GATE	M-02 + M-11 + M-13; confirm bay dimensions, PMC identity, rack depth/heat, exact console, display and engineer-chair clearance.		
SOURCE	Basis · Current brief; product fit unverified Sheet · A04		

TV-01 · 50-inch TV + low-profile mount		1 display AV + carpenter	Current purchase candidate; wall fit held
SPEC	Manufacturer body without stand: 43.7 W × 25.4 H × 2.8 D in, 19.6 lb, VESA 300 × 300. Proposed right-wall pose centers the body at x 184.81, z 129 and 67.7 in AFF, with face x 183.41, bottom 55 and top 80.4 in AFF. Place between bay instruments G-06 and G-07. TCL 50Q651G is the available same-body-size candidate with a SANUS BLL2-B1 mount; the 50S551G remains the rendering reference.		
RELEASE GATE	M-02 + M-07 + M-11 + M-13. Verify purchased 50Q651G and BLL2-B1 manuals, wall structure, connectors, ventilation, glare, desk sightline and instrument-removal arcs. Nominal combined depth is 3.47 in before plug and service allowances.		
SOURCE	Basis · TCL manufacturer body data + evidence/right-wall-tv-layout-v1.4.md Sheet · A04		
CANDIDATE	Candidate · TCL 50Q651G 50-inch Q6 TV / SANUS Elite BLL2-B1 fixed TV mount / TCL 50S551G 50-inch S Class 4K TV		

GTR-01 · TV + guitar/bass mounting layout and structural backing		1 field-fit set Carpenter + AV	Hold field-fit decision
SPEC	Mount the selected TV between the right-wall instruments. Template the actual TV body, mount, connectors, instrument headstocks, bodies, yokes and removal arcs at full size before locating backing or drilling. Final hanger count follows the field-fit elevation.		
RELEASE GATE	M-02 + M-07 + M-11 + M-13. Greg approves the tested TV-and-instrument elevation before holes, backing heights or device locations are fixed.		
SOURCE	Basis · Current v1.5 direction; actual instruments and TV control fit Sheet · A04		
CANDIDATE	Candidate · String Swing CC01K Hardwood Home & Studio Guitar Keeper		

GTR-02 · Owned guitars and basses for TV wall		6 listed instruments Greg + AV	Inventory + field fit first
SPEC	Reconcile the listed one guitar and five basses against the instruments physically present. Record model, overall size, weight, finish, yoke position and removal arc for each; do not assume that every listed instrument fits with the TV.		
RELEASE GATE	M-11 inventory reconciled and M-13 field-fit elevation approved. Display only the count that safely fits with the selected TV.		
SOURCE	Basis · Current brief: 1 guitar + 5 basses Sheet · A04		

Light + power

LGT-01 · Perimeter cove tape + channel		71.76 linear ft net Lighting supplier + electrician	Sample + quote
SPEC	2700K, CRI 90+ minimum; continuous diffused warm line. 71.7553 ft is derived from the current room-record polygon, including estimated bay segments. Separate feed runs and accessible matched drivers; no unsupported continuous-run assumption.		
RELEASE GATE	M-01 + M-03 + M-09 / M-10; replace the estimate with the field perimeter, then approve sample dimming, voltage-drop/run-length design and feed locations.		
SOURCE	Basis · Derived current shell perimeter; bay segments remain estimated Sheet · E01		
CANDIDATE	Candidate · Diode LED BLAZE 100 2700K Tape + S1 Black Channel + OMNIDRIVE Basics 96W Driver		

LGT-02 · Arch backlight tape + channel		76.37 linear ft net Lighting supplier + glazier	Sample + quote
SPEC	Current illustrated arches are 24 W × 80 / 86 / 92 / 86 / 80 H in. Net 76.3746 ft lights two vertical sides plus each 12 in radius semicircular head and excludes all bottom edges. Conceal individual feeds and leave removable access.		
RELEASE GATE	Final field templates and supplier-approved bend, cut and channel detail; continuous curved light may require a different product from straight cove tape.		
SOURCE	Basis · Calculated from current proposed graduated arches Sheet · A02		

LGT-03 · Ceiling inset perimeter backlight		32 linear ft net Lighting supplier + glazier	Sample + quote
SPEC	Four sides of nominal 96 × 96 in ceiling inset; diffused 2700K line with source concealed from the seated view.		
RELEASE GATE	Mirror support, service access and lighting detail coordinated before fabrication.		
SOURCE	Basis · Calculated from proposed inset Sheet · E01		

LGT-04 · Shelf + counter accent tape		12 linear ft net Lighting supplier + millworker	Sample + quote
SPEC	Two 48 in shelves plus one 48 in counter accent = 12 ft net; diffused 2700K lighting. Keep tape heat and driver access away from stored bottles and fridge intake.		
RELEASE GATE	BAR-01 + BAR-04 shop drawings and compatible driver/channel selected.		
SOURCE	Basis · Calculated from proposed bar Sheet · A03		

LGT-05 · Main-room 4 in downlights		6 fixtures Electrician	Select + mock up
SPEC	Current illustration proposes six 2700K, CRI 90+ main-room downlights at x 36, 73 and 110 in on z 154 and 216 in, with black trim or a verified black-trim option. These proposed points avoid the 96 × 96 in ceiling mirror; confirm light distribution, fixture depth, driver space and ceiling ratings. BOO-03 separately carries two booth lights.		
RELEASE GATE	M-03 + M-09 / M-10; ceiling investigation, photometric review, fixture/dimmer test and lighting plan approved. Surface alternative requires visual approval if recessing cannot work.		
SOURCE	Basis · Current full-room illustration; six proposed main-room points Sheet · E01		
CANDIDATE	Candidate · Nora Lighting NM4-RDC27BB 4-inch Round Deep Cone Reflector		

LGT-06 · Guitar-wall track + four heads		1 set Electrician	Select + mock up
SPEC	Black track, four adjustable 2700K CRI90+ heads proposed; compatible track/feed family. Aim to avoid screen, mirror and seated-eye glare.		
RELEASE GATE	Guitar elevation + ceiling support + electrical control choice approved.		
SOURCE	Basis · Current model proposed count4 Sheet · E01		

LGT-07 · Lighting control + matched drivers		1 engineered package Electrician + AV	Quote after samples
SPEC	Independently controllable cove, downlights, mirror glow, bar/shelves, guitar track and booth. One user scene interface. Reconcile earlier DMX requirement with current dimmer-system brief before selecting protocol.		
RELEASE GATE	M-09 / M-10; signed load/run schedule, fixture/dimmer compatibility, service access and camera/low-level dim tests.		
SOURCE	Basis · Control conflict remains open Sheet · E01		
CANDIDATE	Candidate · Diode LED BLAZE 100 2700K Tape + S1 Black Channel + OMNIDRIVE Basics 96W Driver		

PWR-01 · Surveyed electrical + low-voltage work		1 scope Electrician + AV	Survey + quote
SPEC	Map panel/circuits and actual loads; plan AV, lights, fridge and general receptacles from survey. Label circuits. Separate Apollo/TV power arrangement per verified AV plan; diagnose hum before selecting remedies.		
RELEASE GATE	M-09 / M-10; licensed design and inspections as applicable. Never remove safety earth or treat a power strip as an isolation design.		
SOURCE	Basis · Current operational rules; no circuit schedule exists Sheet · E01		

Studio + guitars

AV-01 · Retained AV + plug-and-play commissioning		1 scope AV engineer	Quote now
SPEC	Retain verified PMC mains, HS8s, Turbosound PA/pole, interfaces, Trinnov, sub and member laptop station. PA stays north of the desk: verify actual base footprint, pole stability, aim and cable route; A01 uses the provisional 14 × 14 in source box. Korg always connected at seated height. Label R-01... at cable heads; print patch map; front Furman outlet free; Mac sleep disabled. Confirm both PMC envelopes inside the canted shell and the Korg bench clear of D-2; current plan flags these fit checks.		
RELEASE GATE	M-11 + M-14; cold-start, channel, hum, latency, monitor, PA coverage, booth and laptop tests pass; Trinnov/sub operating rule documented.		
SOURCE	Basis · Current brief + retained inventory Sheet · A01		
CANDIDATE	Candidate · Korg Grandstage X		

Booth

BOO-01 · Booth fabric/absorber work + cloud review		1 measured scope Acoustician + carpenter	Survey + quote
SPEC	Retain existing drum/vocal function and glass separation. Evaluate six nominal 24 × 48 × 2 in wall panels plus one 48 × 48 in cloud as a provisional treatment study; preserve existing absorption until measured.		
RELEASE GATE	M-05 + M-07 + M-14; approve actual coverage, response, fire-performance documentation, clearances and ceiling suspension.		
SOURCE	Basis · Current booth intent; quantities proposed Sheet · A05		

BOO-02 · Booth floor finish + retained rug		1 measured scope Flooring	Sample + quote
SPEC	Charcoal low-pile carpet tile or approved acoustic finish; keep existing Persian rug if serviceable. Trace curved wall and vestibule for takeoff; check slider tracks, thresholds and instrument access.		
RELEASE GATE	M-05 + M-08; selected flooring assembly approved for existing floor/substrate.		
SOURCE	Basis · Current booth element schedule Sheet · A05		

BOO-03 · Booth warm lights + service checks		2 downlights Electrician + HVAC + AV	Survey + quote
SPEC	Two proposed 4 in 2700K lights, separate control from lounge; retain working/task light in all scenes. Recheck HVAC airflow, noise, camera, TV, mic boom, rack and drum clearances.		
RELEASE GATE	M-03 + M-05 + M-09 / M-10 + M-06 / M-14; coordinate cloud, access and microphone positions.		
SOURCE	Basis · Current booth element schedule Sheet · A05		

Complete

CLOSE-01 · Styling, spare materials + handover		1 scope Lead builder + Greg	After commissioning
SPEC	Plant, restrained brass/black accessories and flameless candles. Keep labeled finish samples, spare flooring, LED product records, paint codes, as-built dimensions, patch/circuit maps and driver access photos.		
RELEASE GATE	Full punch list, operation test, cleaning and Greg's room walk-through complete.		
SOURCE	Basis · Approved visual intent + new handover scope Sheet · A01		

Materials + installation

USE EACH SCOPE CARD

Gather the listed materials, complete the prerequisites, follow the ordered steps and record acceptance. Field quantities, attachment designs and trade-specific releases remain open exactly where named.

PRE-01 · Field survey + full-size room mockup

Lead builder · service · Drawing A01

MATERIAL / COMPONENT	QUANTITY BASIS	SPECIFICATION + RELEASE
Field-survey record kit	1 set	Dimension log, marked A01 plan, scale targets, room/object labels and photo index. quote-ready
Full-size layout tape	1 allowance	Low-residue floor-safe tape in at least two colors for bodies and occupied/service envelopes. select after floor test
Temporary wall template film/paper	1 allowance	Removable material for TV, instruments, mirrors and mounting-zone templates. select after finish compatibility test

Tools + access

calibrated laser distance meter · steel tape · digital level · camera · tripod · moisture meter appropriate to floor · non-marring layout tape

Before starting

- [] Confirm access to main room, booth, closet, ceiling inspection point and electrical panels.
- [] Print current A01–A05/E01 and M-01...M-16 sheets; use one dated datum and revision.
- [] Test tape/labels on each retained finish.

Install in this order

1. Establish the main finished-floor datum and named wall control points.
2. Measure shell, openings, booth/sliders, ceiling, services, gear and both raised platforms exactly as M-01...M-16 require.
3. Photograph every measurement with scale and keyed location.
4. Tape every current furniture body plus occupied, swivel, door, appliance, service and instrument-removal envelopes.
5. Record discrepancies and stop downstream release where fit or fabrication changes.
6. Issue a signed field record and photo index.

Accept the work when

- [] Plan dimensions close and both diagonals reconcile.
- [] Every M-number has a measured value, method, photo and responsible person.
- [] Mockup can be walked with doors, sliders, chairs and fridge represented in operation.

Still required to release this work

- [] Field survey lead signs the dated record.
- [] Greg approves the occupied layout; this approval does not release unengineered attachments.

Manufacturer instructions + sources

[Current room plan](#)
[Build content measurement register](#)

PRE-02 · Trade drawings + approval review

Lead builder · service · Drawing A01

MATERIAL / COMPONENT	QUANTITY BASIS	SPECIFICATION + RELEASE
Field-verified coordination set	1 package	Plans, elevations, reflected ceiling plan, details, schedules and revision log. not issued
Submittal and release register	1 register	Tracks shop drawings, samples, product data, calculations, approvals and hold points by guide item ID. create
Permit/review record	1 record	Written determination of landlord, building-official and inspection requirements. obtain

Tools + access

PDF markup software · revision log · submittal register · coordination meeting record

Before starting

- ☐ PRE-01 field record is signed.
- ☐ Conflicts C-01...C-14 have owners and resolution paths.
- ☐ Each trade receives the same current revision.

Install in this order

1. Redraw A01–A05/E01 from the signed field record.
2. Add furniture/service zones, AFF mounting dimensions, circuits/control zones and field-verified backing.
3. Issue substrate-specific attachment details for mirrors, TV, hangers, track, panels and cloud.
4. Coordinate millwork, glazing, lighting, AV, floor, acoustic and HVAC interfaces.
5. Record permit/review direction and inspection points.
6. Publish a revision log and obtain named releases before quoting or ordering.

Accept the work when

- ☐ All drawings carry one revision/date and reconcile at shared dimensions.
- ☐ No custom cut size or attachment relies on a concept image.
- ☐ Every hold point has an owner, deliverable and release signature.

Still required to release this work

- ☐ Design professional issues the construction set.
- ☐ Licensed trades/design professionals supply calculations and code-specific details in their scope.

Manufacturer instructions + sources

[Guide scope schedule](#)

[Trade scopes and conflicts](#)

PRE-03 · Protection, removals + disposal

Lead builder · service · Drawing A01

MATERIAL / COMPONENT	QUANTITY BASIS	SPECIFICATION + RELEASE
Floor and path protection	1 measured allowance	Non-staining breathable protection selected for retained LVP and corridor; taped without finish damage. field-select
Dust containment	1 set	Poly barriers, zipper access, HEPA air control and vent protection compatible with occupied-building rules. trade-select
Asset labels and move log	1 set	Unique removable labels, photos, destination log and cable tags for all retained equipment. ready
Protected storage/crates	1 measured allowance	Padded, dry, secure storage sized after inventory. field-size
Disposal containers	1 allowance	Separated waste/recycling containers for only approved removals. quote

Tools + access

HEPA vacuum/air scrubber as required · lockout/tagout kit · moving blankets · carts · label printer · camera

Before starting

- [] Approve removal drawings and inventory destination.
- [] Licensed electrician identifies circuits before fixture work.
- [] Confirm sliders, camera, HVAC and egress stay operational or have approved outages.

Install in this order

1. Photograph and label every retained item and connection before disconnecting.
2. Move gear to protected storage and update the move log.
3. Install corridor, floor, slider, door, camera, grille and fabric protection.
4. Establish dust isolation without blocking supply/return or exits.
5. Lock out and verify affected lighting circuits.
6. Remove only issued-scope items; log salvage and disposal.
7. Inspect protection daily and repair breaches.

Accept the work when

- [] Retained items reconcile to the move log with no unrecorded damage.
- [] No blocked egress, HVAC path, slider track or camera view.
- [] Removed circuits are safe and identified.

Still required to release this work

- [] GC supplies site-specific containment and disposal plan.
- [] Electrician supplies outage/lockout record.

Manufacturer instructions + sources

[Protection/removal scope](#)
[Current room plan](#)

MIR-01 · Five graduated antique-mirror arches

Glazier · custom · Drawing A02

MATERIAL / COMPONENT	QUANTITY BASIS	SPECIFICATION + RELEASE
Graduated antique-mirror arch panels Product / instructions	5 custom panels	Illustrated 24-in widths and 80/86/92/86/80-in heights are template envelopes only; black-smoked antique appearance with approved gold-vein character. hold fabrication
Safety backing/lamination and edge finish	5 panel sets	Glass makeup and protected bottom/perimeter edges selected by glazier for the actual location. engineer/glazier to specify
Mechanical retention and verified backers	1 engineered set	Substrate-specific backers, retainers, clips/channels and compatible setting materials; loads and fasteners by issued design. not designed
Perimeter interface trim	1 measured set	Black or brass interface pieces coordinated with wall finish and removable halo access. sample/quote

Tools + access

laser/template material · glass handling suction equipment · setting blocks/shims · non-marring PPE · torque/fastener tools specified by glazier

Before starting

- [] Complete M-03, M-07 and finished-wall/floor survey.
- [] Approve a lit physical mirror sample and expected pattern variation.
- [] Receive signed panel schedule, weights, safety-glass build-up and attachment detail.

Install in this order

1. Field-template each unique arch, gap and edge from the finished datum.
2. Fabricator labels panels and dry-checks templates before cutting glass.
3. Install verified backers and inspect them before wall closure.
4. Complete wall finish and halo rough-in while keeping access removable.
5. Set panels on specified blocks/supports and engage engineered mechanical retention in labeled order.
6. Fit edge protection/trim and clean with manufacturer-compatible products.
7. Glazier performs and records final retention and edge inspection.

Accept the work when

- [] Installed profiles match approved templates and A02 visual order.
- [] No unsupported edge, sharp edge, unstable panel or trapped light-service component.
- [] Panel labels, weights, retention and inspection photos are in the handover file.

Still required to release this work

- [] Glazier issues exact cut files, glass makeup, weights, edge and setting requirements.
- [] Qualified designer issues backing, loads, mechanical retention and fasteners.

Manufacturer instructions + sources

[Mirror elevation](#)
[Omega antique mirror samples](#)
[Coordination details](#)

MIR-02 · Lit ceiling mirror inset

Glazier + support designer · custom · Drawing E01

MATERIAL / COMPONENT	QUANTITY BASIS	SPECIFICATION + RELEASE
Antique ceiling-mirror visual assembly Product / instructions	1 engineered assembly	96 x 96-in proposed visual zone; module sizes and joints determined after ceiling survey. hold fabrication
Support frame/backer	1 engineered set	Independent support/load path sized to structure; removable access coordinated with lighting. not designed
Mechanical retention and secondary safety provisions	1 engineered set	Supplier-designed hardware and fasteners for overhead use; adhesive is not the sole support. not designed
Perimeter trim/access panels	1 set	Finished black interface concealing light source while preserving driver and retainer inspection access. custom-detail

Tools + access

rated access equipment · glass lifting/handling system · layout laser · temporary engineered bracing · inspection camera

Before starting

- [] Open and document the approved ceiling inspection point.
- [] Obtain structural/support design, panel weights, glass safety build-up and installation/lift plan.
- [] Coordinate detectors, HVAC, downlights, cove, drivers and access before fabrication.

Install in this order

1. Survey structure and set out the assembly from the field-issued E01 datum.
2. Install and inspect the engineered support frame/backer before concealment.
3. Complete electrical/halo rough-in and verify removable service paths.
4. Stage, label and lift modules under the glazier's approved plan.
5. Engage every specified mechanical retainer and secondary provision; do not rely on adhesive alone.
6. Install trim/access panels without hiding inspection points.
7. Support designer and glazier complete final documented inspection.

Accept the work when

- [] Assembly is level, stable and matches approved module/joint layout.
- [] Every retainer and support is inspectable or documented before closure.
- [] Lighting and drivers can be serviced without removing unsupported glass.

Still required to release this work

- [] Qualified support designer supplies loads, framing, anchors, sequencing and inspection requirements.
- [] Glazier supplies module/cut schedule, weight, safety glass build-up and handling plan.

Manufacturer instructions + sources

[Reflected ceiling coordination](#)
[Coordination detail D3](#)
[Omega samples](#)

BAR-01 · Compact bar carcass

Millworker · custom · Drawing A03

MATERIAL / COMPONENT	QUANTITY BASIS	SPECIFICATION + RELEASE
Cabinet carcass and finished panels	1 assembly	48-in nominal run, proposed 26-in depth and 42-in finished counter height; cabinet-grade core, thickness and black finish set by approved shop drawing. quote-ready after survey
Serviceable door/panel hardware	1 set	Commercial hinges/slides, pulls or touch latches, removable fridge/service panels and stops; exact schedule pending design. select in submittal
Leveling/toe-kick components	1 set	Adjustable levelers/shims and finished toe kick compatible with floor decision. select in submittal
Ventilation grilles/openings	1 set	Keep candidate fridge front vent open and cabinet heat/service paths unobstructed. coordinate
Backing/anchors	1 engineered set	Substrate-specific restraint and blocking identified on shop drawings. field-dependent

Tools + access

track saw/table saw · cabinet clamps · laser/level · scribe tools · manufacturer-specified fastener tools

Before starting

- [] Complete M-11/M-12 and choose the refrigerator.
- [] Approve 24-in versus 26-in depth through occupied/fridge-service mockup.
- [] Coordinate finished floor, outlet, stone, glass front, shelves and lighting.

Install in this order

1. Field-measure the run and service clearances from A03 datums.
2. Submit shop drawings showing materials, panels, hardware, vent, outlet and removable-service route.
3. Prefabricate and finish components; dry-fit the selected appliance opening.
4. Set, level and restrain the carcass to verified backing.
5. Verify appliance can insert, vent, open and pull out for service.
6. Release the installed carcass for stone template, then install finished service panels.

Accept the work when

- [] Finished counter datum is correct and carcass is level/plumb.
- [] Fridge vent, plug, door and pull-out path remain fully usable.
- [] All service panels and hardware operate without colliding with stools or piano.

Still required to release this work

- [] Millworker supplies material/hardware schedule and substrate-specific anchor detail.
- [] Greg releases final bar depth and three-stool fit.

Manufacturer instructions + sources

[Bar and piano elevation](#)
[Fridge/counter detail](#)

BAR-02 · Black stone counter + support

Stone fabricator · custom · Drawing A03

MATERIAL / COMPONENT	QUANTITY BASIS	SPECIFICATION + RELEASE
Honed black stone or approved quartz top	1 custom top	Field-templated nominal 48 x 26-in top; exact material, thickness, slab/lot and eased edge selected by sample. unselected
Supports/brackets	1 engineered set	Continuous cabinet support plus any concealed brackets required by final thickness/overhang. fabricator to design
Compatible setting materials	1 set	Non-staining bedding/sealant approved by both surface and cabinet manufacturers. select with material

Tools + access

digital templating tools · stone handling equipment · level · seaming/setting tools specified by fabricator

Before starting

- ☐ Carcass is installed, level and accepted.
- ☐ Final fridge/stool geometry and overhang are released.
- ☐ Approve physical material sample, edge and seam plan.

Install in this order

1. Field-template the installed carcass and mark walls, appliance and finished edges.
2. Fabricator issues cut/edge/support drawing and confirms cabinet capacity.
3. Dry-check top and protect finished cabinet faces.
4. Install supports and set top with approved materials.
5. Complete seams/edge finish and cure per manufacturer.
6. Verify fridge ventilation/service and clean/protect the top.

Accept the work when

- ☐ Top is level, fully supported and matches approved edge/sample.
- ☐ No unsupported overhang, blocked vent or appliance-service conflict.
- ☐ Care/sealer instructions and material lot are recorded.

Still required to release this work

- ☐ Stone fabricator provides exact material, thickness, weight, joint and support requirements.

Manufacturer instructions + sources

[Bar elevation](#)

[Counter coordination detail](#)

BAR-03 · Smoked-glass bar front

Glazier · custom · Drawing A03

MATERIAL / COMPONENT	QUANTITY BASIS	SPECIFICATION + RELEASE
Smoked safety-glass infill	1 field-sized set	Tint/sample approved under 2700K light; glass type, thickness, edge and safety treatment by glazier. unselected
Brushed-brass trim/retention	1 measured set	Profile and finish sample coordinated with glass edges and cabinet service panel. unselected
Diffused backlight interface	1 set	Opaque/reflective backing and removable LED access coordinated with LGT-04. custom-detail
Compatible setting/seal materials	1 set	Non-staining materials approved for glass, metal and cabinet finish. glazier to specify

Tools + access

glass handling tools · laser/level · non-marring spacers · manufacturer-specified sealant tools

Before starting

- [] Bar carcass is installed and service openings accepted.
- [] Approve lit glass and brass samples.
- [] Receive glazier shop drawing with retention and edge details.

Install in this order

1. Field-template the finished opening and removable service boundaries.
2. Fabricate and label glass and trim from approved template.
3. Complete backlight rough-in and test before glass closes the cavity.
4. Install specified retainers/setting blocks and fit glass without loading edges.
5. Install trim while preserving the service panel and ventilation.
6. Test light diffusion, dimming and panel removal; clean with compatible products.

Accept the work when

- [] Glass is retained, edges protected and free of point loads.
- [] Lighting is even and serviceable.
- [] Fridge vent and service panel remain clear.

Still required to release this work

- [] Glazier supplies glass makeup, weight, retention, setting and cleaning specification.

Manufacturer instructions + sources

[Bar elevation](#)
[Coordination detail](#)

BAR-04 · Backlit bottle shelves

Millworker · custom · Drawing A03

MATERIAL / COMPONENT	QUANTITY BASIS	SPECIFICATION + RELEASE
Black-finished bottle shelves	2 custom shelves	Nominal 48 L x 10 D in; exact core, thickness, edge and finish selected by shop drawing. unselected
Rated shelf brackets/backing	2 sets	Concealed or approved brackets sized for bottles/glassware and fastened to verified backing. not designed
Recessed LED channel covers	2 sets	Removable diffusers/covers and cable chase interface coordinated with LGT-04. custom-detail
End stops or restraint detail	2 sets	Detail to reduce bottle movement where required by final shelf design. designer review

Tools + access

laser · stud/backing locator · level · drill/driver · load-test weights specified by designer

Before starting

- [] Complete M-07 and approve backing.
- [] Approve bottle-height mockup, shelf AFF heights and representative load.
- [] Coordinate LGT-04 feeds and removable cover.

Install in this order

1. Field-mark shelf centers from A03 and verify backing/cable zones.
2. Submit shelf/bracket/load and LED-channel shop detail.
3. Install backing before wall closure and photograph dimensions.
4. Finish wall, then mount brackets with specified substrate fasteners.
5. Fit shelves and LED covers; route cables without pinch points.
6. Apply the specified proof load and document deflection/fasteners.

Accept the work when

- [] Shelves are level, stable and match approved sample.
- [] Rated load and fastener record are documented.
- [] LED and wiring remain accessible; bottles do not block heat or fridge intake.

Still required to release this work

- [] Millworker/designer provides shelf load, bracket and fastener schedule.

Manufacturer instructions + sources

[Bar elevation](#)

BAR-05 · Front-venting glass-door beverage fridge

Millworker + electrician · buy · Drawing A03

MATERIAL / COMPONENT	QUANTITY BASIS	SPECIFICATION + RELEASE
Zephyr Presrv PRB15C01CG beverage cooler Product / instructions	1 unit	15 W x 23.375 D x 33.875–34.875 H in; front-venting built-in candidate. Final model/finish must be reconfirmed. candidate
Dedicated accessible receptacle/plug space	1 location	At least 1-in rear plug allowance plus code-compliant outlet placement; circuit by licensed electrician. design required
Hinge-side clearance	2.25 in minimum	Candidate manual minimum when adjacent to a wall; verify actual orientation. verified candidate fact
Floor/cabinet protection	1 set	Non-blocking pads/protection that do not obstruct leveling or front vent. select

Tools + access

appliance dolly · level · manufacturer-recommended leveling tools · electrical tester by electrician

Before starting

- ☐ Confirm final model, finish, hinge orientation, price, warranty and delivery.
- ☐ Approve cabinet shop drawing with 15.125-in minimum opening, 34-in minimum height, rear plug space and front vent.
- ☐ Verify route and service pull-out path.

Install in this order

1. Inspect delivered unit and model plate before modifying cabinetry.
2. Complete and test the receptacle before insertion.
3. Level the appliance per manual and slide it without pinching cord or blocking the front vent.
4. Set door/hinge clearances and verify full opening.
5. Run initial manufacturer start-up and temperature test.
6. Pull the unit out once to prove service access, then record serial/warranty.

Accept the work when

- ☐ Unit is level, vent unobstructed and door opens without collision.
- ☐ Cord/plug is not crushed and service pull-out works.
- ☐ Temperature and lighting operate per manufacturer check.

Still required to release this work

- ☐ Millworker releases final cutout and face projection.
- ☐ Electrician confirms circuit and outlet location.

Manufacturer instructions + sources

[Zephyr specification](#)
[Bar elevation](#)
[Fridge coordination detail](#)

BAR-06 · Three black bar stools · fit study

Furniture · buy · Drawing A03

MATERIAL / COMPONENT	QUANTITY BASIS	SPECIFICATION + RELEASE
JONATHAN Y Trinity 30-in backless bar stool Product / instructions	3 stools	Target TCIN 89893519 / UPC 840011489117; black 17 W x 17 D-in metal body, 13.5-in round seat, 30-in seat height, gold metal hairpin legs/footrest, 275-lb published capacity, no assembly. Candidate only: three bodies span 53 in at the current 18-in centers and exceed the 48-in bar by 5 in. candidate; full-size fit held
Finish-safe floor glides	3 sets	Confirm supplied feet and any added glide are compatible with the released floor; do not add a glide that destabilizes the hairpin base. field-select

Tools + access

full-size layout tape · tape measure · level · manufacturer assembly tools

Before starting

- [] Retain the A03 48-in bar and current 18-in stool-center geometry as the comparison baseline.
- [] Tape three 17-in bodies at the actual bar: at current centers the outer span is 53 in; even three touching bodies need 51 in.
- [] Operate the refrigerator door, south entry, adjacent lounge chair and piano bench with three occupied mock stools.
- [] Approve a physical gold finish sample against the room brass before any three-unit order.

Install in this order

1. Mark the 48-in counter run, current 18-in centers and three 17-in stool footprints from A03.
2. Seat three people and check the 12-in seat-to-counter height difference, knees, elbows, integrated footrests and counter overhang.
3. Test entry, refrigerator door/service, adjacent chair movement and piano-bench use with all three bodies in place.
4. Record any approved center shift or reduced quantity on the furniture plan; do not silently change the modeled layout.
5. After written fit and finish release, inspect each factory-assembled stool, fit approved glides if needed and place at the recorded centers.

Accept the work when

- [] The accepted quantity and centers are documented; three stools are not represented as fitting within the 48-in run.
- [] Every accepted stool is stable and leaves the entry, refrigerator and piano usable.
- [] TCIN, UPC, black/gold finish, published capacity and care/warranty record are in handover.

Still required to release this work

- [] Greg/furniture lead releases quantity and spacing only after the full-size occupied test.
- [] Supplier confirms current stock, return terms and finish before order; the observed listing is not a reserved unit.

Manufacturer instructions + sources

[A03 bar and piano elevation](#)
Target — JONATHAN Y Trinity stool, TCIN 89893519

KEY-01 · Yamaha NU1X hybrid upright + bench

Piano supplier · retain · Drawing A03

MATERIAL / COMPONENT	QUANTITY BASIS	SPECIFICATION + RELEASE
Yamaha AvantGrand NU1X Product / instructions	1 piano	Published 59.125 W x 18.25 D x 40.3125 H in; physical model and ownership must be confirmed. owned-check
Piano bench	1 bench	Identity, deployed envelope, finish and condition to be recorded in M-11. unverified retained
Floor protection	1 set	Caster/cup/pad system approved for piano weight and final floor without restricting leveling. select after floor decision
Power/audio leads	1 set	Existing or replacement leads labeled and routed without trip/service conflict. inventory

Tools + access

piano mover equipment · rated dollies/straps · level · camera · cable labels

Before starting

- ☐ Read model plate and inspect condition.
- ☐ Complete M-12 placement/bench test and M-15 delivery route.
- ☐ Confirm final floor capacity/protection and accessible power.

Install in this order

1. Photograph and label piano, bench, pedals and cables before moving.
2. Use qualified piano movers and protect thresholds/walls.
3. Place from the field-approved A03 datum, preserving the bar gap and bench envelope.
4. Level/stabilize per Yamaha/mover guidance and install approved floor protection.
5. Connect power/audio, manage slack and test keys, pedals and outputs.
6. Record final location, condition and model plate.

Accept the work when

- ☐ Piano and bench match approved clearances and do not block entry/bar.
- ☐ Instrument is stable, protected and fully functional.
- ☐ Cables are labeled, serviceable and do not create a trip path.

Still required to release this work

- ☐ Greg confirms ownership/model and final gap.
- ☐ Qualified mover provides lift/move method for actual route and weight.

Manufacturer instructions + sources

[Yamaha NU1X specifications](#)
[Bar and piano elevation](#)

SEAT-01 · Jennifer Taylor Home Alpine 90-inch sofa · Ebony Black Boucle

Furniture · buy · Drawing A01

MATERIAL / COMPONENT	QUANTITY BASIS	SPECIFICATION + RELEASE
Jennifer Taylor Home Alpine sofa Product / instructions	1 sofa	SKU 64190-3-MBB, Ebony Black boucle; use 90.5 W x 36 D x 27.5 H-in clearance envelope pending maker confirmation. selected-reference
Manufacturer leg/assembly hardware	1 set	Use only supplied hardware and current manufacturer instructions. included/verify
Finish-safe floor protection	1 set	Pads/glides compatible with oak legs and final floor. select

Tools + access

delivery-route measure · moving blankets · manufacturer assembly tools · level

Before starting

- [] Resolve 90 versus 90.5-in width and approve upholstery sample/return terms.
- [] Complete occupied M-12 mockup and M-15 route.
- [] Confirm current stock, delivery service and damage-inspection procedure.

Install in this order

1. Inspect packaging and upholstery before accepting delivery; record damage.
2. Move by approved route without loading arms or fabric incorrectly.
3. Install supplied legs/hardware in manufacturer order and fit approved floor protection.
4. Place to current A01 pose only after field layout release.
5. Level, allow cushions to recover and recheck occupied circulation.
6. Record SKU, lot, care and warranty.

Accept the work when

- [] Finish, dimensions and two-cushion silhouette match approved reference.
- [] Sofa is stable and clears all occupied/service paths.
- [] Care/return/warranty records are delivered.

Still required to release this work

- [] Manufacturer confirms published width discrepancy.
- [] Greg approves exact fabric and occupied fit.

Manufacturer instructions + sources

[Jennifer Taylor product page](#)
[Room plan](#)

SEAT-02 · IKEA DYVLINGE swivel armchairs · Kelinge black

Furniture · buy · Drawing A01

MATERIAL / COMPONENT	QUANTITY BASIS	SPECIFICATION + RELEASE
IKEA DYVLINGE swivel chair, Kelinge black Product / instructions	2 chairs	Article 805.708.31; 24.75 W x 29.5 D x 26.75 H in, 16.875-in seat; black textured polyester textile and chrome-color five-star base. selected-reference
Manufacturer assembly hardware	2 sets	Use supplied parts and current IKEA instructions; do not substitute. included/verify
Finish-safe floor protection	2 sets	Compatible with five-star bases and final floor without impairing swivel. select

Tools + access

manufacturer assembly tools · torque tool only if manual specifies · moving blankets · tape measure

Before starting

- [] Approve low seat and textile sample.
- [] Complete both occupied/swivel envelopes in M-12.
- [] Verify local stock, two-unit quantity, delivery and return terms.

Install in this order

1. Inventory all parts against the manual.
2. Assemble each chair in manufacturer sequence and tighten only as directed.
3. Verify five-star base engagement and full swivel before placement.
4. Fit approved non-binding floor protection if needed.
5. Place at released A01 rotations and repeat occupied swivel/approach test.
6. Keep article, care and warranty records.

Accept the work when

- [] Both chairs swivel freely, sit level and have no loose connections.
- [] Textile is Kelinge black and is not represented as leather.
- [] Placed chairs clear doors, table, desk and instrument/service paths.

Still required to release this work

- [] Greg approves low seat and exact textile.

Manufacturer instructions + sources

[IKEA product page](#)
[Room plan](#)

SEAT-03 · Smoked-glass cocktail table

Furniture · custom · Drawing A01

MATERIAL / COMPONENT	QUANTITY BASIS	SPECIFICATION + RELEASE
Custom smoked-glass cocktail table	1 table	Preferred: quote 30-in diameter x approximately 16-in high, smoked/black tempered-glass top, black structural base and restrained brushed-brass rim/accent. Fabricator designs glass thickness, edge, support, stability and floor protection. custom quote preferred; preserves render
By-Boo Bunga dimensional reference Product / instructions	1 reference only	Wayfair YBOO1890; 30-in diameter x 16-in high, black glass/conical black metal/gold rim. Exact visual/dimensional reference was out of stock when verified; do not order or imply availability. out-of-stock reference
17 Stories 30-in tinted-glass fallback Product / instructions	1 table	Wayfair W117302305; 30-in diameter x 17-in high. Candidate fallback only after Wayfair confirms the selected gold-base variant and tinted tempered-glass construction in writing because listing fields conflict. candidate; specification held
Floor-safe glides/pads	1 set	Specified for the actual base, rug and finished floor; custom fabricator includes and documents them. field-select

Tools + access

manufacturer assembly tools · level · tape measure · glass-safe gloves

Before starting

- [] Keep the A01 30-in-diameter x approximately 16-in-high table envelope as the preferred design.
- [] Tape a 30-in circle and test occupied chair sweeps, seated reach and circulation.
- [] Approve physical smoked-glass and brass samples under final lighting.
- [] For the 17-in-high fallback, repeat the full-size reach and chair-clearance test and obtain written finish/glass confirmation.

Install in this order

1. Issue the custom fabricator the approved envelope and finish brief; require a shop drawing for glass, edge, supports, stability and glides.
2. If using the buyable fallback, reconcile its listing fields in writing before ordering and record the exact variant.
3. Inspect tempered-glass marking, edges, base and all retainers before assembly or placement.
4. Assemble only to the maker/fabricator sequence without overtightening glass fittings; install specified floor protection.
5. Place at the released A01 center, level it and repeat seated reach, chair swivel and circulation checks.

Accept the work when

- [] Installed table is stable, glass is safety-rated/retained and every edge is undamaged.
- [] The accepted height and footprint work with both chairs, sofa and circulation.
- [] Custom shop drawing or exact retailer variant, care data and replacement/retainer information are delivered.

Still required to release this work

- [] Furniture lead chooses custom preferred or the held fallback after fit/sample review.
- [] Custom fabricator supplies the engineered glass/support/stability detail; this card does not prescribe glass thickness.

Manufacturer instructions + sources

[A01 room plan](#)

[Wayfair — By-Boo Bunga exact-size reference](#)

[Wayfair — 17 Stories 30-in fallback](#)

SEAT-04 · Dark patterned lounge rug + pad

Flooring + furniture · custom · Drawing A01

MATERIAL / COMPONENT	QUANTITY BASIS	SPECIFICATION + RELEASE
Custom dark patterned low-pile lounge rug	1 rug	Preferred when the rendered footprint must be preserved: nominal 120 x 108 in (10 x 9 ft), with approved fiber, pattern, bound/serged edge and cleanability. custom option; preserves render
Ruggable Sloane Black Flatwoven + Standard Pad, 8 x 10 Product / instructions	1 system	SKU RUG-SYS-IND-RCT-CHN-SR007-08x10; charcoal/grey geometric cover with cream accents, 2-mm polyester cover/waterproof barrier plus required same-size nonslip Standard Pad. One foot narrower than the modeled 10 x 9-ft footprint. candidate; full-size fit held
Ruggable Sloane Black Flatwoven + Standard Pad, 9 x 12 alternate Product / instructions	1 system	SKU RUG-SYS-IND-RCT-CHN-SR007-09x12; matches the modeled 9-ft short axis but extends 2 ft beyond its 10-ft long axis. Do not trim the cover or pad. alternate; full-size fit held
Custom rug pad for custom 10 x 9-ft rug Product / instructions	1 pad	RugPadUSA Eco-Plush 1/4-in, 100% felt, custom-cut slightly inside rug perimeter; no grip layer, so use only if heavy furniture securely anchors the rug and Karndean confirms compatibility. candidate for custom rug only

Tools + access

layout tape · straightedge/knife appropriate to pad · HEPA vacuum · rug grippers if approved

Before starting

- [] Retain A01 modeled 120 x 108-in footprint as the comparison baseline; no standard size is a silent 3D substitution.
- [] Tape 8 x 10 and 9 x 12 rectangles around the released sofa/chairs/table and verify doors, circulation, vents and service paths.
- [] Choose custom 10 x 9 if preserving the render footprint matters more than a direct-buy system.
- [] Approve the exact rug/pad sample and obtain written compatibility with the released finished floor.

Install in this order

1. Clean and fully dry the finished floor; confirm the selected rug and pad are the same approved size/system.
2. For Ruggable, lay the same-size Standard Pad and align/smooth the cover from the center outward; do not cut either component.
3. For the custom rug, install the approved custom-cut felt pad slightly inside the edge with no pad exposed.
4. Orient the accepted footprint to the recorded A01 layout, allow it to relax and align all pattern/edges.
5. Place furniture without dragging; test chair swivel, table stability, edge lift and every adjacent route.
6. Record the selected SKU/size or custom edge specification and the manufacturer cleaning method.

Accept the work when

- [] Accepted footprint is documented against the modeled 10 x 9 ft: 8 x 10 is 1 ft narrower; 9 x 12 is 2 ft longer.
- [] Rug lies flat with no trip edge, pad exposure, blocked vent/threshold or rolling-chair conflict.
- [] Cover, pad and finished-floor compatibility are documented; no Ruggable component was trimmed.

Still required to release this work

- [] Greg/furniture lead selects custom 10 x 9, 8 x 10 or 9 x 12 only after the full-size furniture test.
- [] Flooring supplier confirms long-term pad compatibility and warranty treatment in writing.

Manufacturer instructions + sources

[A01 room plan](#)
[Ruggable Sloane Black rug](#)
[Ruggable Standard Rug Pad](#)
[RugPadUSA Eco-Plush 1/4-in custom pad](#)

FIN-01 · Dark main-room floor

Flooring · buy · Drawing A01

MATERIAL / COMPONENT	QUANTITY BASIS	SPECIFICATION + RELEASE
Karndean Van Gogh Rigid Core Ebony SCB89 Product / instructions	14 cartons candidate	14 x 23.64 = 330.96 sq ft for current 328.63-sq-ft allowance; final field takeoff and lot required. candidate
Transition/nosing profiles	1 measured set	Exact profiles/finish for doors, sliders, booth and raised platforms after M-08/M-16. unselected
Perimeter spacers and trim/base	1 measured set	Manufacturer-compatible expansion accessories and approved black/dark trim. unselected
Subfloor preparation materials	1 field allowance	Patch/level/moisture products selected by installer for tested substrate. field-dependent
Spare flooring	1 allowance	Owner spare quantity set after carton rounding and final cut plan. not set

Tools + access

moisture/flatness test tools · manufacturer-approved cutting tools · spacers/tapping tools per manual · HEPA vacuum · rollers only if system requires

Before starting

- [] Greg chooses dark floor versus retained oak.
- [] M-08 identifies existing floating/adhered assembly and substrate; floating floor is removed before this candidate.
- [] M-16 resolves platform/threshold geometry and installer issues warranted assembly.
- [] Use the current Karndean guide to document substrate flatness, concrete/wood moisture, expansion, fixture sequence and transitions; do not add separate underlay without written approval.

Install in this order

1. Protect and inventory retained items; remove only the approved existing floor and preserve boards where feasible.
2. Prepare substrate to manufacturer flatness/moisture requirements and document readings.
3. Acclimate/store product as the current manual requires.
4. Set layout/start line and expansion zones from approved floor plan.
5. Install planks and cuts per manufacturer sequence, staggering and perimeter requirements.
6. Install released thresholds/nosings/base without pinning the floating field.
7. Clean, protect and record lot, cartons, spares and warranty.

Accept the work when

- [] Installed floor is flat, stable and warrantable with documented substrate readings.
- [] Doors, sliders, fridge and platforms operate over completed transitions.
- [] Expansion zones and spare material remain documented.

Still required to release this work

- [] Flooring installer supplies final takeoff, substrate products, transition/base schedule and written warranty.
- [] Greg provides written approval before oak removal.

Manufacturer instructions + sources

[Karndean Ebony SCB89 product page](#)
[Karndean U.S. rigid-core installation guide](#)
[A01 room plan](#)

FIN-02 · Charcoal wall finish + acoustic retention

Finish contractor + acoustician · custom · Drawing A02

MATERIAL / COMPONENT	QUANTITY BASIS	SPECIFICATION + RELEASE
Guilford FR701 style 2100 color 408 Black Product / instructions	1 field takeoff	66-in usable width; production sample/dye lot and measured yardage required. candidate
FabriTRAK GeoTRAK black profiles Product / instructions	1 field takeoff	Final 0.5/1/1.375-in profile depth and linear footage selected with complete assembly. candidate
Acoustic core/backing	1 field takeoff	Core type/thickness, fire/acoustic documentation and substrate compatibility by acoustician/dealer. unselected
Perimeter/corner/outlet/HVAC trim	1 measured set	Track transitions and removable access details for all interruptions. unselected
Charcoal finish for approved solid walls	1 measured scope	Maker/color/primer/sheens selected after mockup; never coat retained fabric. unselected

Tools + access

fabric-track tools by dealer · laser/level · substrate prep tools · HEPA vacuum · sample light at 2700K

Before starting

- [] M-07 documents wall build-up and M-14 establishes acoustic baseline.
- [] Approve full assembly sample, dye lot, fire/acoustic documentation and solid-wall paint sample.
- [] Issue wall elevations with fabric/solid/slat boundaries and access panels.

Install in this order

1. Remove only finish layers approved after acoustic review.
2. Repair/prepare substrate and install verified blocking where required.
3. Install track/core from approved elevations, keeping devices, grilles and service panels accessible.
4. Stretch and lock fabric with seams and grain aligned; do not contaminate face.
5. Apply approved charcoal finish only to released solid substrates.
6. Complete junction trim at doors, slats, ceiling and floor.
7. Inspect, clean and remeasure acoustic response.

Accept the work when

- [] Fabric is taut, removable where required and matches approved dye lot.
- [] No covered device, grille, label or service access.
- [] Finish disposition and before/after acoustic records are archived.

Still required to release this work

- [] Acoustician/dealer issues exact track-core-fabric assembly, takeoff and test documentation.
- [] Painter issues substrate/primer/topcoat system.

Manufacturer instructions + sources

[FR701 sample](#)
[FabriTRAK GeoTRAK](#)
[Mirror wall elevation](#)

FIN-03 · Black slat panels at bay returns

Finish carpenter · buy · Drawing A04

MATERIAL / COMPONENT	QUANTITY BASIS	SPECIFICATION + RELEASE
WoodUpp Akupanel item 1029 Product / instructions	5 panels minimum before waste	94.49 x 23.62 x 0.866-in candidate, black wrapped slats on black felt; final count/cut plan required because wall is assumed 102 in high. candidate
Battens and cavity insulation	1 field takeoff	Only if approved assembly uses expanded acoustic build-up; dimensions/material/test documentation by designer. unselected
Black termination/infill trim	1 measured set	Resolve 7.51-in height shortfall and all panel edges/joints. unselected
Panel fasteners	1 scheduled set	Manufacturer/system fasteners matched to verified substrate and backing. not released
Penetration/access trim	1 set	For hangers, wiring, devices and removable service zones. unselected

Tools + access

track/mitre saw with dust extraction · laser/level · stud/backing locator · manufacturer-specified drill/driver · PPE

Before starting

- [] Field-verify both return lengths/angles, ceiling height and M-13 backing zones.
- [] Approve panel sample, fire documentation and exact wall build-up.
- [] Issue cut/termination plan resolving the 7.51-in shortfall.

Install in this order

1. Lay out slat rhythm, joints, top/bottom termination and penetration centers on each return.
2. Install approved battens/backing/insulation without covering service paths.
3. Cut panels with supported faces and controlled dust.
4. Fasten at the approved pattern into verified substrate/backing.
5. Fit black infill/termination and trimmed access penetrations.
6. Photograph hidden fasteners/backing and inspect alignment.

Accept the work when

- [] Slats are plumb, rhythm/joints match approved elevation and cut edges are finished.
- [] Hanger/TV/service backing remains locatable and accessible.
- [] Installed assembly matches submitted fire/acoustic build-up.

Still required to release this work

- [] Architect/acoustician/installer releases panel count, cut plan, build-up and substrate fasteners.

Manufacturer instructions + sources

[WoodUpp product](#)
[TV and instrument elevation](#)

FIN-04 · Ceiling, trim + exposed solid-surface paint

Painter · custom · Drawing E01

MATERIAL / COMPONENT	QUANTITY BASIS	SPECIFICATION + RELEASE
Benjamin Moore Aura Waterborne Interior Paint, Matte Product / instructions	1 painter takeoff	SKU N522 in approved sampled black, such as Black 2132-10; published theoretical spread 350–400 sq ft/gal is not a buy quantity. Measure solid surfaces and price the substrate-specific coat schedule. candidate; color/quantity held
Benjamin Moore substrate-specific primer/sealer/stain blocker Product / instructions	1 painter takeoff	Painter selects from the current Aura N522 TDS for each verified substrate and existing coating condition; no universal primer is specified. field-dependent
Benjamin Moore Scuff-X Interior Matte optional high-touch alternate Product / instructions	1 approved-area takeoff	SKU N484 in approved black formula for doors/trim or other high-touch solid surfaces only after side-by-side color/sheen mockup. optional candidate
Patch, prep, masking and protection materials	1 field allowance	Painter selects fillers, abrasives, cleaners and low-tack/non-staining protection compatible with inspected substrates, mirrors, fabric, labels, devices and gear. trade-select

Tools + access

HEPA sanding/extraction · work lights · wet-film/dry-film gauges if required · spray/roller tools selected by coating maker

Before starting

- [] Rough-in inspection is signed and all access locations recorded.
- [] Approve substrate preparation and sheen/color mockups under room lighting.
- [] Remove/protect gear and mask fabric, grilles, devices and labels.

Install in this order

1. Repair and prepare each released solid substrate to coating specification.
2. Prime test areas and verify adhesion/bleed before broad application.
3. Apply ceiling, fascia and trim coats in approved sequence and film coverage.
4. Maintain access-panel cuts and clean device edges.
5. Remove masking before it damages finish and correct punch items by same system.
6. Record product codes, lots and spare paint.

Accept the work when

- [] Uniform approved color/sheen with no coating on acoustic fabric, glass, devices or labels.
- [] Access panels and service clearances remain operable.
- [] Paint schedule and touch-up stock are handed over.

Still required to release this work

- [] Painter provides product/primer/substrate schedule, coverage takeoff and application data.

Manufacturer instructions + sources

[Aura Matte N522 technical data sheet](#)
[Benjamin Moore Aura Matte N522 product page](#)
[Benjamin Moore Scuff-X Matte N484](#)
[E01 reflected ceiling coordination](#)

DESK-01 · Fixed production desk + 12U rack

Millworker + AV · custom · Drawing A04

MATERIAL / COMPONENT	QUANTITY BASIS	SPECIFICATION + RELEASE
Fixed production desk	1 custom assembly	Nominal 72 L x 32 D x 30 H in; top/core/edge/base/finish set after equipment fit. unselected
12U rack enclosure	1 rack	Maker, rail spacing/depth/load, ventilation and finish required; reuse only after verification. unselected
Rack accessories	1 scheduled set	Rails, cage nuts/screws, shelves, blank panels, ventilation/fans and rack power sized to final equipment. unselected
Cable trays/grommets/service panels	1 set	Removable, radius-safe cable management with labeled separation of power and signal. unselected
Equipment restraints/arms	1 set	Console/display/monitor support selected from actual loads and service motions. unselected
Backing/anchors/levelers	1 engineered set	Substrate-specific restraint and adjustable support on shop drawing. not released

Tools + access

laser/level · millwork tools · rack-square gauge · ventilation test tools · manufacturer fastener tools

Before starting

- [] M-02/M-11/M-13 verify bay, PMC, console, displays, rack depth/heat and chair clearances.
- [] AV integrator issues rack elevation and cable/airflow schedule.
- [] Approve desk mockup and shop drawing.

Install in this order

1. Field-measure bay and lay out knee, rack, chair, speaker and service zones.
2. Submit desk/rack shop drawings with materials, load support, cooling, cable access and anchors.
3. Prefabricate, finish and dry-fit rack/equipment openings.
4. Install backing, set/level/restraint desk and keep panels removable.
5. Install rack rails/accessories and verify square/depth/air path.
6. Fit trays/grommets and hand off to AV for equipment set.

Accept the work when

- [] Desk/rack are stable, level and match approved finish.
- [] All equipment can be connected, ventilated and removed without dismantling fixed work.
- [] Chair, speakers, TV and instrument removal paths remain clear.

Still required to release this work

- [] Millworker supplies material/anchor/load shop drawing.
- [] AV integrator supplies rack elevation, heat/load, power and cable schedule.

Manufacturer instructions + sources

[TV and instrument elevation](#)
[Room plan](#)

TV-01 · 50-inch TV + low-profile mount

AV + carpenter · buy · Drawing A04

MATERIAL / COMPONENT	QUANTITY BASIS	SPECIFICATION + RELEASE
TCL 50S551G dimensional reference Product / instructions	1 reference only	Existing v1.4 geometry reference: 43.7 W x 25.4 H x 2.8 D in, 19.6 lb, VESA 300 x 300 mm. Retain for geometry history; not the current buy claim. geometry reference
TCL 50Q651G 50-in Q6 QLED Google TV Product / instructions	1 display	Best Buy SKU 6579462; exact 43.7 W x 25.4 H x 2.8 D-in body without stand, 19.6 lb, black, VESA 300 x 300 mm; M6 x 12 top and M6 x 16 bottom screws per TCL specification. Same modeled cabinet envelope; candidate only until M-13. candidate; purchase and M-13 held
SANUS Elite BLL2-B1 fixed mount Product / instructions	1 mount	Best Buy SKU 5463303; black, 32–80-in listed range, 150-lb capacity, 0.67-in nominal wall offset, includes 300 x 300-mm interface. Compatibility and actual projection remain subject to SANUS confirmation and M-13. candidate; wall fit held
Mount hardware/spacers and substrate fasteners	1 coordinated set	Use SANUS-supplied TV hardware/spacers and qualified-installer-selected wall fasteners for the verified wall assembly; do not infer anchors from the 150-lb mount rating. field-dependent
Recessed/accessible power, data and signal set	1 set	Code-compliant power/data interface, rated signal/control cables, connector bend allowance and service loop; no loose concealed power cord. AV/electrical design required

Tools + access

mount template · laser/level · stud/backing locator · torque tools per mount manual · AV signal tester

Before starting

- [] Retain the v1.4 43.7 x 25.4 x 2.8-in cabinet envelope; identify 50Q651G explicitly as the purchase candidate rather than silently swapping the model.
- [] Retrieve the current model-specific 50Q651G manual/support documents at purchase and reconcile them with the delivered unit; a different model's manual is not accepted as the governing document.
- [] Complete M-13 using the purchased display, SANUS mount, 300 x 300-mm VESA template, connectors and the actual instruments.
- [] Issue wall backing/fastener and code-compliant power/data details before finish closure; prove plug/connector clearance behind the 0.67-in-profile mount.

Install in this order

1. Inspect the delivered 50Q651G model/serial, cabinet, connector locations, 300 x 300-mm VESA pattern and specified screw lengths; bench-test the display.
2. Read the current 50Q651G support documents and SANUS BLL2 manual; reconcile brackets, spacers, screw engagement, lift crew and wall type.
3. Install inspected backing and code-compliant power/data rough-in before finish closure.
4. Template the actual display, mount and cable exits on the released A04/M-13 elevation with every guitar/yoke/removal arc.
5. Fasten the mount to the released substrate detail, verify level and manual-specified tightening, attach TV brackets without bottoming screws, then lift and engage safety locks.
6. Connect labeled cables with proved bend clearance and service loop; test power, signal, ventilation, lateral position and safe removal/service.

Accept the work when

- [] Delivered 50Q651G matches the recorded 43.7 x 25.4 x 2.8-in cabinet, 19.6-lb weight and 300 x 300-mm VESA pattern.
- [] BLL2 safety locks engage; display is level and actual projection/connector clearance are documented rather than inferred from 2.8 + 0.67 in.
- [] Power/data are code-compliant and accessible; screen clears every instrument body, headstock, yoke, removal arc and desk sightline.
- [] Model-specific TCL support record and SANUS BLL2 manual are included in closeout.

Still required to release this work

- [] AV installer retrieves and records the current model-specific 50Q651G manual/support document at purchase.

[] Qualified designer/carpenter supplies backing and wall-fastener detail; electrician supplies the in-wall power/data method.

Manufacturer instructions + sources

[TCL 50S551G v1.4 geometry reference](#)

[TCL 50Q651G manufacturer product/specification](#)

[Best Buy — TCL 50Q651G, SKU 6579462](#)

[SANUS BLL2 manufacturer page](#)

[SANUS BLL2 installation manual](#)

[A04 TV and instrument elevation](#)

GTR-01 · TV + guitar/bass mounting layout and structural backing

Carpenter + AV · custom · Drawing A04

MATERIAL / COMPONENT	QUANTITY BASIS	SPECIFICATION + RELEASE
Structural backing for TV/instrument layout	1 field-fit set	Continuous or localized backing sized to approved full-size template; material/thickness/fasteners by attachment design. not designed
Instrument hangers Product / instructions	10 proposed display positions	Ten-position design target; six instruments listed in inventory. Final count follows M-13; String Swing CC01K or CC01 assigned per actual neck/weight/finish. No hanger order before full-size fit. candidate
Hanger substrate fasteners	1 scheduled set	Per hanger, load and verified backing; do not use generic wall anchors without released detail. not released
Penetration/finish trim	1 set	Black trim/grommets coordinated with slat/fabric wall and removable access. unselected

Tools + access

full-size removable template film · laser/level · backing locator · drill/driver · torque tools per hanger maker

Before starting

- [] Inventory actual instruments under GTR-02.
- [] Complete M-13 with TV, mount, connectors, yokes and removal arcs.
- [] Greg approves final count/elevation and qualified installer releases backing/fasteners.

Install in this order

1. Transfer approved full-size template to field datum and mark every load/penetration.
2. Install and photograph backing before wall closure.
3. Complete wall finish/slat penetrations without losing backing locations.
4. Install each assigned hanger with specified fasteners and orientation.
5. Apply a controlled proof/inspection procedure specified by installer before hanging instruments.
6. Hang one instrument at a time and test removal arc, finish contact, TV and lighting clearance.

Accept the work when

- [] Installed centers match approved field template.
- [] Every hanger is matched to instrument weight/neck/finish and verified backing.
- [] All instruments remove safely without TV, light, desk or neighboring-instrument contact.

Still required to release this work

- [] Installer supplies backing, loads, fasteners and proof/inspection method.
- [] Greg approves final displayed instrument count and positions.

Manufacturer instructions + sources

[String Swing hanger](#)
[TV and instrument elevation](#)

GTR-02 · Owned guitars and basses for TV wall

Greg + AV · retain · Drawing A04

MATERIAL / COMPONENT	QUANTITY BASIS	SPECIFICATION + RELEASE
Owned guitar	1 listed instrument	Physical model, dimensions, weight, finish and hanger fit to verify. unverified retained
Additional instruments for remaining display positions	up to 4 held inventory / loan allowance	Ten display positions minus six listed instruments. Reconcile existing unlisted instruments and any approved loans before considering purchases; model, size, finish, hanger and funding remain undecided. inventory and display decision required; no purchase release
Owned basses	5 listed instruments	Physical models, dimensions, weights, finishes and hanger fit to verify. unverified retained
Protective cases/storage	6 sets	Retain accessible storage for any instrument not approved for display. inventory

Tools + access

scale · tape/calipers · camera · removable labels · finish-safe handling supports

Before starting

- [] Create one inventory row per physical instrument.
- [] Do not assume all six fit or that CC01K suits every neck.
- [] Prepare safe temporary storage during wall work.

Install in this order

1. Photograph front/back/model/finish and record weight, overall body/headstock and neck/yoke dimensions.
2. Inspect finish condition and identify nitrocellulose or delicate surfaces.
3. Assign candidate hanger only after maker compatibility review.
4. Template each body, headstock, yoke and removal arc in M-13.
5. Greg selects the field-approved display count; store remaining instruments safely.
6. After hanger release, place and remove each instrument under observation.

Accept the work when

- [] Inventory reconciles to physical items and current owner list.
- [] Each displayed instrument has a documented hanger assignment and no finish-pressure concern.
- [] Non-displayed instruments have an identified protected location.

Still required to release this work

- [] Greg confirms ownership and display priority.
- [] Instrument technician/maker guidance resolves finish or unusual-neck compatibility.

Manufacturer instructions + sources

TV and instrument elevation
String Swing finish guidance

LGT-01 · Perimeter cove tape + channel

Lighting supplier + electrician · buy · Drawing E01

MATERIAL / COMPONENT	QUANTITY BASIS	SPECIFICATION + RELEASE
Diode LED BLAZE 100 2700K tape Product / instructions	71.76 linear ft net	Part DI-24V-BLBSC1-27-016 candidate; field perimeter and waste/run split required. candidate
Diode LED S1 black channel bundle with classic frosted lens Product / instructions	1 field takeoff	SKU DI-CHB-S1-96B, 96-in straight lengths; field takeoff, cut plan, waste and spare lenses required. Confirm quoted bundle contents. candidate
Diode LED S1 black accessory pack Product / instructions	1 scheduled set	SKU DI-CHB-S1-ACCB; quantity by joint/end/feed schedule after distributor deducts accessories included in each channel bundle. candidate
Diode-compatible feeds/leads/connectors/Class 2 wire Product / instructions	1 scheduled set	Project-specific CLICKTIGHT PRO connectors or supplier-approved factory/soldered leads, polarity-correct connections and conductor sizing from the signed run/voltage-drop schedule. design required
Diode LED OMNIDRIVE Basics 24V 96W Class 2 drivers Product / instructions	1 load schedule	SKU DI-ODBELV-24V96W-LPS; count by zone, connected watts, conductor length and voltage drop, with accessible ventilated locations. candidate

Tools + access

channel saw/cutting fixture · solder/crimp tools specified by supplier · multimeter · light meter · dimming test load

Before starting

- [] Replace estimated perimeter with M-01 field length.
- [] Approve cove profile, source concealment and 2700K dimming mockup.
- [] Receive run/feed/driver/access and voltage-drop schedule; each candidate run stays within 55 ft.

Install in this order

1. Mark channel runs, joints, feeds and accessible driver locations from E01.
2. Install straight/aligned channel and deburr/clean before tape.
3. Pull labeled low-voltage leads separately from incompatible services.
4. Cut/connect tape only at maker points and seat it in clean channel.
5. Fit lenses/end caps, connect matched drivers and controls.
6. Energize by zone; test polarity, flicker, low-end dimming and visible hot spots.

Accept the work when

- [] Continuous even line with concealed source and aligned joints.
- [] Run lengths/driver loads match signed schedule and access remains open.
- [] Scene control passes flicker and camera tests.

Still required to release this work

- [] Lighting supplier/electrician supplies final takeoff, wire sizing, run/feed and driver schedule.

Manufacturer instructions + sources

[Diode LED BLAZE product page](#)
[BLAZE specification sheet](#)
[Diode LED S1 channel and bundle accessories](#)
[OMNIDRIVE Basics specification sheet](#)
[CLICKTIGHT PRO installation guide](#)
[E01 reflected ceiling plan](#)

LGT-02 · Arch backlight tape + channel

Lighting supplier + glazier · buy · Drawing A02

MATERIAL / COMPONENT	QUANTITY BASIS	SPECIFICATION + RELEASE
Diode LED BLAZE 100 24V 2700K tape candidate Product / instructions	76.37 linear ft net	SKU DI-24V-BLBSC1-27-016 may serve straight legs; 3.93-in cut points and 55-ft maximum run per feed. Curved arch-head source/channel remains supplier-designed and manufacturer-approved. candidate for straight segments; curve unresolved
Straight/flexible black channels and diffusers	1 field-template takeoff	Distinct components may be required for verticals and curved heads. unselected
End caps/clips/joiners	1 scheduled set	Count from five field templates and supplier detail. unselected
Individual concealed feeds/leads	5 minimum runs	One serviceable feed strategy per arch unless supplier design states otherwise. design required
Diode LED OMNIDRIVE Basics 24V 96W Class 2 drivers Product / instructions	1 load schedule	SKU DI-ODBELV-24V96W-LPS candidate; quantity/load/voltage-drop and accessible locations coordinated under LGT-07. candidate pending signed load schedule

Tools + access

field templates · channel forming/cutting tools approved by supplier · multimeter · dimming test equipment

Before starting

- [] MIR-01 final templates and glass/backing details are released.
- [] Approve a full curved-head light mockup with mirror sample.
- [] Supplier signs bend/cut/channel/feed and driver schedule.

Install in this order

1. Transfer each arch template to light-channel fabrication schedule.
2. Install backing, channels and removable access before mirror panels.
3. Pull and label individual feeds without crossing retainer zones.
4. Cut/connect light source per maker points and fit diffusers/end caps.
5. Bench-test each arch, then install mirrors without trapping service components.
6. Commission all five together for uniform output and dimming.

Accept the work when

- [] Halos follow both verticals and head evenly with bottom edge unlit.
- [] No channel conflict with glass retention or exposed bright source.
- [] Each feed/driver can be serviced without unsafe glass removal.

Still required to release this work

- [] Lighting supplier supplies approved curved system and takeoff.
- [] Glazier coordinates access and no-go retention zones.

Manufacturer instructions + sources

[A02 mirror elevation](#)
[Diode LED BLAZE product page](#)
[BLAZE specification sheet](#)
[Diode LED S1 channel and bundle accessories](#)
[OMNIDRIVE Basics specification sheet](#)
[CLICKTIGHT PRO installation guide](#)

LGT-03 · Ceiling inset perimeter backlight

Lighting supplier + glazier · buy · Drawing E01

MATERIAL / COMPONENT	QUANTITY BASIS	SPECIFICATION + RELEASE
Diode LED BLAZE 100 24V 2700K tape Product / instructions	32 linear ft net	Four sides of nominal 96 x 96-in zone; final module/perimeter field dimensions control. Candidate SKU DI-24V-BLBSC1-27-016; cut only at 3.93-in marks and keep each feed within the 55-ft published limit. candidate
Diode LED S1 black channel bundle with classic frosted lens Product / instructions	1 field takeoff	Candidate SKU DI-CHB-S1-96B in straight 96-in lengths; profile must conceal source from seated views and remain removable. candidate
Diode LED S1 accessory packs/corners Product / instructions	1 scheduled set	Candidate SKU DI-CHB-S1-ACCB plus supplier-approved corner/join detail; exact pieces from panel, feed and service-access design. candidate; quantity unresolved
Feeds/leads and OMNIDRIVE Basics 96W drivers Product / instructions	1 load schedule	Driver candidate SKU DI-ODBELV-24V96W-LPS; count/load/wire/voltage drop coordinated in LGT-07 outside unsupported mirror area. design required

Tools + access

laser/level · channel cutting tools · multimeter · dimming/camera test

Before starting

- ☐ MIR-02 support/modules and service access are released.
- ☐ Approve sightline mockup from all seated positions.
- ☐ Coordinate driver/feed routes clear of mirror retention.

Install in this order

1. Set out channel perimeter from issued E01 and mirror support frame.
2. Install channels/access components before glass modules.
3. Pull labeled leads and terminate tape at maker cut points.
4. Fit lenses/corners and test complete halo before mirror closure.
5. After mirrors install, retest dimming, flicker and service access.

Accept the work when

- ☐ Even concealed perimeter glow from all occupied views.
- ☐ No support/retainer conflict and every driver remains accessible.
- ☐ Zone responds correctly in all scenes.

Still required to release this work

- ☐ Lighting supplier/electrician issues final channel, corner, feed and driver schedule.

Manufacturer instructions + sources

[E01 reflected ceiling plan](#)
[D3 coordination detail](#)
[Diode LED BLAZE product page](#)
[BLAZE specification sheet](#)
[Diode LED S1 channel and bundle accessories](#)
[OMNIDRIVE Basics specification sheet](#)
[CLICKTIGHT PRO installation guide](#)

LGT-04 · Shelf + counter accent tape

Lighting supplier + millworker · buy · Drawing A03

MATERIAL / COMPONENT	QUANTITY BASIS	SPECIFICATION + RELEASE
Diode LED BLAZE 100 24V 2700K tape Product / instructions	12 linear ft net	Two 48-in shelves plus one 48-in counter accent; final millwork dimensions control. Candidate SKU DI-24V-BLBSC1-27-016; cut only at 3.93-in marks and keep each feed within the 55-ft published limit. candidate
Diode LED S1 black channel bundle with classic frosted lens Product / instructions	3 runs	Candidate SKU DI-CHB-S1-96B; millworker confirms whether the straight surface/millwork profile suits each routed recess and remains removable. candidate
Diode LED S1 accessory packs plus feeds/leads Product / instructions	3 run sets	Candidate SKU DI-CHB-S1-ACCB, with project-specific CLICKTIGHT PRO or supplier-approved leads; exact count per millwork feed/joint schedule. candidate; quantity unresolved
Diode LED OMNIDRIVE Basics 24V 96W Class 2 driver Product / instructions	1 load group	Candidate SKU DI-ODBELV-24V96W-LPS; quantity/load/location from signed schedule, accessible and clear of bottles/fridge intake. design required

Tools + access

millwork routing template · channel saw · multimeter · dimming test load

Before starting

- [] BAR-01/BAR-04 shop drawings are released.
- [] Approve recessed profile and diffusion mockup.
- [] Assign feed chases and driver access before fabrication.

Install in this order

1. Route/fabricate straight channel recesses before millwork finish.
2. Install channels, pull labeled leads and protect recesses through finish work.
3. Cut/connect tape at maker points and fit lenses/end caps.
4. Connect accessible driver/control and restore removable covers.
5. Test heat, diffusion, dimming and fridge-vent separation with bottles in place.

Accept the work when

- [] Even light with no exposed diodes or pinched leads.
- [] Channels/covers and driver remain removable.
- [] No stored item or appliance vent is heated/blocked.

Still required to release this work

- [] Millworker and lighting supplier issue channel/recess/feed detail and driver location.

Manufacturer instructions + sources

[A03 bar elevation](#)
[Diode LED BLAZE product page](#)
[BLAZE specification sheet](#)
[Diode LED S1 channel and bundle accessories](#)
[OMNIDRIVE Basics specification sheet](#)
[CLICKTIGHT PRO installation guide](#)

LGT-05 · Main-room 4 in downlights

Electrician · buy · Drawing E01

MATERIAL / COMPONENT	QUANTITY BASIS	SPECIFICATION + RELEASE
Nora NM4-RDC27BB 4-in black downlight Product / instructions	6 fixtures	2700K matte-black candidate, 15W, 3.5-in cutout, 4.875-in module height. candidate
Remote drivers/junction components	6 fixture sets	Use exact listed components supplied/approved with selected fixture. included/verify
Compatible dimmer/control interface	1 zone set	Final device from LGT-07 compatibility test. unselected
Extension/access accessories	1 scheduled set	Only manufacturer-listed components; driver stays accessible. field-dependent

Tools + access

ceiling scanner/inspection camera · laser · manufacturer cutout template · electrical testers · light meter

Before starting

- [] M-03 verifies cavity, structure and insulation; no direct spray-foam contact.
- [] Photometric review approves six current points and light levels.
- [] Bench-test exact fixture/driver/dimmer load at low end.

Install in this order

1. Transfer six issued E01 points and scan each for conflicts.
2. Complete wiring/junction rough-in and inspection before cuts.
3. Cut only after mirror/HVAC/detector coordination is signed.
4. Install driver/junction and module per manufacturer clearances with access retained.
5. Energize, aim if applicable and measure scene levels.
6. Test dimming, flicker, camera response and heat/clearance.

Accept the work when

- [] All six fixtures align with E01 and avoid mirror/support conflicts.
- [] Drivers/junctions remain accessible and compatibility test passes.
- [] Light output, color and scenes match approved mockup.

Still required to release this work

- [] Electrician/lighting designer supplies photometric, circuit and compatibility schedule.

Manufacturer instructions + sources

[Nora fixture](#)
[Reflected ceiling plan](#)

LGT-06 · Guitar-wall track + four heads

Electrician · buy · Drawing E01

MATERIAL / COMPONENT	QUANTITY BASIS	SPECIFICATION + RELEASE
WAC 4-ft 120V single-circuit H Track, black Product / instructions	1 track	SKU HT4-BK; 4-ft H-style track section. Feed, end cap and support hardware are separate and selected after ceiling/junction survey. candidate
WAC Silo X20 black H-track heads Product / instructions	4 heads	SKU H-2020-927-BK; 20W, 2700K, 90 CRI, adjustable 15–50-degree beam. Four heads total 80W nominal; mock up beam and glare with actual TV/instruments. candidate
WAC H-track black live-end/feed and end cap Product / instructions	1 coordinated set	Electrician selects exact WAC H-family feed after confirming feed side, grooved-side polarity and junction geometry; do not guess the feed SKU. field-select
Mounting/backing fasteners	1 released set	Qualified installer selects for verified ceiling structure and the WAC instructions; track/head ratings do not establish support capacity. not released
Compatible dimmer/control	1 zone	Coordinated in LGT-07 and approved by full/low-output and camera-flicker mockup. unselected

Tools + access

laser · ceiling scanner · manufacturer mounting tools · electrical tester · light meter

Before starting

- [] Approve guitar/TV elevation and ceiling backing.
- [] Select one compatible track/feed/head family and test beam/glare.
- [] Coordinate control zone and circuit.

Install in this order

1. Lay out track from issued E01 and confirm every support/feed point.
2. Install and inspect backing/wiring before ceiling closure.
3. Mount track with specified fasteners, fit feed/end caps and verify continuity.
4. Insert four compatible heads and lock per manufacturer.
5. Aim only after TV/instruments/desk are in place.
6. Test dimming, glare, screen reflection and seated-eye exposure.

Accept the work when

- [] Track is straight, supported and electrically tested.
- [] Four heads lock securely and illuminate instruments without screen/seated glare.
- [] Control and aiming positions are recorded.

Still required to release this work

- [] Lighting designer selects track family, length, heads, beams and control.
- [] Qualified designer/electrician supplies support/fastener and circuit detail.

Manufacturer instructions + sources

[E01 reflected ceiling plan](#)
[A04 TV/instrument elevation](#)
[WAC H Track product page](#)
[WAC H Track installation instructions](#)
[WAC Silo X20 product page](#)

LGT-07 · Lighting control + matched drivers

Electrician + AV · custom · Drawing E01

MATERIAL / COMPONENT	QUANTITY BASIS	SPECIFICATION + RELEASE
Lighting control processor/interface	1 engineered package	One user interface with independent cove, downlight, mirror, bar/shelf, track and booth zones; DMX versus phase/ELV architecture unresolved. not designed
Matched dimmers/relays	1 load schedule	One or more devices per signed load/fixture compatibility schedule. unselected
24V drivers Product / instructions	1 load schedule	Accessible matched drivers sized per tape run and Class 2 limits; OMNIDRIVE 96W is candidate. candidate
Keypads/labels	1 set	Scene interface and engraved/plain-language labels approved by Greg. unselected
Driver/control enclosures and access panels	1 set	Ventilated/code-compliant accessible locations. unselected

Tools + access

load calculator · manufacturer compatibility tools · multimeter · oscilloscope/flicker meter if used · camera test setup · label printer

Before starting

- [] M-09/M-10 document circuits, neutrals, fixtures and retained controls.
- [] Resolve control protocol and emergency/safety-device interaction.
- [] Bench-test every exact fixture/driver/dimmer combination.

Install in this order

1. Build a zone/load/run schedule linked to LGT-01...06 and BOO-03.
2. Select compatible controls, drivers, interfaces and accessible enclosure locations.
3. Submit riser, device schedule, addressing/labels and scene intent.
4. Install after approved rough inspection; label line and low-voltage terminals.
5. Program lounge, session and meditation scenes plus booth task requirement.
6. Test low-end stability, flicker, camera response, outage recovery and manual operation.
7. Archive configuration and service map.

Accept the work when

- [] Every zone operates independently and scenes are repeatable.
- [] No flicker/dropout/overload across tested range and drivers remain accessible.
- [] Labels/configuration/as-builts let another technician service the system.

Still required to release this work

- [] Electrician/lighting designer issues architecture, load schedule, device SKUs and riser.
- [] Greg approves interface and scene levels.

Manufacturer instructions + sources

[Diode driver family](#)
[Reflected ceiling plan](#)

PWR-01 · Surveyed electrical + low-voltage work

Electrician + AV · service · Drawing E01

MATERIAL / COMPONENT	QUANTITY BASIS	SPECIFICATION + RELEASE
Branch-circuit/receptacle work	1 engineered scope	Circuits, breakers, conductor/raceway and device types/quantities derive from licensed survey and load design. not designed
Receptacles/boxes/plates	1 device schedule	Locations for AV, TV, fridge, lighting and general use; exact ratings and finishes by electrical schedule. unselected
Low-voltage pathways	1 route schedule	Separate labeled pathways for analog, digital, network, display and member-laptop connections. not designed
Cable supports/trays/grommets	1 measured set	Accessible, bend-radius-safe components coordinated with desk/rack and millwork. unselected
Labels and as-built directory	1 set	Permanent circuit, pathway and endpoint labels. required

Tools + access

licensed electrical test equipment · circuit tracer · load logger as required · grounding/noise test tools · label printer

Before starting

- ☐ M-09/M-10 trace panel, loads, grounding and controls.
- ☐ AV supplies rack/power/signal requirements.
- ☐ Permit/review and outage plan are approved.

Install in this order

1. Create circuit/load/device and low-voltage pathway schedules.
2. Coordinate boxes, routes and access with millwork, mirrors, panels and ceiling.
3. Install permitted rough-in, supports and accessible boxes; maintain separation.
4. Inspect before closure and photograph routes with dimensions.
5. Terminate devices, update panel directory and label endpoints.
6. Energize/test polarity, grounding, loads and GFCI/AFCI functions as applicable.
7. Run joint AV hum/static diagnosis without defeating safety earth.

Accept the work when

- ☐ Inspection passes and directory/device labels match as-built.
- ☐ No hidden inaccessible junction or blocked service route.
- ☐ Recorded power arrangement supports cold-start AV tests without unsafe grounding workarounds.

Still required to release this work

- ☐ Licensed electrician supplies code design, device/circuit/conductor/raceway schedule and inspection record.
- ☐ AV integrator supplies load and pathway requirements.

Manufacturer instructions + sources

Reflected ceiling coordination
Trade scope TR-03/TR-07

AV-01 · Retained AV + plug-and-play commissioning

AV engineer · service · Drawing A01

MATERIAL / COMPONENT	QUANTITY BASIS	SPECIFICATION + RELEASE
Retained AV/electronics inventory	1 verified set	PMC/HS8/Turbosound, interfaces, Trinnov, sub, rack electronics, Korg and member-laptop station; identities/conditions to reconcile. owned-check
Rack hardware and cable management	1 scheduled set	Shelves, blanks, cage hardware, ventilation, trays and strain relief from final rack elevation. unselected
Audio/data/display cables and adapters	1 pull schedule	Types, lengths, connectors and spares from signal-flow and pathway plan. unselected
R-number cable labels	1 complete set	Durable label at both ends/head plus patch/rack records. required
PA pole/base restraint and floor protection	1 set	Actual load/footprint/aim and occupied-path stability to verify. unverified

Tools + access

audio analyzer/interface · calibrated measurement mic · cable tester · network tester · label printer · SPL meter

Before starting

- [] M-11 reconciles model plates and dimensions; M-14 captures baseline.
- [] Issue rack elevation, signal flow, patch map, cable/pull schedule and power plan.
- [] DESK-01 and PWR-01 service paths are complete.

Install in this order

1. Photograph, label and test retained items before relocation.
2. Install rack hardware/power/cable management from approved elevation.
3. Pull and terminate labeled cables with required separation and service loops.
4. Set monitors, PA, Korg, amps and laptop station from released plan.
5. Patch and trace every R-number path with a second person.
6. Diagnose hum/static jointly with electrician; do not lift safety earth.
7. Run cold-start, latency, monitoring, PA coverage, TV, booth and member-laptop tests; archive results.

Accept the work when

- [] Every retained item is identified, functional and located in the as-built record.
- [] Every labeled cable traces to the patch/signal-flow drawing.
- [] Cold-start member workflow, Korg always-on audio, monitoring and PA coverage pass.

Still required to release this work

- [] AV integrator supplies rack elevation, signal flow, cable/connector quantities, power loads and commissioning forms.
- [] Greg documents Trinnov/sub/Furman/no-sleep operating rules.

Manufacturer instructions + sources

[Room plan](#)
[Korg product reference](#)
[AV trade scope](#)

BOO-01 · Booth fabric/absorber work + cloud review

Acoustician + carpenter · custom · Drawing A05

MATERIAL / COMPONENT	QUANTITY BASIS	SPECIFICATION + RELEASE
Wall absorber assemblies	6 provisional panels	Nominal 24 x 48 x 2 in only; core, frame, fabric, fire data and final quantity follow M-14 design. provisional
Ceiling cloud assembly	1 provisional cloud	Nominal 48 x 48 in only; weight, suspension, air gap and secondary safety by qualified design. provisional
Acoustic fabric/trim	1 field takeoff	Finish selected with complete panel/core test documentation. unselected
Wall mounting hardware/backing	1 engineered set	Substrate-specific supports from treatment elevation. not designed
Cloud suspension/support	1 engineered set	Structure-specific suspension and safety provisions; no generic anchors. not designed

Tools + access

measurement microphone/system · laser/level · backing locator · access equipment · manufacturer mounting tools

Before starting

- ☐ M-05/M-07 survey booth/glass/walls/ceiling and M-14 measure baseline.
- ☐ Acoustician issues treatment locations, performance target and product assembly.
- ☐ Support designer releases cloud load/suspension and backing.

Install in this order

1. Protect sliders, kit, camera, HVAC and retained absorption.
2. Install/photograph approved wall and ceiling backing before closure.
3. Fabricate/receive panels and verify labels, dimensions, weight, finish and fire data.
4. Lay out wall panels/cloud from issued A05 elevations.
5. Mount wall panels with specified hardware and service removability.
6. Suspend cloud under released design with all safety provisions.
7. Restore gear and run post-install acoustic/HVAC/noise measurements.

Accept the work when

- ☐ Panels/cloud match approved locations and remain stable/serviceable.
- ☐ No obstruction to sliders, HVAC, camera, mic boom, TV or kit access.
- ☐ Before/after measurements and assembly documentation meet acoustician acceptance.

Still required to release this work

- ☐ Acoustician supplies core/frame/fabric system, final quantities, locations and target.
- ☐ Qualified designer supplies cloud/backing loads, suspension and fasteners.

Manufacturer instructions + sources

[Booth plan](#)

[Acoustic/HVAC trade scope](#)

BOO-02 · Booth floor finish + retained rug

Flooring · custom · Drawing A05

MATERIAL / COMPONENT	QUANTITY BASIS	SPECIFICATION + RELEASE
Charcoal low-pile carpet tile or approved acoustic floor	1 field takeoff	Final product/SKU/color/tile size follows curved booth and vestibule template. unselected
Manufacturer-approved adhesive/tackifier	1 coverage takeoff	Compatible with tested substrate and future service/removal intent. unselected
Subfloor prep materials	1 field allowance	Patch/level/moisture system selected after M-08. field-dependent
Slider/threshold/edge transitions	1 measured set	Low-profile profiles that preserve both slider tracks and kit access. unselected
Retained Persian rug	1 rug	Condition, exact size, cleaning and keep/remove decision to record. retained-check

Tools + access

template material · moisture/flatness tools · flooring cutters · adhesive tools per maker · roller if specified

Before starting

- [] M-05 templates curve/vestibule/sliders and M-08 tests substrate.
- [] Approve floor and retained-rug samples/condition.
- [] Issue tile pattern, takeoff, adhesive and transition detail.

Install in this order

1. Remove/protect booth contents and slider tracks.
2. Prepare substrate to selected system and document moisture/flatness.
3. Snap layout from approved datum and pre-cut curved/threshold edges.
4. Apply approved adhesive/tackifier and install tiles in released pattern.
5. Install transitions without reducing slider operation or kit path.
6. Clean/cure, replace approved rug and test all slider layers.

Accept the work when

- [] No loose edge, trip point or adhesive contamination in tracks.
- [] Sliders, doors, kit movement and mic-boom use remain clear.
- [] Product lot, spare tiles, cleaning and warranty records are delivered.

Still required to release this work

- [] Flooring installer supplies final product, quantity, substrate/adhesive and transition schedule.

Manufacturer instructions + sources

[Booth plan](#)

BOO-03 · Booth warm lights + service checks

Electrician + HVAC + AV · service · Drawing A05

MATERIAL / COMPONENT	QUANTITY BASIS	SPECIFICATION + RELEASE
4-in 2700K booth downlights Product / instructions	2 fixtures	Exact fixture/black trim/driver selected after cloud/ceiling survey; may use approved Nora family if compatible. unselected
Separate booth dimmer/control	1 zone set	Independent of lounge with usable task-light scene. unselected
HVAC service/balance parts	1 field allowance	No parts selected until airflow/noise/access survey identifies need. field-dependent
AV/service cable hardware	1 field allowance	Mic, TV, desk and kit route supports/labels from booth AV schedule. unselected

Tools + access

ceiling inspection tools · electrical tester · light meter · airflow meter · measurement microphone · cable tester

Before starting

- [] Coordinate final cloud, camera, HVAC, mic boom and ceiling support.
- [] Trace booth circuit/control and approve fixture/driver/dimmer compatibility.
- [] Record baseline airflow/noise and retained AV condition.

Install in this order

1. Issue booth reflected ceiling/service plan.
2. Complete inspected electrical rough-in and any documented HVAC service.
3. Install two fixtures with accessible drivers and clear cloud/suspension zones.
4. Install/label booth AV supports and restore TV/desk/kit/mic routes.
5. Program separate booth task and dim scenes.
6. Measure light, airflow, noise and AV operation with booth configured.

Accept the work when

- [] Two fixtures and controls operate without cloud/camera/mic conflicts.
- [] Air path and service access remain open; HVAC/noise results are documented.
- [] Booth TV, desk, kit and microphone workflow pass.

Still required to release this work

- [] Electrician selects fixtures/control and supplies circuit detail.
- [] HVAC/acoustic consultant defines any service parts and acceptance values.
- [] AV integrator supplies booth cable route.

Manufacturer instructions + sources

[Booth plan](#)
[Nora candidate](#)

CLOSE-01 · Styling, spare materials + handover

Lead builder + Greg · service · Drawing A01

MATERIAL / COMPONENT	QUANTITY BASIS	SPECIFICATION + RELEASE
Approved plant and vessel	1 set	Live/faux decision, size and maintenance selected to avoid speakers, instruments and service paths. unselected
Restrained brass/black accessories	1 curated set	Quantities and shelf loads approved after room commissioning. unselected
Flameless candles	1 set	Battery/rechargeable only; no open flame. unselected
Spare finish materials	1 handover set	Labeled paint, flooring, fabric, slat, LED and trim spares by installed lot. required
Operations/as-built binder	1 digital+print set	As-builts, submittals, warranties, cleaning, patch/circuit/signal maps, driver/access photos and open items. required

Tools + access

label printer · camera · inventory bins · cleaning tools approved for each finish

Before starting

- [] All construction, commissioning and punch work is complete.
- [] Speaker/airflow/service/egress zones are marked for styling.
- [] Collect current product and care records from every trade.

Install in this order

1. Walk the complete room with Greg and close or log punch items.
2. Place styling items within approved loads and clear zones.
3. Inventory and label spare materials by product/lot/location.
4. Assemble searchable as-builts, photos, manuals, warranties and configuration backups.
5. Demonstrate lighting, AV, appliance, cleaning and service access.
6. Record open items, owners and dates; obtain handover signature.

Accept the work when

- [] No styling item blocks airflow, speakers, instruments, egress or service access.
- [] Spare materials and records reconcile to installed products.
- [] Owner can operate scenes, AV, fridge and access service points from handed-over instructions.

Still required to release this work

- [] Each trade supplies final as-builts, warranties, cleaning and spare quantities.
- [] Greg approves final styling selection.

Manufacturer instructions + sources

[Room plan](#)
[Build phase P6](#)

Sequence · 7 phases / 44 checks

PROGRESS CONTROL

Check boxes capture progress and evidence. They never release affected purchase, fabrication, permit, engineering or installation holds. Revisions caused by field findings flow through every affected layout and review.

P0 · Freeze the field record

Owner · Owner representative + field survey lead

Sequence allowance · Low-confidence allowance: 1-2 site days after access

Depends on · None

Ready when

- ✓ Current brief, approved concept, frozen Pass 7 source commit 1a1d56d, initial 70-element snapshot, labeled plan and inventory are in the field packet.
- ✓ Main room, closet, vestibule and booth are accessible with ceiling and electrical access arranged.

- ☐ **P0-T1** · Laser-check every main-room wall, both diagonals, ceiling height at four points and both bay returns.

Evidence · Dimension log, marked plan and scale photos agree.

- ☐ **P0-T2** · Survey D-2, the south-wall D-3 entry at x 0.99..37.31, the nominal 34 by 46 inch closet, the 29.04 inch vestibule, both 70.6 inch slider layers and the nominal 123 by 95 inch booth body from named control points.

Evidence · Openings, jams, swings, thresholds and glass overlap are recorded; D-3 is photographed from both sides with its west-jamb hinge and northward swing into the room identified.

- ☐ **P0-T3** · Open one approved ceiling and wall inspection point; record plenum, structure, studs, backing and acoustic-fabric build-up.

Evidence · Photos include a ruler and the exact inspection location.

- ☐ **P0-T4** · Photograph the panel schedule, breakers, receptacles, data plates, tie lines, lighting controls and HVAC supply/return path.

Evidence · Each device is keyed to the marked plan.

- ☐ **P0-T5** · Audit every retained instrument, speaker, rack item and booth object against the inventory by model and current location.

Evidence · Discrepancies are listed without relabeling assumed items as owned.

- ☐ **P0-T6** · Lay out the current proposed west-wall sequence and the rest of the room full size: NU1X center x9.5/z90 at 270 degrees, 16.4375-inch modeled body gap, 48-inch bar center x13/z160 at 270 degrees, stools at x37/z142, 160 and 178, uninterrupted west wall, lounge, desk, Korg and the south-entry and D-2 swings. Test the proposed 26-inch bar depth required by the verified refrigerator candidate.

Evidence · Dimensioned photos show the north-to-south west-wall order, furniture and occupied envelopes, access route and both door swings; neither bar depth, gap nor any seating fit is released by the mockup alone.

- ☐ **P0-T7** · Complete M-16 before revising the floor plan: survey both raised platforms in front of the left and right storage doors facing the speakers.

Evidence · The field record gives each platform width, depth and height from the main finished floor; step or slope geometry; threshold as a separate reading; offsets to adjacent door and wall corners; door-clearance operation; and labeled scale photos plus a dimensioned sketch.

Stop if

- ! Any shell discrepancy changes fit, access or a fabrication dimension; discrepancies over 2 percent escalate immediately to Greg and the design professional.
- ! The labeled-plan door or booth geometry does not match the room.
- ! Ceiling, wall, floor or panel access cannot be inspected safely.

P1 · Issue the coordination set

Owner · Design professional + general contractor

Sequence allowance · Low-confidence allowance: 1-3 weeks after the field record

Depends on · P0

Ready when

- ✓ Field record is signed and dated.
- ✓ Every conflict has an owner and a written resolution path.

- ☐ **P1-T1** · Redraw the main room, closet, vestibule and booth from the original-record controls and field record; keep the west wall uninterrupted and place D-3 on the south boundary at its west end.

Evidence · Plan dimensions close and match the field log.

- ☐ **P1-T2** · Prepare furniture, equipment, door-swing and access plans around the approved three-stool concept, the TV between the right-wall instruments and every field-recorded raised platform.

Evidence · The plan shows NU1X north of the bar, D-3 on the south boundary with its west hinge and northward swing, both raised platforms, and every unresolved seating and equipment-fit hold.

- ☐ **P1-T3** · Prepare north, west, bay and booth elevations with AFF heights, mounting zones and field-verified backing.

Evidence · Mirror, shelf, piano, desk, TV, actual instrument, absorber, platform and 94.49-inch slat-panel termination heights are dimensioned.

- [] P1-T4** · Prepare a reflected ceiling plan for the ceiling mirror, cove, downlights, track, booth lights, detectors and retained devices.
Evidence · Every fixture has a coordinate, circuit/control zone and access note.
- [] P1-T5** · Have the electrician and building official or design professional confirm permit/review scope, egress criteria and the 36-inch planning target.
Evidence · Written direction states the governing review and required path width.
- [] P1-T6** · Issue structural attachment details for wall mirrors, overhead mirror, TV mount, instrument blocking, track, panels and ceiling-mounted work.
Evidence · Details name substrates, fasteners, loads and inspection hold points.
- [] P1-T7** · Set change control: every field or as-built departure updates each affected plan, elevation, reflected ceiling plan, fit check, quote and order before work resumes.
Evidence · Revision log names the changed dimension, downstream documents, reviewer and release decision.

Stop if

- ! Permit or review responsibility is still unnamed.
- ! Door swings, access path or equipment service zones remain unresolved.
- ! Any attachment detail relies on unverified backing or ceiling structure.

P2 · Quote, sample and release purchases

Owner · Owner representative + general contractor
Sequence allowance · Vendor lead times; release only after field and design holds clear
Depends on · P1

Ready when

- ✓ Issued coordination drawings carry a revision and date.
- ✓ Quote requests use field-verified quantities and written alternates.

- [] P2-T1** · Quote five wall arches and the overhead mirror as separate packages with safety, edge, backing, weight and attachment data.
Evidence · Glazier quote follows issued dimensions and attachment details.
- [] P2-T2** · Quote the 48-inch bar, shelves and three stools with the Pass 7 source's 24-inch depth and the proposed 26-inch depth allowance; coordinate the Zephyr body, 1-inch rear plug clearance, front vent and service pullout against the uninterrupted west wall.
Evidence · Shop drawing proves appliance, outlet, vent and pull-out service while the full-size layout records the current furniture and occupied envelopes; depth, gap and seating remain held for Greg's approval.
- [] P2-T3** · Obtain samples for wall finishes, 94.49-inch slat panels, booth finishes, a compatible dark-floor assembly and the explicit keep-oak-plus-rugs alternative.
Evidence · Approved sample board records product, color, sheen, assembly, fire data and room location.
- [] P2-T4** · Quote the complete lighting and control package from the reflected ceiling plan, including drivers, dimming, emergency compatibility and commissioning.
Evidence · Fixture and control schedule has approved SKUs and substitutions.
- [] P2-T5** · Confirm the 59.125 by 18.25 by 40.3125 inch NU1X, the 53.98 by 18.15 inch Grandstage X body and stand, PMC model, booth kit, selected TV and the six listed guitars/basses physically present.
Evidence · Purchase list separates owned, relocate, buy and pending-verification items and uses verified product envelopes.
- [] P2-T6** · Release long-lead orders only after field dimensions, finish samples, access path and written owner approval match the order.
Evidence · Order log records approver, revision, deposit, lead time and cancellation terms.

Stop if

- ! A quote uses the old 96-inch bar, four stools, reversed bar/piano order, invented west-wall D-3, old booth position or an uncoordinated refrigerator depth.
- ! A vendor substitutes a product without a reviewed sample or technical submittal.
- ! A long-lead item lacks verified delivery access or field dimensions.
- ! A field or as-built change has not been reviewed against every affected quote and order.

P3 · Protect, isolate and open the work**Owner** · General contractor**Sequence allowance** · Low-confidence allowance: 2-4 site days**Depends on** · P1**Ready when**

- ✓ Permit/review path and selective-demolition scope are documented.
- ✓ Retained equipment, glass, flooring and acoustic fabric are tagged and protected.

- ☐ **P3-T1** · Photograph, label, disconnect and relocate retained AV, instruments and booth contents to a protected inventory zone.

Evidence · Move log identifies each item and destination.

- ☐ **P3-T2** · Protect the oak LVP, sliders, closet door, camera, grille and acoustic fabric while flooring and finish decisions remain open.

Evidence · Protection is continuous at traffic and dust paths.

- ☐ **P3-T3** · Remove the main-room and booth troffers, abandoned fixtures and only the finishes marked for removal on issued drawings.

Evidence · Circuits are made safe and removed items are logged.

- ☐ **P3-T4** · Open only the wall and ceiling areas needed for approved backing, wiring, lighting and inspection.

Evidence · Hidden conditions are photographed before concealment.

- ☐ **P3-T5** · Confirm whether the oak LVP is floating or adhered, then record flatness, moisture, threshold build-up and dark-floor assembly options.

Evidence · Installer states whether the proposed product is warrantable; oak removal remains a Greg approval hold.

Stop if

- ! Demolition exposes moisture, damaged framing, unsafe wiring or undocumented isolation construction.
- ! The acoustic fabric cannot be removed and reinstated as assumed.
- ! Protected equipment or glass remains in the active work zone.
- ! A hidden condition changes an issued layout and the affected documents have not been reissued.

P4 · Complete rough-in and backing**Owner** · General contractor + licensed electrician + AV integrator**Sequence allowance** · Low-confidence allowance: 1-2 weeks, subject to inspection**Depends on** · P2, P3**Ready when**

- ✓ Approved submittals and attachment details are on site.
- ✓ Wall and ceiling cavities are open for coordinated work.

- ☐ **P4-T1** · Install inspected backing for arches, shelves, TV mount, instrument hangers, slat panels, displays, absorbers and ceiling mirror supports.

Evidence · Backing photos include dimensions before closure.

- ☐ **P4-T2** · Install permitted branch circuits, receptacles, drivers and controls from the electrician's field-verified design.

Evidence · Rough inspection and circuit directory are complete.

- ☐ **P4-T3** · Route separate labeled pathways for power, analog audio, digital audio, network, display and member-laptop connections.

Evidence · Pathway plan and pull labels match the rack schedule.

- ☐ **P4-T4** · Rough in the cove, downlights, guitar track, mirror halos, bar LEDs and booth lighting from the approved ceiling and control plans.

Evidence · Driver access and fixture cutouts are verified before closure.

- ☐ **P4-T5** · Service the documented HVAC scope without covering the closet grille, return path, controls or camera view.

Evidence · Air path and maintenance access remain open.

- ☐ **P4-T6** · Run an inspection hold before walls and ceiling close; compare every rough-in to the issued revision.

Evidence · Signed punch list is closed or carried visibly.

Stop if

- ! Electrical capacity, grounding topology or control compatibility is unresolved.
- ! A ceiling fixture or mirror support lacks verified structure.
- ! Door, slider, HVAC or equipment-service access is obstructed.
- ! Installed rough-in departs from the issued revision without downstream layout review.

P5 · Install shell, finishes and fixed elements

Owner · General contractor + finish trades

Sequence allowance · Low-confidence allowance: 1-3 weeks plus vendor lead time

Depends on · P4

Ready when

- ✓ Rough inspections and concealment photos are complete.
- ✓ Approved samples and field templates are on site.

- [] P5-T1** · Close and finish wall and ceiling openings; apply the controlled main-room wall-finish decision and matte-black ceiling finish.

Evidence · Mockup, sheen and acoustic-treatment disposition match the approval record.

- [] P5-T2** · Execute Greg's approved floor decision: keep oak with rugs, or remove/preserve it as feasible and install a warrantable dark-floor assembly; complete the booth floor finish.

Evidence · Written approval, installer warranty, transitions and door/slider operation are recorded.

- [] P5-T3** · Install the approved bar, shelves, fridge, slat-panel termination and desk; preserve appliance, rack and cable service access.

Evidence · Millwork dimensions, refrigerator clearances, 102-inch-wall panel joint/trim and service openings match submittals.

- [] P5-T4** · Install wall arches and overhead mirror under the approved glazing and attachment details.

Evidence · Glazier documents safety backing, edge condition, fasteners and final inspection.

- [] P5-T5** · Install booth absorbers, ceiling cloud and lighting while retaining sliders, kit sightline, TV, desk and mic-boom use.

Evidence · Booth plan and elevations match the installed work.

- [] P5-T6** · Mount the approved TV-and-instrument layout from the full-size M-13 field template only after the actual instruments and selected TV are assigned.

Evidence · The TV body, mount, connectors and service path clear every yoke, instrument body, headstock, removal arc, light, desk and speaker; install only the field-approved instrument count.

Stop if

- ! A field template or as-built condition differs from an issued layout and the affected documents have not been reviewed and reissued.
- ! Mirror, millwork or flooring dimensions require site cutting outside approved tolerances.
- ! A finish change would remove acoustic treatment without written disposition.

P6 · Set equipment, commission and hand over

Owner · AV integrator + general contractor + owner representative

Sequence allowance · Low-confidence allowance: 2-4 commissioning days

Depends on · P5

Ready when

- ✓ Fixed work is complete, clean and powered.
- ✓ Open inspection and safety items are closed.

- [] P6-T1** · Set the approved three stools, NU1X, lounge, Korg, desk, monitors, rack, amps and booth kit from the verified plan, preserving the north-to-south west-wall order of NU1X and bar and keeping the south entry clear.

Evidence · Full-size layout, recorded seating clearances and both door swings match the approved field record.

- [] P6-T2** · Patch and label every cable R-01 onward at the cable head; issue rack, tie-line and signal-flow records.

Evidence · A second person traces each labeled path successfully.

- [] P6-T3** · Have the electrician and AV integrator test circuits, investigate hum/static and document the accepted power arrangement.

Evidence · Test record names the observed fault, corrective work and retest result.

- [] P6-T4** · Commission lounge, session and meditation lighting scenes at 2700K; verify all controls, drivers and service access.

Evidence · Scene levels and control labels are recorded.

- [] P6-T5** · Measure room response, noise floor and HVAC-on/HVAC-off conditions; tune monitoring from the recorded baseline.

Evidence · Before/after files, mic position and settings are archived.

- [] P6-T6** · Verify member laptop audio, always-on Korg audio, Turbosound PA coverage and stability, no-sleep computer, separate Apollo/TV power, empty front Furman plug and always-powered Trinnov/sub rules.

Evidence · A cold-start member workflow completes without troubleshooting; PA aiming and cable routes preserve occupied access.

- [] P6-T7** · Deliver as-builts, change-impact log, approved submittals, warranties, spare finishes, cleaning instructions and open-item log.

Evidence · As-builts include every approved field change and the owner representative signs the handover record.

Stop if

- ! Door, slider, access or required egress path is blocked.
- ! Electrical noise, overheating, control failure or unstable mounting remains.
- ! The member workflow or retained power rules fail the witnessed test.

Trade scope + acceptance

Use these boundaries in bid invitations and coordination reviews. Exclusions are named so work is not assumed by silence.

TR-01 · General contractor / site coordinator

SCOPE	• Site logistics, protection, selective demolition, sequencing and daily coordination. • Coordinate main room, closet, vestibule and booth as one work area.
DELIVER	• Baseline schedule with low-confidence allowances identified. • Submittal, RFI, inspection, photo and punch logs.
ACCEPT	✓ Issued revision is present at each installation. ✓ Retained items and access routes remain protected and usable.
EXCLUDES	– Structural, electrical, HVAC, acoustic or code design outside the contractor's license.

TR-02 · Design professional / permit coordinator

SCOPE	• Field-verified plans, elevations, reflected ceiling plan and attachment coordination. • Confirm permit/review and egress criteria with the building official.
DELIVER	• Issued coordination set with revision history. • Written permit, review and inspection matrix.
ACCEPT	✓ Drawings reconcile the corrected doors, vestibule, booth and closet. ✓ Locked owner decisions are visible and unresolved choices are marked.
EXCLUDES	– Treating the concept render or old v0.1 draft as permit documents.

TR-03 · Licensed electrician / lighting controls

SCOPE	• Survey panel, circuits, grounding topology, fixtures, controls and available capacity. • Design and install permitted power and lighting work.
DELIVER	• Circuit and control schedules, fixture submittals and test results. • Updated panel directory and as-built device plan.
ACCEPT	✓ Rough and final inspections pass. ✓ Lighting scenes, drivers, dimming and service access work under load.
EXCLUDES	– Assuming a ground-loop cause or copying the unverified old circuit scheme.

TR-04 · Carpenter / millworker / flooring installer

SCOPE	• Backing, bar, shelves, desk interfaces, wall preparation, slat panels and floor finishes. • Build from field templates at bay, closet, door and slider edges.
DELIVER	• Shop drawings, finish samples, hardware schedule and field templates. • Substrate, floor-flatness, floor-assembly and transition report.
ACCEPT	✓ Fixed work matches verified dimensions and approved samples. ✓ Appliance, rack, cable, door and slider service access remains open.
EXCLUDES	– Changing the 48-inch bar, three stools or approved TV-between-instruments direction, removing oak flooring or hiding a slat-panel joint without written approval.

TR-05 · Glazier / mirror installer

SCOPE	• Five wall arches, overhead mirror, edge treatment, safety backing and attachment system. • Coordinate halos, brass trim, access panels and adjacent finishes.
DELIVER	• Shop drawings, glass makeup, weights, samples and attachment calculations. • Installation and final inspection record.
ACCEPT	✓ Glass, backing, edges and supports match approved details. ✓ No exposed sharp edge, unstable panel or blocked service access remains.
EXCLUDES	– Fabricating from concept-image proportions or unverified ceiling structure.

TR-06 · HVAC / acoustic consultant

SCOPE	• Document supply, return, airflow, noise and main-room/booth acoustic baseline. • Review wall-fabric disposition, booth absorbers and ceiling cloud.
DELIVER	• HVAC access and performance note. • Before/after acoustic measurements and treatment placement plan.
ACCEPT	✓ Air path, maintenance access and camera/grille clearances remain open. ✓ Treatment decisions cite measured conditions rather than assumed NRC.
EXCLUDES	– Claiming the existing grey fabric's performance without testing or construction data.

TR-07 · AV / studio integrator

SCOPE	• Verify equipment, rack, monitoring, Turbosound PA/pole north of desk, patching, laptop workflow, labels and signal paths. • Coordinate AV power and low-voltage routes with the electrician.
DELIVER	• Equipment and cable schedule, rack elevation, patch map and signal-flow drawing. • Commissioning record for monitoring and member workflow.
ACCEPT	✓ All R-number labels trace correctly. ✓ Cold-start laptop, Korg, DAW, PA coverage and monitoring tests pass.
EXCLUDES	– Substituting IB1S for IB1 or moving unidentified inventory without approval.

Retained conditions + gear

DEFAULT ACTION	Protect, identify and verify retained work before removals. An unknown existing assembly stays in place until the named decision is made.
R-01	Existing light-oak LVP; dark-floor change remains controlled
VERIFY	Floating versus adhered assembly, substrate, moisture, flatness, transitions and door clearances.
ACTION	Protect and keep oak-plus-rugs explicit; if the selected dark floor requires removal, obtain Greg's written approval and preserve the oak where feasible.
R-02	Grandfathered existing grey acoustic fabric and hidden wall assembly
VERIFY	Construction, attachment, condition and measured acoustic contribution.
ACTION	Keep in place until the controlled finish/acoustic decision is issued.
R-03	HVAC closet, D-2, supply grille and dome camera
VERIFY	Field dimensions, airflow, access, swing and camera view.
ACTION	Protect and keep serviceable; finish only exposed approved faces.
R-04	D-3 entry and required access path
VERIFY	South-wall opening at x 0.99..37.31, west-jamb hinge, northward swing into the room, hardware, threshold and official egress criteria.
ACTION	Keep the full swing and reviewed path clear through every phase.
R-05	Two-layer sliding glass booth doors
VERIFY	Track condition, pane makeup, overlap, seals, head height and service access.
ACTION	Protect, clean and retain unless a reviewed repair is required.
R-06	Booth kit, Persian rug, desk, TV and mic boom
VERIFY	Actual identity, dimensions, condition and deployed positions; Pass 7 records the Persian rug as a provisional 66 by 88 inches from photos, still requiring field measurement, and includes no booth floor lamp.
ACTION	Inventory before moving; reset from the verified booth plan.
R-07	Korg Grandstage X and sitting-height stand
VERIFY	53.98 by 18.15 inch body, stand footprint, bench, music rest, pedals, cable bend, power, audio and MIDI paths.
ACTION	Keep in the main room and always available in audio.
R-08	HS8 pair, PMC pair, Turbosound PA/pole, rack and production electronics
VERIFY	Models, stand/base footprints, pole stability, PA aiming, service clearances, signal paths and power behavior.
ACTION	Protect, label, reinstall and commission; do not infer the PMC model.
R-09	Front Furman outlet, Trinnov and sub power rules
VERIFY	Witness current behavior and accepted electrician/AV power arrangement.
ACTION	Keep the front plug free; preserve required always-powered devices in the commissioned workflow.

Site-survey register · 16 bundles

RECORD ONCE		Photograph the mark, keep the raw reading, identify the measuring face and enter the result in the dated revision record. Findings update all affected plans, quantities and release reviews.
M-01	Main-room polygon and diagonals Greg tape measurement from May 2026; measured-as-typed, unverified current. A 2 percent discrepancy triggers escalation and redesign review, not fabrication tolerance.	
METHOD	Laser each wall at floor and 60 inches AFF; tape-check both diagonals.	
RECORD	Marked plan, raw readings, closure calculation and scale photos.	
UNLOCKS	P1-T1 · P1-T2 · P2-T2	
M-02	Bay face and canted returns Typed polygon gives 30.54 and 28 degrees; least reliable shell dimensions.	
METHOD	Measure both return lengths, offsets from the east wall line, face length and corner angles.	
RECORD	Four control points, diagonals and a rigid full-size desk-wall template.	
UNLOCKS	P1-T2 · P1-T3 · P5-T3 · P5-T6	
M-03	Ceiling plane, plenum and structure No original room plan states the ceiling height. The 102-inch plane is a low-confidence working assumption; slab/drop construction and load capacity are unknown.	
METHOD	Laser floor-to-ceiling at four points; inspect one approved opening to structure.	
RECORD	Heights, plenum depth, framing direction, member spacing and photos.	
UNLOCKS	P1-T4 · P1-T6 · P2-T1 · P4-T4	
M-04	D-2 and D-3 door schedule The 2024 plan vectors place D-3 on the south boundary at x 0.99..37.31 after normalization, hinged at the west jamb and swinging north into the room. That planner registration is moderate-confidence; current opening, clear width, hardware and head remain unverified.	
METHOD	Measure rough and finished openings, leafs, jambs, hinges, swings, thresholds and hardware.	
RECORD	Door schedule with photos from both sides and swing arcs on plan.	
UNLOCKS	P1-T1 · P1-T2 · P1-T5 · P6-T1	
M-05	Booth, vestibule and sliders The 2024 plan prints a 123 by 95 inch nominal booth body. Its vectors register a 29.04 inch vestibule and two parallel 70.6 inch slider layers aligned at x 75.65..146.25 for planning; curve, leaf position and head remain unverified.	
METHOD	Survey control points for vestibule depth, booth boundaries, curve, glass tracks, overlap and head height.	
RECORD	Point list, curve offsets, slider section and booth interior dimensions.	
UNLOCKS	P1-T1 · P1-T3 · P5-T5	
M-06	HVAC closet, grille and camera Closet is nominally 34 by 46 inches from the labeled plan; field size and HVAC performance are unknown.	
METHOD	Measure closet faces, door, grille, camera view, access panels and visible duct path.	
RECORD	Plan/elevation dimensions plus access and maintenance envelopes.	
UNLOCKS	P1-T1 · P4-T5	

M-07	Wall build-up and backing Existing grey stretched fabric is confirmed; its construction and acoustic performance are unknown.
METHOD	Open one approved fabric panel; locate studs and measure layers, spacing and existing blocking.
RECORD	Annotated section, stud map, photos and attachment assessment.
UNLOCKS	P1-T3 · P1-T6 · P4-T1

M-08	Floor, substrate and thresholds Light-oak LVP is existing. Karndean SCB89 forbids installation over a floating floor; existing installation and substrate are unknown.
METHOD	Inspect one threshold, determine floating versus adhered installation, map flatness, measure existing plank and test moisture for each proposed assembly.
RECORD	Substrate report, warranty statement, transition heights, door clearances and keep-oak/dark-floor options.
UNLOCKS	P2-T3 · P3-T5 · P5-T2

M-09	Panel, circuits and device map No verified panel or circuit schedule exists for this room.
METHOD	Licensed electrician traces breakers and records receptacles, loads, grounding topology and controls.
RECORD	Panel photo, circuit schedule, device plan and test notes.
UNLOCKS	P1-T4 · P2-T4 · P4-T2 · P6-T3

M-10	Existing lighting and control Prior rig was partly moved; current fixtures and control are unverified.
METHOD	Count, locate and energize each troffer, can, track head, entertainment fixture, switch and controller.
RECORD	Fixture map, circuit/control response and retained/remove disposition.
UNLOCKS	P1-T4 · P2-T4 · P4-T4

M-11	Gear identity and dimensions Manufacturer data gives NU1X 59.125 W by 18.25 D by 40.3125 H inches and Grandstage X 53.98 W by 18.15 D inches excluding stand; field identity and installed envelopes remain open.
METHOD	Read model plates and measure actual PMC cabinets/stands, piano, Grandstage body/stand, drum kit, PA, display, desk and rack.
RECORD	Photo inventory with model, quantity, location and measured envelope; compare against manufacturer dimensions.
UNLOCKS	P2-T5 · P6-T1 · P6-T2

M-12	Full-room floor fit The v1.5 plan uses current selected-furniture body sizes and the ReferenceLayout.affordable proposed poses. The 16.4375-inch piano-to-bar body gap is modeled, not taped; occupied clearances, raised platforms and physical fit have not been field-proven.
METHOD	Tape the current v1.5 furniture footprints and occupied envelopes at their issued rotations, including the conservative 90.5 by 36 inch Alpine sofa envelope at x83/z53, two 24.75 by 29.5 inch DYVLINGE chairs at x126/z103 rotated 90 degrees and x107/z145 rotated 150 degrees, NU1X center x9.5/z90 at 270 degrees, bar center x13/z160 at 270 degrees, three stools at x37/z142, 160 and 178, D-3 on the south boundary at x 0.99..37.31, both M-16 platforms, and every service zone. Operate doors, sliders, fridge, stools, chairs and service panels.
RECORD	Dimensioned overhead and corner photos; actual furniture and occupied-envelope clearances; south-wall D-3 northward swing; M-16 platform boundaries; access and service routes; and a signed current-layout sketch.
UNLOCKS	P1-T2 · P2-T2 · P6-T1

M-13	Full-size TV and instrument wall template The TV-between-instruments arrangement is approved design direction. Actual bodies and removal arcs control the count; no ten-instrument fit is promised.
-------------	---

METHOD	Place the selected TV between the right-wall guitars/basses. Trace the actual TV body and mount plus every physically present instrument body, headstock, yoke and removal arc on paper or removable wall film at proposed elevations.
RECORD	TV body, mount, connector and service-clearance dimensions; instrument-to-position map; yoke centers; removal arcs; field-approved display count; and interference photos.
UNLOCKS	P1-T3 · P4-T1 · P5-T6

M-14	Acoustic and HVAC baseline No measured RT60, noise-floor, bleed or airflow baseline is on record.
METHOD	Record calibrated room response, noise floor and HVAC-on/off readings in the empty main room and booth.
RECORD	Audio files, mic position, settings, temperature and operating conditions.
UNLOCKS	P2-T3 · P5-T1 · P5-T5 · P6-T5

M-15	Delivery and service access No verified delivery route exists for piano, glass, millwork or selected lounge furniture.
METHOD	Measure the route from loading point to room, including doors, turns, stairs, elevator, thresholds and staging area.
RECORD	Route plan with minimum dimensions and item-specific handling notes.
UNLOCKS	P2-T1 · P2-T5 · P2-T6

M-16	Raised storage-door platforms Both raised areas are visible in the room condition but have no verified dimensions, profiles, offsets or operated-door clearance record.
METHOD	Survey both raised platforms in front of the storage doors at the left and right sides when facing the speakers. For each platform, measure width, depth and height from the main finished-floor datum; record every step or slope; measure the door threshold separately; and locate the platform from the nearest door jambs and wall corners.
RECORD	Separate left/right W × D × H records; main-floor datum; step/slope profile; threshold reading; door- and wall-corner offsets; operated door-clearance envelope; labeled scale photos; and a dimensioned plan plus section sketch.
UNLOCKS	P0-T7 · P1-T1 · P1-T2 · P1-T3

Candidate products + manufacturer sources

SELECTION STATUS

These are research-backed candidates or owned-equipment checks. A manufacturer link is evidence for the listed facts; it is not purchase authorization or a released project-specific assembly.

TCL-50Q651G	TCL 50Q651G 50-inch Q6 TV current-purchase-candidate · checked 2026-09-28
SOURCE	https://us.tcl.com/products/q-class-4k-uhd-hdr-qled-smart-tv-with-google-tv?variant=44055800053825
VERIFIED	✓ 43.7 W × 25.4 H × 2.8 D in without stand; 19.6 lb; VESA 300 × 300 mm. ✓ Same body envelope as the rendered 50S551G reference. ✓ \$299.99; the manufacturer variant maps to 50Q651G and listed available on September 28.
RELEASE	M-13 wall template, actual TV/mount manuals, backing, connectors, ventilation and instrument-removal clearance.

SANUS-BLL2-B1	SANUS Elite BLL2-B1 fixed TV mount candidate-fit · checked 2026-09-28
SOURCE	https://www.sanus.com/en_US/products/tv-mounts/bll2/
VERIFIED	✓ 0.67 in nominal wall offset; rated for 32–80 in TVs up to 150 lb. ✓ Universal interface includes 300 × 300 mm; installer must confirm the actual TV and substrate. ✓ \$89.99 retailer observation; TV plus mount is nominally 3.47 in deep before connector clearance.
RELEASE	Verify TV compatibility, blocking and cable/service access before drilling.

JONATHAN-Y-TRINITY-89893519	JONATHAN Y Trinity 30-inch backless stool hold-fit · checked 2026-09-28
SOURCE	https://www.target.com/p/-/A-89893519
VERIFIED	✓ 17 × 17 in body; 30 in seat height; 13.5 in seat diameter. ✓ Black metal seat, gold hairpin legs and footrest; unupholstered alternative to the leather reference. ✓ \$189.99 each / \$569.97 for three; retailer listed stock September 28.
RELEASE	Three 17 in bodies need 53 in at current 18 in centers, beyond the 48 in bar. Resolve quantity or bar layout in M-12 before buying.

RUGGABLE-SLOANE-BLACK-8X10	Ruggable Sloane Black flatwoven rug + Standard Pad candidate-size-change · checked 2026-09-28
SOURCE	https://ruggable.com/products/sloane-black-rug?variant=41460137525303
VERIFIED	✓ 8 × 10 ft charcoal/grey patterned cover and matching pad system. ✓ 12 in narrower than the modeled 9 × 10 ft rug; the room image has not been changed. ✓ \$579 observed; made to order, listed 1–2 week shipping.
RELEASE	Tape the actual rug edges in M-12 and confirm floor-finish compatibility. Buy one matching cover/pad system; do not double the pads.

BY-BOO-BUNGA-A-REFERENCE	By-Boo Bunga · size and appearance reference reference-only-out-of-stock · checked 2026-09-28
SOURCE	https://www.wayfair.com/furniture/pdp/by-boo-bunga-solid-coffee-table-yboo1890.html
VERIFIED	✓ 30 in diameter × 16 in high; black glass, black conical base and gold rim. ✓ \$614.99 observed, but the US listing showed out of stock.
RELEASE	Custom quote preserves the 30 × 16 in design. Fabricator designs glass thickness, edges, retention and stability.

TCL-50S551G	TCL 50S551G 50-inch S Class 4K TV dimensional-reference · checked 2026-09-28
SOURCE	https://us.tcl.com/products/tcl-50-s-class-4k-uhd-hdr-led-smart-tv-with-google-tv-50s551g
DIMENSIONS	W 43.7 in · D 2.8 in · H 25.4 in
VERIFIED	✓ TCL lists the body without stand at 43.7 inches wide, 25.4 inches high, and 2.8 inches deep. ✓ TCL lists the weight without stand as 19.6 pounds and the wall-mount pattern as VESA 300 by 300 millimeters. ✓ The model is used as the v1.4 dimensional reference. TCL's direct listing was sold out on September 28, 2026; it is not a released purchase.
RELEASE	Confirm the exact available model and delivered body, compatible listed mount, structural backing, connector and cable service, ventilation, glare, sightline, and full-size M-13 fit with actual instruments before purchase or drilling.

JENNIFER-TAYLOR-ALPINE-64 190-3-MBB	Jennifer Taylor Home Alpine 90-inch Sofa, Ebony Black Boucle selected-reference · checked 2026-09-28
SOURCE	https://www.jennifertaylorhome.com/alpine-90-sherpa-sofa-ebony-black-boucle/
DIMENSIONS	W 90.5 in · D 36 in · H 27.5 in · seat width 70.5 in · seat depth 24 in · seat height 17.5 in · arm height 27.5 in
VERIFIED	✓ The official dimension graphic lists 90.5 inches wide while the text specification lists 90 inches; this guide uses the conservative 90.5-inch planning width pending manufacturer confirmation. Depth is 36 inches and height is 27.5 inches. ✓ The listed seat is 70.5 inches wide by 24 inches deep by 17.5 inches high; arm height is 27.5 inches. ✓ The direct listing showed \$1,252.99 and ready to ship in 5 business days when checked.
RELEASE	Complete the M-12 occupied mockup and M-15 delivery-route check; resolve the 90 versus 90.5 inch published-width discrepancy with the manufacturer; verify current price, stock, timing, exact upholstery, delivery, and return terms before ordering.

IKEA-DYVLING E-80570831	IKEA DYVLINGE Swivel Chair, Keling Black selected-reference · checked 2026-09-28
SOURCE	https://www.ikea.com/us/en/p/dyvlinge-swivel-chair-keling-black-80570831/
DIMENSIONS	W 24.75 in · D 29.5 in · H 26.75 in · seat height 16.875 in
VERIFIED	✓ IKEA article 805.708.31 is listed at 24.75 inches wide, 29.5 inches deep, and 26.75 inches high. ✓ The listed seat height is 16.875 inches. ✓ The direct listing showed \$199 each, or \$398 for the selected pair, when checked.
RELEASE	Complete the M-12 occupied swivel-envelope mockup and M-15 route check; verify local stock, current price, delivery, and return terms before ordering two chairs.

YAMAHA-NU1X	Yamaha AvantGrand NU1X owned-check · checked 2026-09-26
SOURCE	https://usa.yamaha.com/products/musical_instruments/pianos/avantgrand/nu1x/specs.html
DIMENSIONS	W 59.125 in · D 18.25 in · H 40.3125 in
VERIFIED	✓ Yamaha lists the NU1X at 59-1/8 inches wide, 18-1/4 inches deep, and 40-5/16 inches high. ✓ Yamaha lists the weight as 240 pounds 11 ounces. ✓ Yamaha's regional NU1X specification page marks this exact model discontinued; the U.S. site retains its legacy specification and support page.
RELEASE	Measure the owned NU1X at its widest, tallest, and deepest points and confirm bench, power, service, and circulation clearances before bar millwork or final floor marking.

KORG-GRAND STAGE-X	Korg Grandstage X owned-check · checked 2026-09-26
SOURCE	https://www.korg.com/us/products/synthesizers/grandstage_x/
DIMENSIONS	W 53.98 in · D 18.15 in · H 6.61 in
VERIFIED	✓ Korg's owner manual lists the instrument at 53.98 inches wide, 18.15 inches deep, and 6.61 inches high, excluding the music stand. ✓ The listed weight is 55.12 pounds. ✓ The listed power consumption is 20 watts.
RELEASE	Measure the selected stand, bench, music rest, pedals, and rear cable bend in the room; then confirm door, HVAC, and playing clearances at the southeast position.

STRING-SWING-CC01K	String Swing CC01K Hardwood Home & Studio Guitar Keeper candidate · checked 2026-09-26
SOURCE	https://www.stringswing.com/guitar-hanger-hardwood-wall-mount-for-acoustic-and-electric-guitars/
VERIFIED	✓ The pivoting yoke is padded and is rated by String Swing for instruments up to 15 pounds. ✓ The hardwood block is offered in Cherry, Oak, Ash, and Black Walnut. ✓ String Swing directs wider classical-guitar and bass necks to its original CC01 yoke rather than assuming CC01K fits every instrument.
RELEASE	Inventory every instrument's weight, neck width, headstock geometry, and finish; assign CC01K or CC01 per instrument; mock up both rows; and have the installer fasten into verified structural backing.

ZEPHYR-PRESRV-PRB15C01CG	Zephyr Presrv PRB15C01CG 15-inch Beverage Cooler candidate · checked 2026-09-26
SOURCE	https://docs.zephyronline.com/docs/specs/Presrv_PRB15C01CG_spec.pdf
DIMENSIONS	W 15 in · D 23.375 in · H min 33.875 in · H max 34.875 in · cutout W min 15.125 in · cutout H min 34 in · rear min 1 in · wall-side min 2.25 in
VERIFIED	✓ The unit is front-venting and may be built in when its front air vent remains unobstructed. ✓ Zephyr lists overall dimensions of 15 inches wide, 23-3/8 inches deep, and 33-7/8 to 34-7/8 inches high. ✓ The installation manual requires a cabinet opening at least 15-1/8 inches wide and 34 inches high.
RELEASE	Cabinet shop must issue a coordinated shop drawing that preserves the front vent, 15-1/8-inch minimum opening, 34-inch minimum height, 1-inch rear plug clearance, door swing, outlet location, and pull-out service access.

DIODE-LED-BLAZE-100-SYSTEM	Diode LED BLAZE 100 2700K Tape + S1 Black Channel + OMNIDRIVE Basics 96W Driver candidate · checked 2026-09-26
SOURCE	https://www.diodeled.com/blaze.html
DIMENSIONS	tape W 0.31 in · channel L 96 in · channel W 0.67 in · channel H 0.31 in
VERIFIED	✓ BLAZE 100 part DI-24V-BLBS1-27-016 is 24-volt, 2700K, 90+ CRI tape rated at 113 lumens and 1.46 watts per foot. ✓ The manufacturer specifies a 55-foot maximum run and 3.93-inch cut points for this tape. ✓ The recommended S1 black channel is DI-CHB-S1-96B, supplied in 96-inch lengths with a classic frosted lens.
RELEASE	Lighting designer and electrician must produce a zone, feed, channel-joint, driver-load, driver-access, and dimmer schedule. Keep every feed at or below 55 feet and every driver at or below 96 watts, confirm a neutral at each PD-5NE, and bench-test the exact tape-driver-dimmer load for low-end stability and flicker before release.

NORA-NM4-RDC27BB	Nora Lighting NM4-RDC27BB 4-inch Round Deep Cone Reflector candidate · checked 2026-09-26
SOURCE	https://noralighting.com/product/nm4-rdc/
DIMENSIONS	cutout Ø 3.5 in · trim Ø 4.5 in · H 4.875 in
VERIFIED	✓ Part NM4-RDC27BB is the 2700K matte-black configuration. ✓ Nora lists 90+ CRI, 1027 delivered lumens, 15 watts, a 37-degree narrow-flood beam, and Triac or ELV dimming to 10 percent. ✓ The listed ceiling cutout is 3.5 inches; the trim is 4.5 inches wide and the module is 4.875 inches high.
RELEASE	Approve a reflected-ceiling and photometric plan, verify the actual ceiling cavity and insulation condition, obtain the exact dimmer/load compatibility result, and mock up 2700K output against the black ceiling before ordering.

WOODUPP-AKUPANEL-1029	WoodUpp Akupanel Colored Black Wrapped on Black Felt, item 1029 candidate · checked 2026-09-26
SOURCE	https://woodupp.com/products/akupanel
DIMENSIONS	W 23.62 in · H 94.49 in · thk 0.866 in · slat width 1.063 in · slat depth 0.512 in · gap 0.512 in
VERIFIED	✓ Item 1029 is a black-wrapped slat on black felt panel measuring 94.49 by 23.62 inches and 0.866 inch thick. ✓ The construction uses 0.354-inch felt, 0.512-inch-deep by 1.063-inch-wide slats, and 0.512-inch gaps. ✓ WoodUpp claims acoustic absorption Class A only when installed with 45 mm battens and insulation between them.
RELEASE	Order a finish sample and have the architect, acoustician, and installer approve the exact wall build-up, cavity insulation, substrate, fastener pattern, fire-test documentation, and interfaces with instrument backing and fabric-track areas.

FABRITRAK-GEOTRAK-BLACK	FabriTRAK GeoTRAK Black Fabric-Retention Profiles candidate · checked 2026-09-26
SOURCE	https://www.fabritrak.com/products/geotrak
DIMENSIONS	profile depth options 0.5/1/1.375 in
VERIFIED	✓ GeoTRAK is a PVC-free black fabric-retention framework with fabric-receiving jaws. ✓ FabriTRAK lists 1/2-inch, 1-inch, and 1-3/8-inch profile depths. ✓ The system is site-installed by FabriTRAK dealers and professional installers and may be paired with acoustic core and finish fabric.
RELEASE	A qualified dealer must submit the exact track, core, fabric, substrate, perimeter, outlet, door, HVAC, slat-junction, and service-removal details and the test documentation for the complete proposed assembly.

KARNDLEAN-VAN-GOGH-EBONY-SCB89	Karndean Van Gogh Rigid Core Ebony SCB89 candidate · checked 2026-09-26
SOURCE	https://www.karndean.com/en-us/floors/products/ebony-scb89
DIMENSIONS	plank L 48 in · plank W 7 in · thk 0.177 in
VERIFIED	✓ Ebony SCB89 is a black and charcoal-gray rigid-core plank measuring 48 by 7 inches. ✓ Karndean lists a 20 mil wear layer, 4.5 mm total thickness, and 23.64 square feet per carton. ✓ Karndean's U.S. rigid-core installation guide says laminate and any floating floor must be removed before installation.
RELEASE	Identify whether the existing oak LVP is floating or adhered, inspect the underlying substrate, verify flatness and moisture conditions, order a room sample, and obtain the installer's written warranty for the exact floor assembly before release.

OMEGA-ANTIQUED-MIRROR-SAMPLES	Omega Antique Mirror Dark Cloud, Smoky Quartz, and Gold Vein Overlay Samples candidate · checked 2026-09-26
SOURCE	https://omegamirrorproducts.com/products/antique-mirrors/
VERIFIED	✓ Omega presents Dark Cloud Antique, Smoky Quartz Mirror, and Gold Vein Overlay Mirror as distinct decorative patterns. ✓ The products are handcrafted and pattern variation is expected. ✓ Omega offers physical samples for evaluation before fabrication.
RELEASE	Order physical samples and build a full-size visual mockup. A local mirror fabricator and structural engineer must design the final panel sizes, edge treatment, safety backing or lamination, substrate, mechanical retention, access, and every overhead attachment before any wall-arch or ceiling release.

GUILFORD-FR701-2100-408	Guilford of Maine FR701, style 2100, color 408 Black candidate · checked 2026-09-26
SOURCE	https://www.guilfordofmaine.com/swatches/2100-408
DIMENSIONS	usable W 66 in
VERIFIED	✓ Color 408 is the black option in style 2100 FR701. ✓ The fabric is 100 percent post-consumer recycled polyester with a 66-inch usable width and no backing or added finish. ✓ Duvaltex reports 95 percent acoustic transparency for the fabric before anechoic termination.
RELEASE	Order a current fabric card and production sample, approve the dye lot and visual texture under the room lighting, verify stretch and retention with the selected track, and test or document the exact track-core-fabric assembly required for the project.

LOCAL SOURCE FILES	Canonical schedule · guide.json Execution sequence · research/build-content.json Product evidence · research/products.json
--------------------	--
